

Weekly Report

Report # 8

Sept 2, 2020

# Norway House Cree Nation

Health Centre of Excellence



Project:

CD4 – Health Centre of Excellence

Aman Chana

JNR Construction

# Weekly Progress Report

Sep 3, 2020, ID #76

## REPORT DETAILS

**Description** Weekly Progress report # 8

**Created by** Aman Chana

**Status** Draft

**Last update** Sep 3, 2020 10:22 PM

**Last updated by** Aman Chana

### 1. WORK LOG

Crew	# Workers	# Total hours	Work performed
JNR	20	1000	SEE BELOW
Totals	20	1000	

### 2. CREW ONSITE

2.1 The following crews were active in this report period

- ☒ JNR
- ☐ Mechanical
- ☐ Electrical

### 3. ARCHITECTURAL

3.1 Ongoing Work  
N/A

3.2 Completed Work

N/A

## 4. STRUCTURAL

4.1 Ongoing Work

- Formwork preparation.
- Laying out rebar for footings.
- Removal of footing at higher elevation.
- Dewatering.
- Prefab cages for piers
- Cutting, chipping and drilling surface under pad footings.
- Bringing pad footing surface elevations under acceptable limits via track mounted drill
- Layout of footings and pier.
- Prep locations for concrete pour.
- Concrete pouring, finishing and covering for footings.
- Screed during pour.
- Stripping forms, building footing boxes, installing footing rebar
- drilling for dowels, and blowing off excess debris for markings.

4.2 Completed Work

N/A

## 5. MECHANICAL

5.1 Ongoing Work

N/A

5.2 Completed Work

N/A

## 6. ELECTRICAL

6.1 Ongoing Work

N/A

6.2 Completed Work

N/A

## 7. CIVIL

### 7.1 Ongoing Work

- Layout of footings corner.
- Directing Driller on site
- Marking Dowel Locations
- Removal/Hauling of blast rock from Div. B.

### 7.2 Completed Work

N/A

## 8. SAFETY AND COVID-19 SCREENING

### 8.1 Number of Covid Screening reports completed

- 115 Covid screening reports completed on site this week.

-As cases continue to spike province wide new travel protocols have been established for the community. All JNR staff and visitors to site are adhering to the new policy's in place and are exercising social distancing and safe hygiene practices to decrease the risk of possible transmission.

## 9. SITE VISIT SCHEDULE

### 9.1 Next scheduled site visit

Next Bi weekly meeting will be held on September 9th. Due to the latest Provincial covid protocols a virtual MS teams meeting has been scheduled.

## NOTES

### Schedule update

- Schedule Summary will be included in weekly reports going forward.
- Summary shows to date where construction currently sits according to the overall schedule.
- The line items tasks will be shaded according to percent complete to gauge overall standing of particular tasks

- 130 footings completed on site.
- Concrete pad forming and rebar install continues on site.
- Next concrete pour should have an additional 75 pad locations poured and approximately 50 pier locations.

## PHOTOS (36)



Drone shot of forming labour in area A1\_20200829\_115200

**Aman Chana**

Aug 29, 2020 4:52 PM



pad forming and dewatering\_20200829\_114900

**Aman Chana**

Aug 29, 2020 4:49 PM



poured pad locations\_20200824\_040600

**Aman Chana**

Aug 24, 2020 9:06 AM



surveying pad locations\_20200824\_040600

**Aman Chana**

Aug 24, 2020 9:06 AM





sonotube rebar prep\_20200824\_035400

**Aman Chana**

Aug 24, 2020 8:54 AM



stripping pad forms\_20200823\_093500

**Aman Chana**

Aug 23, 2020 2:35 PM



Dewatering\_20200823\_092300

**Aman Chana**

Aug 23, 2020 2:23 PM



Dewatering\_20200823\_091300

**Aman Chana**

Aug 23, 2020 2:13 PM



drilling for dowels\_20200823\_091200

**Aman Chana**

Aug 23, 2020 2:12 PM



sonotube rebar prep\_20200823\_090900

**Aman Chana**

Aug 23, 2020 2:09 PM



pad location concrete pour\_20200823\_034200

**Aman Chana**

Aug 23, 2020 8:42 AM



concrete line pump pour\_20200823\_034100

**Aman Chana**

Aug 23, 2020 8:41 AM





Concrete pad pour\_20200823\_034000

**Aman Chana**

Aug 23, 2020 8:40 AM



Concrete pad pour\_20200823\_033900

**Aman Chana**

Aug 23, 2020 8:39 AM



completed concrete pad location

**Arshdeep Grewal**

Aug 22, 2020 4:32 PM



completed concrete pad location\_20200822\_113200

**Aman Chana**

Aug 23, 2020 4:32 PM





Concrete pump line\_20200822\_095100

**Aman Chana**

Aug 22, 2020 2:51 PM



Concrete pad pour

**Arshdeep Grewal**

Aug 22, 2020 2:47 PM



Concrete pad pour\_20200822\_094700

**Aman Chana**

Aug 22, 2020 2:47 PM



pad location completed rebar

**Arshdeep Grewal**

Aug 22, 2020 2:43 PM



pad location completed rebar\_20200822\_094300  
**Aman Chana**  
Aug 22, 2020 2:43 PM



Pad location completed rebar  
**Arshdeep Grewal**  
Aug 22, 2020 2:40 PM



Pad location completed rebar\_20200822\_094000  
**Aman Chana**  
Aug 22, 2020 2:40 PM



pad location rebar install\_20200822\_080100  
**Aman Chana**  
Aug 22, 2020 1:01 PM



20200822\_095349\_photo

**Arshdeep Grewal**

Aug 22, 2020 9:53 AM



20200822\_095349\_photo\_20200822\_045300

**Aman Chana**

Aug 22, 2020 9:53 AM



20200822\_095319\_photo

**Arshdeep Grewal**

Aug 22, 2020 9:53 AM



20200822\_095236\_photo

**Arshdeep Grewal**

Aug 22, 2020 9:52 AM





20200822\_095209\_photo\_20200822\_045200\_20200822\_045200

**Aman Chana**

Aug 22, 2020 9:52 AM



20200821\_131623\_photo

**Arshdeep Grewal**

Aug 22, 2020 8:40 AM



20200821\_180409\_photo\_20200821\_130400

**Aman Chana**


Aug 21, 2020 6:04 PM



concrete pour\_20200821\_130400

**Aman Chana**


Aug 21, 2020 6:04 PM

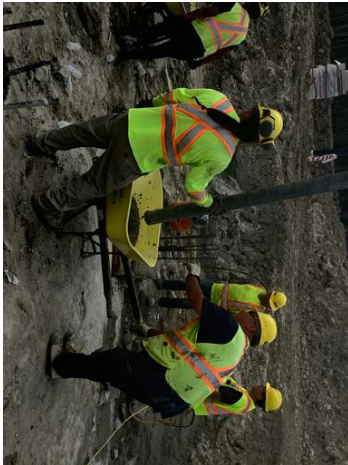

line pump in action\_20200821\_124300

**Aman Chana**


Aug 21, 2020 5:43 PM

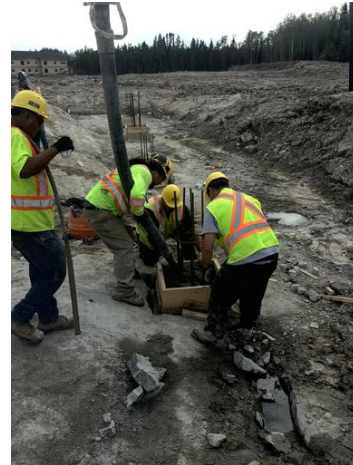

Pad location concrete pour\_20200821\_124100

**Aman Chana**

Aug 21, 2020 5:41 PM

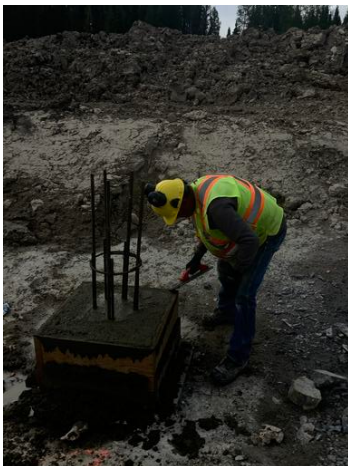

top of pad concrete finishing\_20200821\_123900

**Aman Chana**

Aug 21, 2020 5:39 PM



pad location concrete vibration\_20200821\_123800

**Aman Chana**

Aug 21, 2020 5:38 PM



## Norway House - Health Center of Excellence Schedule Timeline

