

Weekly Report

Report # 9

Sept 14, 2020

# Norway House Cree Nation

Health Centre of Excellence



Project:

CD4 – Health Centre of Excellence

Aman Chana

JNR Construction

# Weekly Progress Report

Sep 14, 2020,

## REPORT DETAILS

**Description** Weekly Progress report # 9

**Created by** Aman Chana

### 1. WORK LOG

Crew	# Workers	# Total hours	Work performed
JRN	22	1617	See below for details
Totals	22	1617	

### 2. CREW ONSITE

2.1 The following crews were active in this report period

- ☒ JNR
- ☐ Mechanical
- ☐ Electrical

### 3. ARCHITECTURAL

3.1 Ongoing Work  
N/A

3.2 Completed Work  
N/A

## 4. STRUCTURAL

4.1 Ongoing Work  
-Formwork preparation in area A3 .  
-Laying rebars for footing in A3.  
-Removal of footing formwork in Area A1  
-Dewatering on going after heavy rainfall on site  
-Prefab rebar cages for piers that are to be poured.  
-Preparing standing sonotubes for Piers in Div. A

4.2 Completed Work  
N/A

## 5. MECHANICAL

5.1 Ongoing Work  
N/A

5.2 Completed Work  
N/A

## 6. ELECTRICAL

6.1 Ongoing Work  
N/A

6.2 Completed Work  
N/A

## 7. CIVIL

## 7.1 Ongoing Work

- Surveyor on site completing layout of footings and pier, and numbering of footings in field.
- Checking Piers and noting elevations
- Surveying blast area
- Review design for bolt setup, and drafting bedrock blasting volumes.
- Working on East parking lot leveling and removing rock from last blast
- PC 350 Hoe excavating clay out of area B cl
- 650 Dozer leveled the clay in the parking lot in preparation for electrical lay down area .
- Excavation in building area B and C on going

## 7.2 Completed Work

N/A

## 8. SAFETY AND COVID-19 SCREENING

## 8.1 Number of Covid Screening reports completed

Government of Manitoba re implemented a travel ban to North of the 53rd parallel to any non essential travel. JRN is continuing screening all visitors and staff daily who report to site.

154 Covid screening reports completed on site last week.

M Block and associates Concrete inspection rep was on site the 9,10,11th of September. Screening report was normal and was deemed safe to be on site.

## 9. SITE VISIT SCHEDULE

## 9.1 Next scheduled site visit

Next schedule to be determined. As Covid cases rise travel from the management team to site will be determined as needed. Consultants to determine when the next visit to site is based on milestones that need to be inspected.

## NOTES

### Schedule update

- Schedule Summary is included in weekly report.
- Summary shows to data where construction currently sits according to the overall schedule.
- The line items tasks will be shaded according to percent complete to gauge overall standing of particular tasks

### Progress to date

- Area A1 is 100 percent completed for pad locations and 98 pier poured to date
- Concrete pad forming and rebar install continues on site in area A3.
- Area A2 has 19 pad locations completed

- Area A3 has 37 pad locations completed and 37 piers poured to date
- Area B1 has 1 pad location completed to date
- Next concrete pour is potentially scheduled for Friday Sept 18th have an additional 60 pad locations poured and approximately 40 pier locations.

## PHOTOS (21)



pouring piers

**Wayne Dee**

Sep 14, 2020 7:43 AM



pump truck pouring piers

**Wayne Dee**

Sep 14, 2020 7:43 AM



pump boom on site

**Wayne Dee**

Sep 14, 2020 7:43 AM



area to be dewatered after rains

**Wayne Dee**

Sep 14, 2020 7:43 AM





Pump truck pouring piers

**Wayne Dee**

Sep 14, 2020 7:43 AM



materials being unloaded

**Wayne Dee**

Sep 14, 2020 7:43 AM



IMG\_0294

**Wayne Dee**

Sep 14, 2020 7:43 AM



piers and pads area A1

**Wayne Dee**

Sep 14, 2020 7:43 AM



IMG\_0276

**Wayne Dee**

Sep 14, 2020 7:43 AM



IMG\_0291

**Wayne Dee**

Sep 14, 2020 7:43 AM



piers being pumped full of concrete

**Wayne Dee**

Sep 14, 2020 7:43 AM



pumping truck

**Wayne Dee**

Sep 14, 2020 7:43 AM





IMG\_0273

**Wayne Dee**

Sep 14, 2020 7:43 AM



IMG\_0296

**Wayne Dee**

Sep 14, 2020 7:43 AM



drone shot of pad locations

**Wayne Dee**

Sep 14, 2020 7:43 AM



IMG\_0283

**Wayne Dee**

Sep 14, 2020 7:43 AM





Rock dill chipping

**Wayne Dee**

Sep 14, 2020 7:43 AM



pier and pad locations

**Wayne Dee**

Sep 14, 2020 7:43 AM



IMG\_0286

**Wayne Dee**

Sep 14, 2020 7:43 AM



IMG\_0284

**Wayne Dee**

Sep 14, 2020 7:43 AM




Dewatering

**Wayne**

**Dee**

Sep 9, 2020 6:41 AM

# Footings Poured to date Details

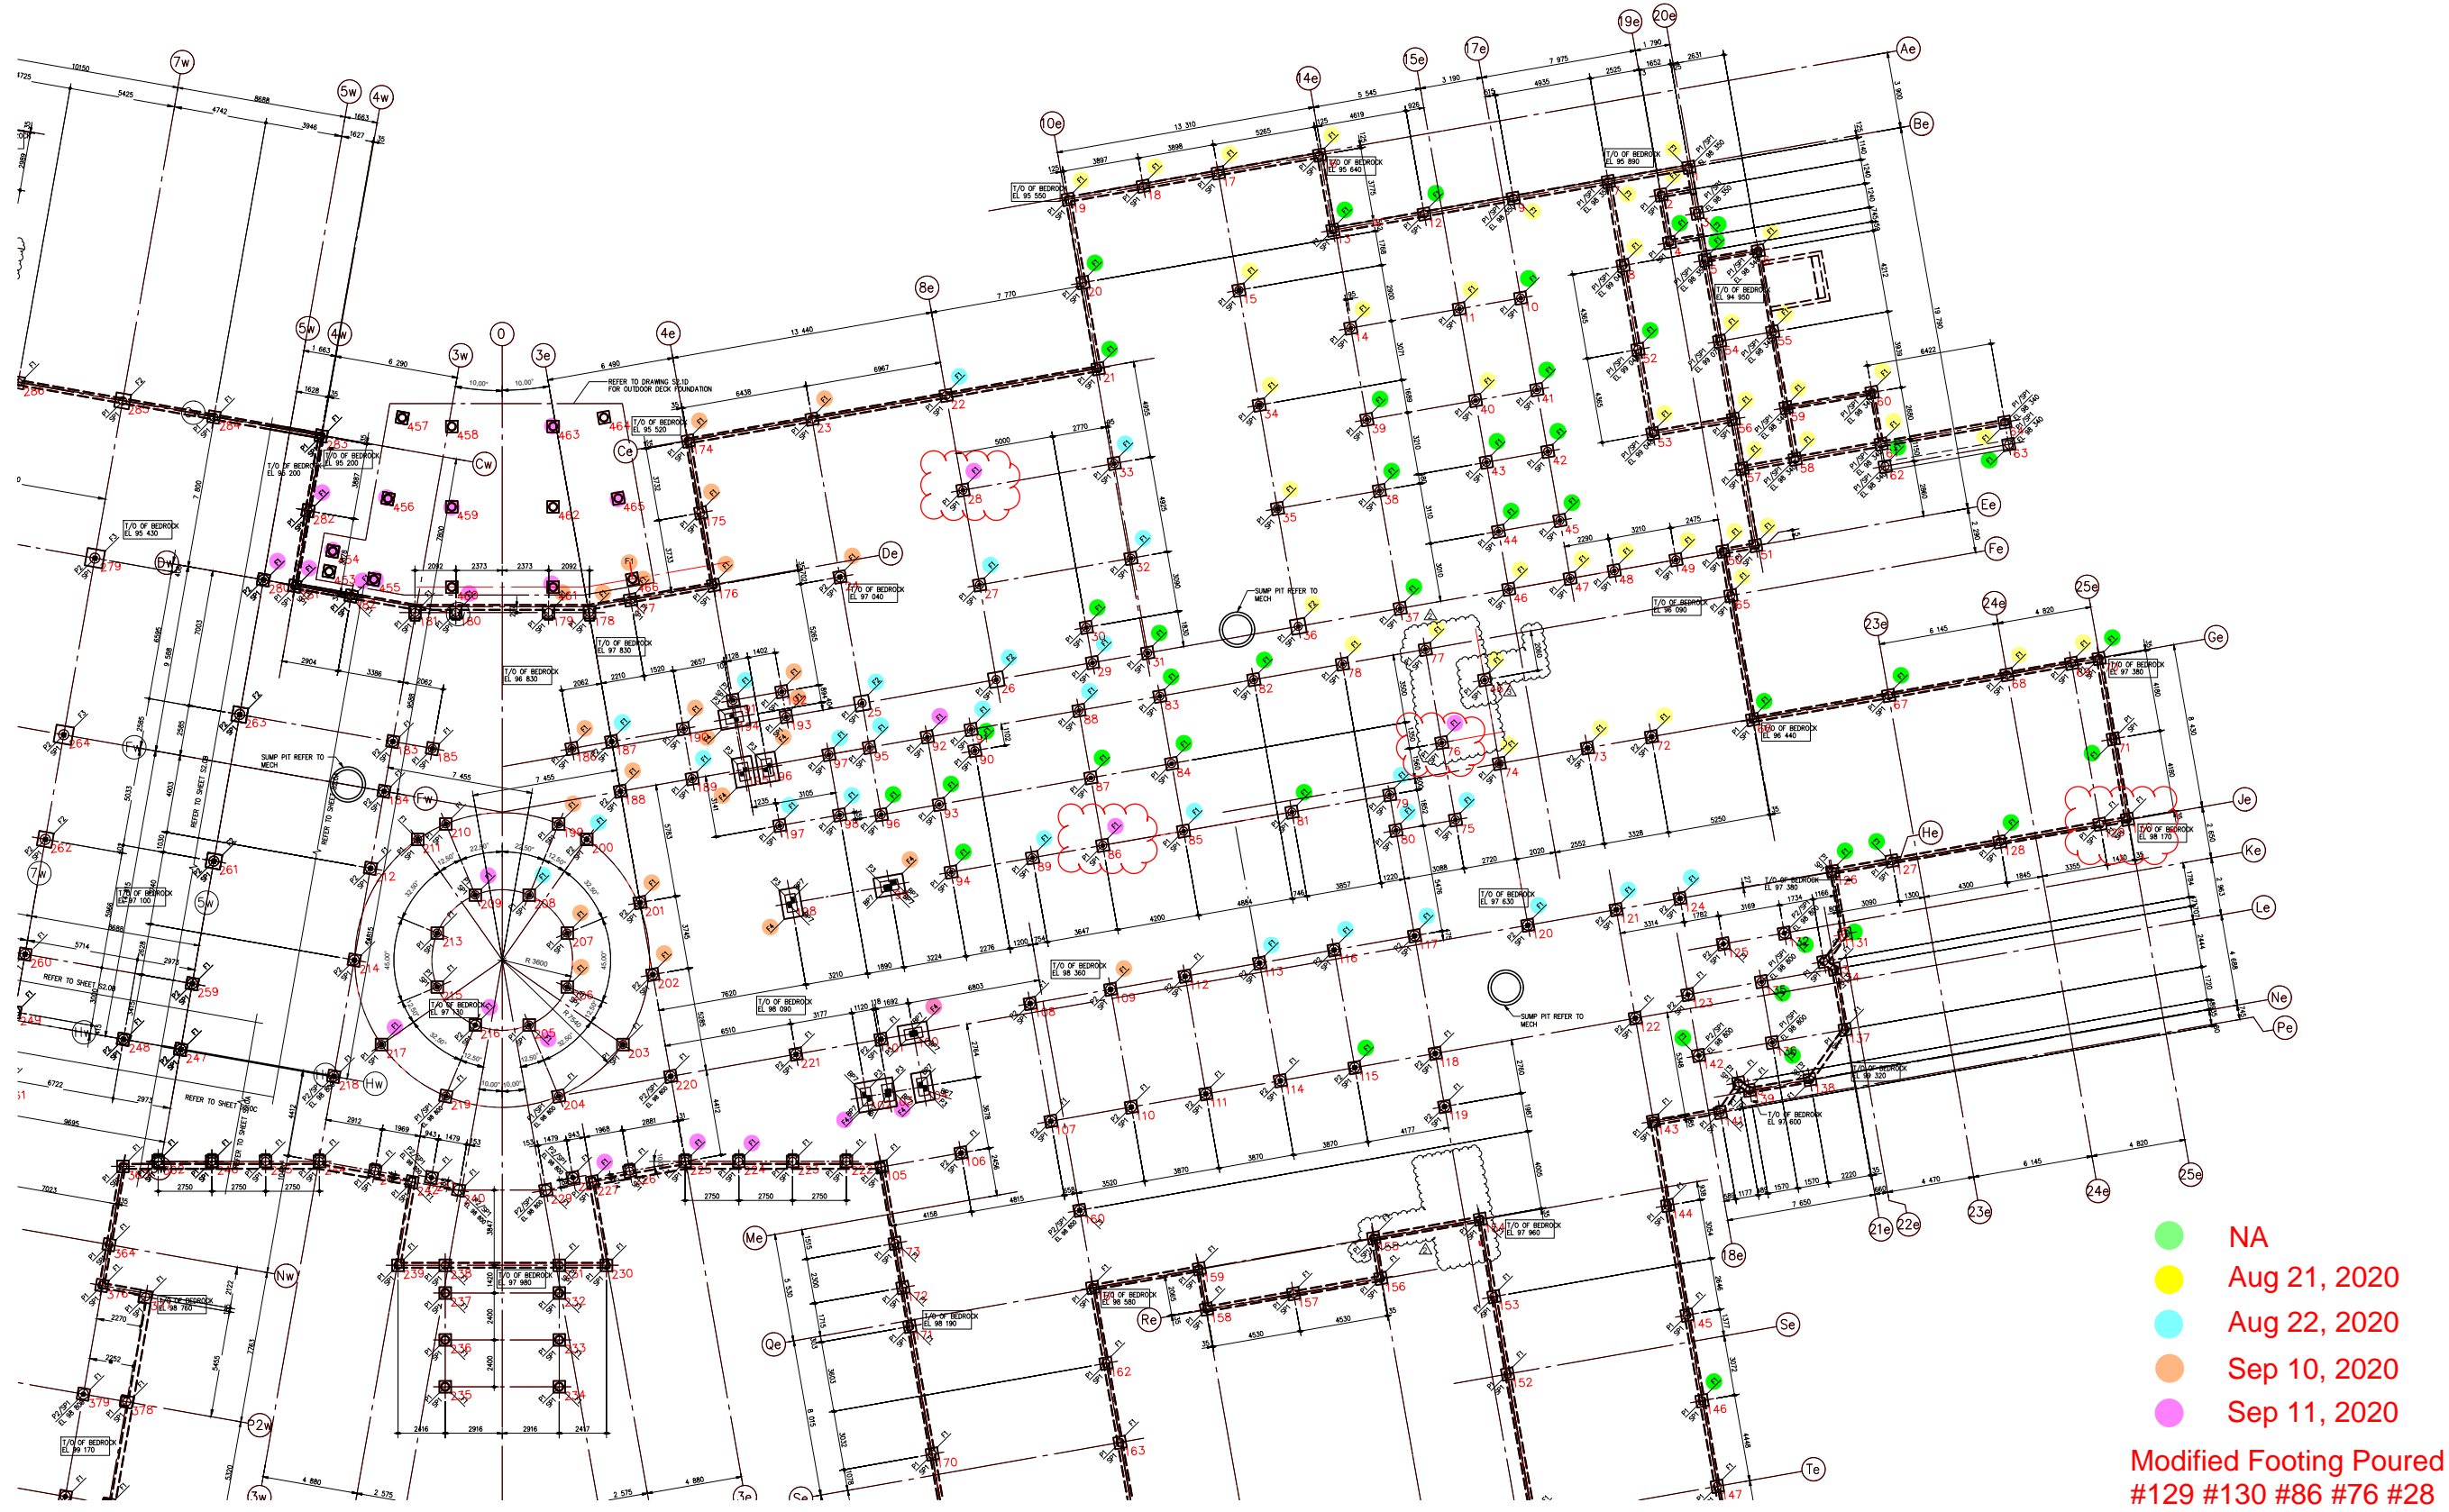



[illegible]

Modified Footing Poured  
#129 #130 #86 #76 #28



## Norway House - Health Center of Excellence Schedule Timeline

