

Weekly Report  
Report # 26

July 18, 2020

# Norway House Cree Nation

Health Centre of Excellence



Project:

- CD3 – Professional Accommodations

Larry Cove

JNR Construction

<b>Project Name:</b> Professional Accommodations		<b>Project Number:</b> CD3 – 19015B	
<b>Safety Statistics</b>			
Description	Previously Reported	This Period	Project to Date
Man Hours	34925.75	1087.5	36013.25
Sub trades	1966	40	2006
FLHAs	4499	149	4648
First Aides	14	0	14
Incidents	10	0	10
Daily Covid-19 Screenings	1053	99	1152
<b>Quality/Engineering</b>			
Items	Submitted	Resolved	Outstanding
RFIs	57	56	1
Shop Drawings	70	67	3
NCRs	1	0	1

**Outstanding Concerns:**

- RFIs
  - RFI 051 – Appliance Clearance – July 15/20
- Shop Drawings
  - SD 057 – VRV System – July 7/20
  - SD 028 Rev01 – Electrical Structure - July 13/20
  - SD 060 – Controls – July 16/20
- NCR’s
  - NCR 01 – Elevator Shaft Wall Concrete Segregation – May 20/20

Completed This Period	Comments or Concerns
Roof Sheathing Install	
Fascia Board Install and Build Out	
Roof Truss Bracing	
Exterior Sheathing Install	
Backing in Stairwells for Handrails	
Hold Downs Install	
Wood Stud Wall Backing	
Mechanical Rough Ins	
To Complete Next Period	To complete the following Period
Dampproofing Exterior Grade Beam Concrete Wall	Install Cement Board Panels on Grade Beam and Backfill
Install Exterior Sheathing	Gable Wing Wall Construction
Build Out Fascia Board	Build Catwalk in Attic Space
Rough in Mechanical Openings	Fiberglass Window Installation
Soffit Framing	Continue Soffit Framing
Install Insulation Baffles	

Progress Photos



Exterior View – South West Wing



Exterior View – North West Wing



Exterior View – South East Wing



Exterior View – North East Wing

**Progress Photos**



Roof Sheathing Install – Gable End-  
East Wing



Roof Sheathing Install – North East Wing



Fascia Board Install – North East Wing



Fascia Board Build Out – North East Wing


Progress Photos



Roof Truss Bracing – East Wing



Roof Truss Bracing – East Wing

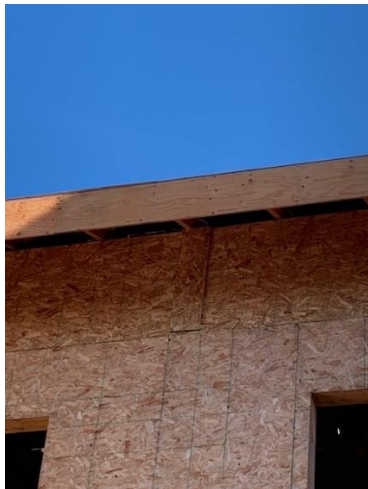

Exterior Sheathing to Underside of  
Roof Trusses -North West Wing



Backing Install in Stairwell No. 2  
for Handrail

Progress Photos



Hold Down Install on Main Floor -  
West Wing



Hold Down Install to Second Floor-  
West Wing



Wood Backing Install – East Wing



Wood Backing Install – West Wing

Progress Photos



Duct Work Risers Install on Main Floor-  
East Wing



Duct Work Riser Install to Second Floor-  
East Wing
