

Weekly Report
Report # 2

January 2020

Norway House Cree Nation

Health Centre of Excellence



Project:

- CD3 – Professional Accommodations

Larry Cove

JNR Construction

Project Name: Professional Accommodations		Project Number: CD3 – 19015B	
Safety Statistics			
Description	Previously Reported	This Period	Project to Date
Man Hours	11416.5	871	12287.5
FLHAs	1151	126	1277
First Aides	5	0	5
Incidents	4	0	4
Quality/Engineering			
Items	Submitted	Resolved	Outstanding
RFIs	10	9	1
Shop Drawings	6	5	1
NCRs	0	0	0

Outstanding Concerns:


- RFIs
 - o RFI ## - Hold Down Connection- Jan 17/20
- Shop Drawings
 - o SD 006 – Underslab Vapour Barrier – Jan 13/20

Completed This Period	Comments or Concerns
Completed form work and rebar on grade beam	
Completed formwork and rebar	
Concrete pour of elevator slab and grade beam	Heat, hoard and monitor cure temperatures for seven days
To Complete Next Period	To complete the following Period
Complete center beam formwork and rebar	Pour concrete for center beam
	Install wood beams, floor joist and floor sheathing installation
Install sump pits	Install weeping tile
	Backfill around grade beam

Progress Photos



Overhead of Site of concrete pour

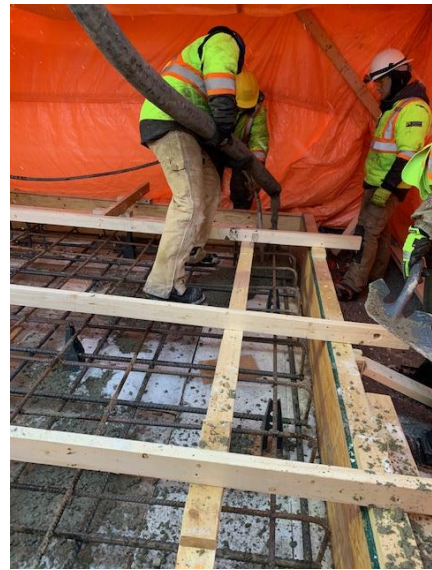

Concrete pour of elevator slab



Concrete pour of grade beam



Vibrating concrete for grade beam

Progress Photos



Trowel work for grade beam



Finish work on elevator slab
