

Weekly Report

Report # 15

May 2, 2020

# Norway House Cree Nation

Health Centre of Excellence



Project:

- CD3 – Professional Accommodations

Larry Cove

JNR Construction


<b>Project Name:</b> Professional Accommodations		<b>Project Number:</b> CD3 – 19015B	
<b>Safety Statistics</b>			
<b>Description</b>	<b>Previously Reported</b>	<b>This Period</b>	<b>Project to Date</b>
Man Hours	24906.25	710.5	25616.75
Sub trades	36	0	36
FLHAs	3022	141	3163
First Aides	9	0	9
Incidents	8	0	8
Daily Covid-19 Screening Logs	0	89	89
<b>Quality/Engineering</b>			
<b>Items</b>	<b>Submitted</b>	<b>Resolved</b>	<b>Outstanding</b>
RFIs	27	27	0
Shop Drawings	38	37	1
NCRs	0	0	0

**Outstanding Concerns:**

- RFIs
  - RFI
- Shop Drawings
  - SD 033 – Sikadur 25 Super-Low Viscosity Injection Resin – March 5/20

Completed This Period	Comments or Concerns
Install second floor wood trusses	
Install vapour barrier	
Install second floor sheathing	
Construct formwork for elevator shaft walls	
Install second floor wood beams	
Construct first floor interior walls	
Install second floor wood beams	
Install scaffolding and guardrails	
To Complete Next Period	To complete the following Period
Install second floor wood trusses	
Install vapour barrier	Install vapour barrier
Install second floor sheathing	
Install second floor interior walls	Install second floor interior walls
Pour concrete for elevator shaft wall	Strip formwork from elevator shaft wall
	Construct formwork for elevator shaft roof
	Install mechanical risers


Progress Photos

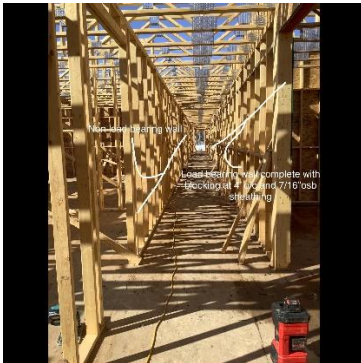

Interior Wall Framing



Second Floor Wood Truss Install

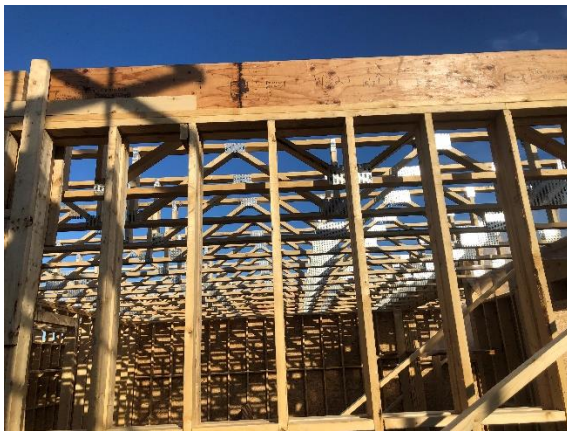

Second Floor Wood Beam Install



Stairwells Rim Board Install

Progress Photos



Second floor LVL Install



Subfloor Adhesive Applied



Second Floor Sheathing Install



Elevator Shaft Formwork
