

Weekly Report

Report # 18

May 23, 2020

# Norway House Cree Nation

Health Centre of Excellence



Project:

- CD3 – Professional Accommodations

Larry Cove

JNR Construction

Project Name: Professional Accommodations		Project Number: CD3 – 19015B	
Safety Statistics			
Description	Previously Reported	This Period	Project to Date
Man Hours	27793.75	843	28636.75
Sub trades	124	238	362
FLHAs	3435	116	3551
First Aides	11	0	11
Incidents	9	0	9
Daily Covid-19 Screenings	309	91	400
Quality/Engineering			
Items	Submitted	Resolved	Outstanding
RFIs	32	29	3
Shop Drawings	45	39	6
NCRs	1	0	1

**Outstanding Concerns:**

- RFIs
  - RFI 028 – Motorized Intake/Exhaust Damper for ERV Sizes - May 5/20
  - RFI 031 – Plumbing Interference – May 19/20
  - RFI 032 – Plumbing Interference Mechanical Room – May 21/19
- Shop Drawings
  - SD 033 – Sikadur 25 Super-Low Viscosity Injection Resin – March 5/20
  - SD 018 Rev 2 – VRV System – May 12/20
  - SD 019 Rev 1 – Second Floor Wood Trusses – May 19/20
  - SD 020 Rev 1 – Roof Trusses – May 19/20
  - SD 015 Rev 1 – Main Floor Wood Trusses – May 19/20
  - SD 040 – Stair #2 – Plan Drawing Stamped – May 21/20
- NCR's
  - NCR 01 – Elevator Shaft Wall Concrete Segregation

Completed This Period	Comments or Concerns
Second floor sheathing – west wing	
Second floor exterior wall construction and erection – west wing	
Vapour barrier and rim board sealed	
Exterior sheathing between main and second floor	
Layout and install sanitary and domestic water lines – east wing	
Layout and install duct work in crawlspace – west wing	
To Complete Next Period	To complete the following Period
Install ledger on exterior of elevator shaft	
Install wood beams on second floor	
Install second floor wood trusses	
Exterior wall construction and erection	
Interior walls construction and erection – east wing	Interior wall construction and erection – west wing
Second floor sheathing	
Mechanical plumbing layout and installation	Continue with plumbing layout and installation
Mechanical duct work layout and installation	Continue with duct work layout and installation
	Damp proofing of grade beam
	Roof Framing

## Progress Photos



Overhead View



Exterior View – North East Side



Exterior View – South West Side



Second Floor Exterior Wall Framing  
– North East Side



## Progress Photos



Second Floor Exterior Wall Sheathing  
-North East Side



Second Floor Exterior Walls  
-South East Side



Second Floor Exterior Window  
– South East Side



Second Floor Exterior Wall  
– North East End

## Progress Photos



Second Floor Sheathing Install  
- North East Side



Sub Floor Adhesive Applied  
-North East Side




Vapour Barrier Rim Board Detail  
-South West Side



Insulation and Vapour Barrier  
On Rim Board -Second Floor Stair 2 East Side

## Progress Photos

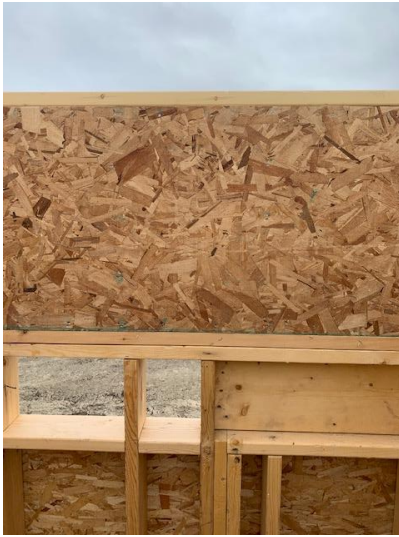

Interior Sheathing Install on Rim Board  
- Stair 2 East Side



Exterior Sheathing Install  
Between Main and Second Floor



Roof Trusses on Site



Double Top Plate Installation  
On Exterior Wall – South East End




## Progress Photos



Sanitation and Domestic Water Lines  
To Second Floor



Sanitation and Domestic Water Lines  
In CrawlSpace

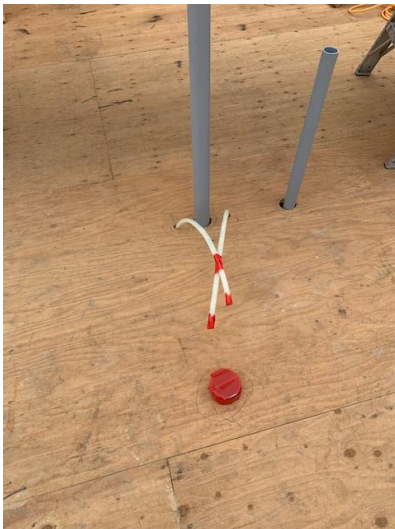

Sanitation and Domestic Water Lines  
Penetrated Second Floor



Sanitation and Domestic Water Lines  
With Bracing



## Progress Photos



Duct Work Installation in Crawlspace



Duct Work Installation in Crawlspace



Duct Work Sleeves Installed in Fire Stop Wall in Crawlspace



Duct Work and Sleeve Installed in Fire Stop Wall in Crawlspace
