

Weekly Report

Report # 19

May 30, 2020

Norway House Cree Nation

Health Centre of Excellence



Project:

- CD3 – Professional Accommodations

Larry Cove

JNR Construction

Project Name: Professional Accommodations		Project Number: CD3 – 19015B	
Safety Statistics			
Description	Previously Reported	This Period	Project to Date
Man Hours	28636.75	908.5	29545.25
Sub trades	362	271	633
FLHAs	3551	155	3706
First Aides	12	0	12
Incidents	9	0	9
Daily Covid-19 Screenings	400	102	502
Quality/Engineering			
Items	Submitted	Resolved	Outstanding
RFIs	33	30	3
Shop Drawings	45	42	3
NCRs	1	0	1

Outstanding Concerns:

- RFIs
 - RFI 031 – Plumbing Interference – May 19/20
 - RFI 032 – Plumbing Interference Mechanical Room – May 21/20
 - RFI 033 – Support for Duct Work – May 29/20
- Shop Drawings
 - SD 018 Rev 2 – VRV System – May 12/20
 - SD 040 – Stair #2 – Plan Drawing Stamped – May 21/20
 - SD 031 Rev1 – ERV-1 – May 27/20
- NCR's
 - NCR 01 – Elevator Shaft Wall Concrete Segregation

Completed This Period	Comments or Concerns
Second floor sheathing – west wing	
Second floor exterior wall construction and erection – west wing	
Second floor interior wall construction and erection – east wing	
Layout and install sanitary and domestic water lines in crawlspace – east and west wings	
Layout and install duct work in crawlspace – west wing	
Install ledger board on exterior of elevator shaft wall	
Install second floor wood beams	
Install second floor wood trusses	
Remove formwork for elevator shaft wall	
To Complete Next Period	To complete the following Period
Construct and erect interior walls on west and east wings	Install sheathing on roof
Roof Framing	
Install roof trusses	Install roof trusses
Mechanical duct work layout and installation	
Electrical rough in and stringing of wiring on main floor	Electrical rough in and stringing of wiring on main floor

Progress Photos



Interior View – South East Side



Second Floor Corridor Walls -West End



Corridor and Demising Wall Installation
West Wing



Second Floor Exterior Wall Framing
– North East Side

Progress Photos



Second Floor Exterior Wall Sheathing
North East Side



Second Floor Interior Corridor Wall
-West Wing



Second Floor Exterior Windows
– Fitness Centre Room




Second Floor Exterior Window
– Fitness Centre Room

Progress Photos



Second Floor Sheathing Install
- North Side

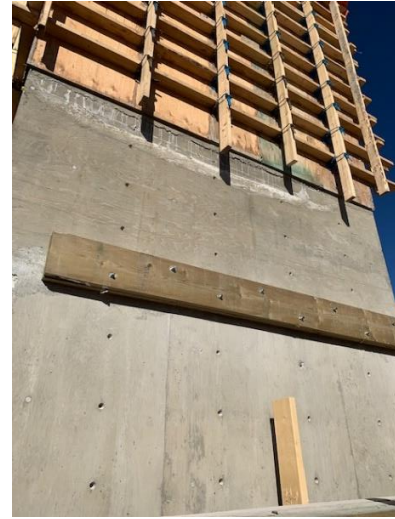

Ledger Board Install on Elevator Shaft Wall



Second Floor Beam and Truss Install
at Elevator – West Side



Second Floor Beam and Truss Install
at Elevator - East Side

Progress Photos



Vapour Barrier Install at Exterior Wall
And Interior Corridor Wall – West End



Acoustic Sealant Applied under
Interior Demising Wall – West Side



Grout Tie Holes – Interior Elevator Shaft Wall




Exterior Weeping Tile Installation

Progress Photos




Seal Domestic Water Lines at Main Floor

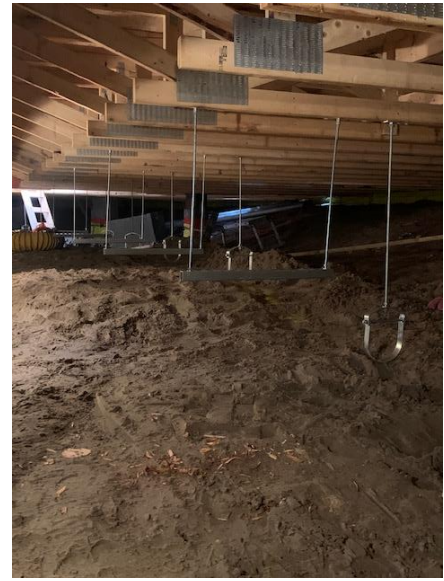

Plumbing Line Hangers Install
In Crawlspace -East side



Main Sanitary Line Install with Hanger
In Crawlspace – East Side

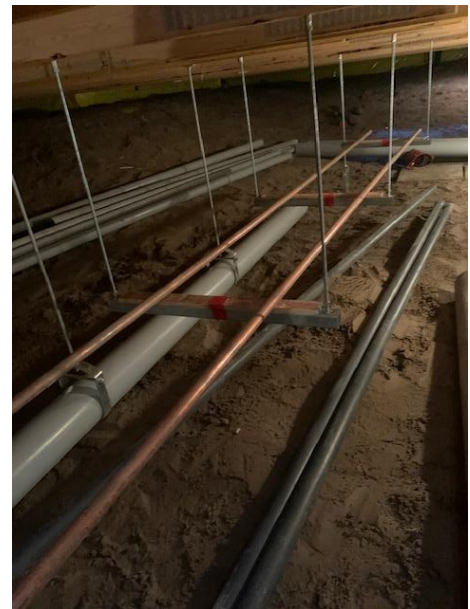

Sanitary and Domestic Water Lines
with Hangers in Crawlspace – West Side

Progress Photos



Duct Work Installation in Crawlspace
West Side



Duct Work Branch Line Installation
in Crawlspace – West Side



Duct Work Risers in Crawlspace
West Side



Duct Work Risers Leading to Main Floor
West End
