

Weekly Report

Report # 25

July 11, 2020

# Norway House Cree Nation

Health Centre of Excellence



Project:

- CD3 – Professional Accommodations

Larry Cove

JNR Construction

Project Name: Professional Accommodations		Project Number: CD3 – 19015B	
Safety Statistics			
Description	Previously Reported	This Period	Project to Date
Man Hours	34118.25	807.5	34925.75
Sub trades	1685	281	1966
FLHAs	4373	126	4499
First Aides	14	0	14
Incidents	10	0	10
Daily Covid-19 Screenings	1043	104	1053
Quality/Engineering			
Items	Submitted	Resolved	Outstanding
RFIs	54	51	3
Shop Drawings	66	62	4
NCRs	1	0	1

**Outstanding Concerns:**

- RFIs
  - RFI 046 - Fire Stopping and Curb Requirement – July 1/20
  - RFI 048 – Emergency Lighting Battery Bank Mounting Heights – July 1/20
  - RFI 049 – Location of Thermostat for Second Floor Fan Coil Unit – July 2/20
- Shop Drawings
  - SD 050 – Gypsum Concrete Underlayment – June 23/20
  - SD 055 – Lap Siding – June 30/20
  - SD 057 – VRV System – July 7/20
  - SD 058 – Water Closets WC-1 and WC-2 – July 7/20
- NCR's
  - NCR 01 – Elevator Shaft Wall Concrete Segregation – May 20/20

Completed This Period	Comments or Concerns
Roof Sheathing Install	When wet or raining unable to work on roof
Gable End Roof Truss Install	
Fascia Board Install	
Roof Framing and Bracing	
Exterior Sheathing Install	
Interior Sheathing Install	
Suite Entrance Framing	
Mechanical Rough Ins	
To Complete Next Period	To complete the following Period
Install roof sheathing	
Install roof bracing	
Blocking wood walls	Continue blocking wood walls
	Dampproof and install cement board panels on exterior of grade beam and backfill
	Roofing (shingles)

## Progress Photos



Exterior View – South West Side



Exterior View – North West Side



Exterior View – South East Side



Exterior View – North East Side

## Progress Photos



Roof Sheathing Install – North East Wing



Roof Sheathing Install – South East Wing



Gable End Roof Truss Install – East Wing



Fascia Board Install – North West Wing




## Progress Photos



Roof Framing – East Wing



Roof Bracing Install – West Wing

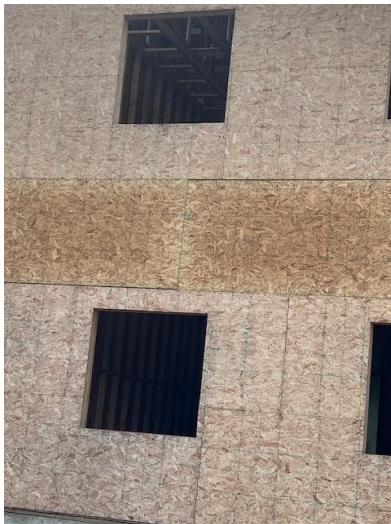

Exterior Sheathing Install Between  
Main and Second Floor -North West Wing



Sheathing Install on Second Floor  
Corridor Walls

## Progress Photos



Suite Entrance Framing on Second Floor-  
West Wing



Plumbing Lines Install on Second  
Floor – East Wing



Plumbing Vent Pipe Penetration  
Through Roof Sheathing – East Wing



Plumbing Lines Install in Attic Space –  
East Wing



## Progress Photos



Duct Work Risers Install on Main Floor-  
West Wing



Duct Work Riser Install on Second Floor-  
East Wing



Fire Damper Install in Fire Stop Wall  
in Crawlspace – East Wing



Duct Work Branch Line Install in  
Crawlspace – East Wing
