

Weekly Report

Report # 29

August 22, 2020

# Norway House Cree Nation

Health Centre of Excellence



Project:

- CD3 – Professional Accommodations

Larry Cove

JNR Construction

Project Name: Professional Accommodations		Project Number: CD3 – 19015B	
Safety Statistics			
Description	Previously Reported	This Period	Project to Date
Man Hours	38151.5	537	38688.5
Sub trades	2724	485	3209
FLHAs	5035	112	5147
First Aides	14	0	14
Incidents	10	0	10
Daily Covid-19 Screenings	1427	93	1520
Quality/Engineering			
Items	Submitted	Resolved	Outstanding
RFIs	63	60	3
Shop Drawings	81	77	4

**Outstanding Concerns:**

- RFIs
  - RFI 051 – Appliance Clearance – July 15/20
  - RFI 058 - Fire Hose Cabinet – August 18/20
  - RFI 059 – Rusting Plates Remediation – August 21/20
- Shop Drawings
  - SD 061 Rev02– Aluminum Entrances and Glazing – August 21/20
  - SD 062 Rev01 – Electrical Lighting – August 13/20
  - SD 064 – Bug and Rain Screen Vent – August 13/20
  - SD 056 – Fire Sprinklers – August 14/20

Completed This Period	Comments or Concerns
Construction of Catwalk in Attic	
Add Framing Members to Lintels	
Attach Blue Skin to Grade Beam	
Install CFI Panels to Grade Beam	
Trim Fascia Boards	
Roof Shingles Install	
Fire Stop Electrical Penetrations from Second to Main Floor	
Electrical Rough In	
Install Batt Insulation and Vapour Barrier for Mock-up	
To Complete Next Period	To complete the following Period
Roofing Shingles	
Install CFI Panels on Grade Beam	
Install Batt Insulation and Vapour Barrier on Exterior Walls	Install Batt Insulation and Vapour Barrier on Exterior Walls
Install Gypsum Board on Ceilings	Install Gypsum Board on Ceilings
Crawlspace Remediation	
Soffit Framing	Soffit Framing
Construct Gable Wing Walls	Construct Gable Wing Walls
Electrical Rough-Ins	Electrical Rough-Ins

## Progress Photos



Exterior View – South West Wing



Exterior View – North West Wing



Exterior View – South East Wing



Exterior View – North East Wing

### Progress Photos



Overhead View – South Side



Overhead View – North Side



Catwalk Construction in Attic Space



Framing Members added to Lintels above Windows



## Progress Photos



Blueskin Applied to Grade Beam –  
South West Wing



CFI Panels Install on Grade Beam – North East Wing



CFI Panels Install on Grade Beam – North  
West Wing



Trim Fascia Board –West End


## Progress Photos



Roof Shingle Install - North West Wing



Roof Shingles Install – South East Wing

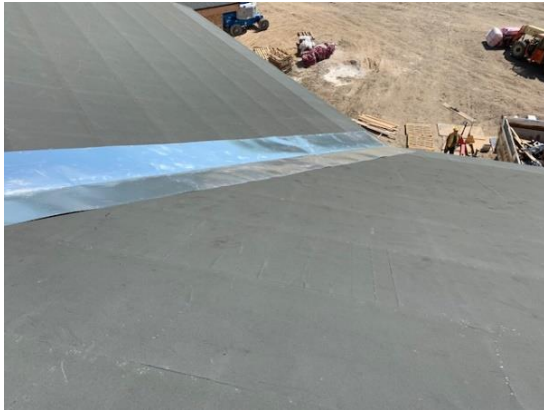

Roof Valley metal Install – South East Wing



Fire Stopping Applied to Electrical Penetration on Second Floor – West Wing



## Progress Photos



Fire Stopping Applied to Electrical Penetration on Second Floor – West Wing



Electrical Wiring Pull on Second Floor – West Wing



Electrical Wiring Pull on Main Floor – West Wing



Electrical Box Install on Exterior Wall – West Wing



## Progress Photos



Batt Insulation Install in Suite 2Y:16 for Mock-up



Batt Insulation Install in Stairwell No. 3 For Mock-up



Vapour Barrier Install in Stairwell No. 3 For Mock-up



Vapour Barrier Install in Suite 2Y:16 for Mock-up
