

Weekly Report

Report # 30

August 29, 2020

# Norway House Cree Nation

Health Centre of Excellence



Project:

- CD3 – Professional Accommodations

Larry Cove

JNR Construction

Project Name: Professional Accommodations		Project Number: CD3 – 19015B	
Safety Statistics			
Description	Previously Reported	This Period	Project to Date
Man Hours	38688.5	484.5	39173
Sub trades	3209	631	3840
FLHAs	5147	113	5260
First Aides	14	0	14
Incidents	10	0	10
Daily Covid-19 Screenings	1520	108	1628
Quality/Engineering			
Items	Submitted	Resolved	Outstanding
RFIs	63	62	1
Shop Drawings	84	79	5
Green Globes	3	0	3

**Outstanding Concerns:**

- RFIs
  - RFI 051 – Appliance Clearance – July 15/20
- Shop Drawings
  - SD 066 – Fire Sprinklers – August 14/20
  - SD 061 Rev02– Aluminum Entrances and Glazing – August 21/20
  - SD 067 – Mould Remediation Products – August 22/20
  - SD 068 – Lighting Type WT – August 25/20
  - SD 062 Rev02 – Electrical Lighting – August 25/20

Completed This Period	Comments or Concerns
Construct Attic Compartment Walls	
Place Below Grade Insulation	
Place Clean Stone over Weeping Tile	
Install CFI Panels to Grade Beam	
Install Drainage Boards on CFI Panels	
Roof Shingles Install	
Install Steel Stair's No. 2 & No. 3	
Install Vapour Barrier on Second Floor Ceilings	
Fire Stop Hold Downs on Second Floor	
Fire Stop Electrical Penetrations from Second to Main Floor	
Electrical Rough ins on Main Floor	
Mould Remediation in Crawlspace	
To Complete Next Period	To complete the following Period
Roofing Shingles	
Install Steel Stair's No. 3 & No. 1	
Install Vapour Barrier on Main Floor Ceilings	Install Batt Insulation and Vapour Barrier on Second Floor Exterior Walls
Install Gypsum Board on Second Floor Ceilings	Install Gypsum Board on Second Floor Ceilings
Crawlspace Remediation	
Soffit Framing	Soffit Framing
Construct Gable Wing Walls	Construct Gable Wing Walls
Electrical Rough-Ins	Electrical Rough-Ins
	Mechanical Rough-Ins

## Progress Photos



Exterior View – South West Wing



Exterior View – North West Wing



Exterior View – South East Wing



Exterior View – North East Wing


## Progress Photos



Attic Fire Compartment Wall Installation



Below Grade Insulation Installation

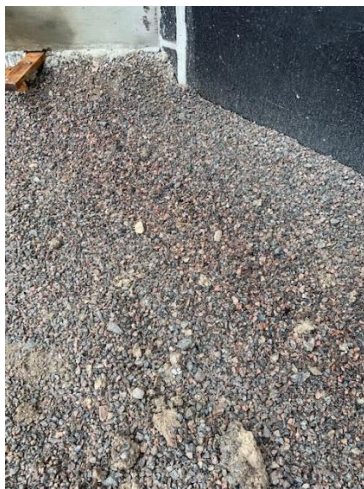


Clean Stone Placed Over Weeping Tile



CFI Panels Installation on Grade Beam-South West Wing



## Progress Photos

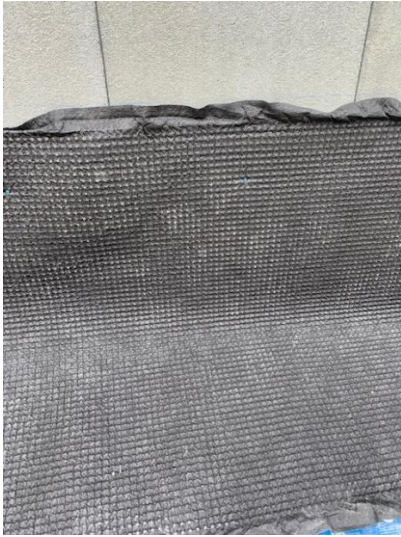

Drainage Board Install on CFI Panels –  
South East Wing



Roofing Shingles Install – West Wing



Roof Vent Install – West Wing



Steel Stair No. 2 Installation

## Progress Photos



Temporary Steps Install on Stair No. 2



Handrail Install on Stair No. 2



Steel Stair No. 3 Installation



Vapour Barrier Installation on Second Floor Suite Ceiling – West Wing



## Progress Photos



Vapour Barrier Installation on Second Floor Corridor Ceiling – West Wing



Fire Stopping Applied to Hold Downs on Second Floor – West Wing



Fire Stopping Applied to Electrical Penetrations in Attic Compartment Wall – West Wing



Electrical Wiring Pull on Main Floor – East Wing



### Progress Photos



Electrical Wiring and Box Install on  
Main Floor – East Wing



Electrical Conduit Install at Panel on  
Main Floor – East Wing
