

Weekly Progress Report

Jul 10, 2020

REPORT DETAILS

Description Weekly Progress Report # 1 Submitted by Aman Chana

Status Submitted

Last update Jul 10, 2020 3:59 PM

Last updated by Aman Chana

1. WORK LOG

| Crew | # Workers | # Total hours | Work performed |
|--------|-----------|---------------|-----------------------|
| JNR | 13 | 936 | See below for details |
| Totals | 13 | 936 | |

2. CREW ONSITE

2.1 The following crews were active in this report period



JNR



Mechanical



Electrical

3. ARCHITECTURAL

3.1 Ongoing Work

N/A

3.2 Completed Work

N/A

4. STRUCTURAL

- 4.1 Ongoing Work
- 1. Drilling for Concrete foundation dowels
 - 2. Structural Layout of footing locations
- 4.2 Completed Work
- N/A

5. MECHANICAL

- 5.1 Ongoing Work
- N/A
- 5.2 Completed Work
- N/A

6. ELECTRICAL

- 6.1 Ongoing Work
- N/A
- 6.2 Completed Work
- N/A

7. CIVIL

- 7.1 Ongoing Work

Blasting and Excavation Site Preparation

1. Drilling and placing blasting charges
2. Excavation of blasted materials
3. Excavation for sump pit locations and weeping tile
4. Dewatering excavated areas
5. Site access road preparation

7.2 Completed Work

N/A

NOTES

Site Supervisor Wayne Dee mobilized to site April 28th 2020

Site Supervisor David Somerville mobilized to site June 12th 2020

Work being completed on site to date:

1. Ongoing preparation and setup of site trailers.
2. Framing and dry walling interior partitions of site trailers.
3. Framing of exterior wood decks and pathways in between trailers
4. Setup of temporary site electrical generators
5. Setup of site sanitation facilities
6. Blasting days lost due to inclement weather i.e. rain and lightning; 14 days

Blasting materials can not be out in the threat of thunderstorms due to explosive materials safety protocols

PHOTOS (23)



Preparation for dewatering due to heavy rainfall

Wayne Dee

Jul 10, 2020 2:16 PM



Drilling for pad locations

Wayne Dee

Jul 10, 2020 2:16 PM



Preparation for dewatering due to heavy rainfall

Wayne Dee

Jul 10, 2020 2:15 PM



Deck framing in progress

Hooman Kazempour

Jul 10, 2020 1:02 PM



Excavation post blasting

Hooman Kazempour

Jul 10, 2020 1:02 PM



Deck framing in progress

Hooman Kazempour

Jul 10, 2020 1:02 PM



Drone shot of site office setup

David Somerville

Jul 7, 2020 5:29 PM



Site access road preparations

David Somerville

Jul 7, 2020 5:29 PM



Site access road preparations

David Somerville

Jul 7, 2020 5:29 PM



Drone shot of site trailer setup

David Somerville

Jul 7, 2020 5:29 PM



Site access road preparations

David Somerville


Jul 7, 2020 5:29 PM



Excavation post blasting

David Somerville

Jul 7, 2020 5:29 PM

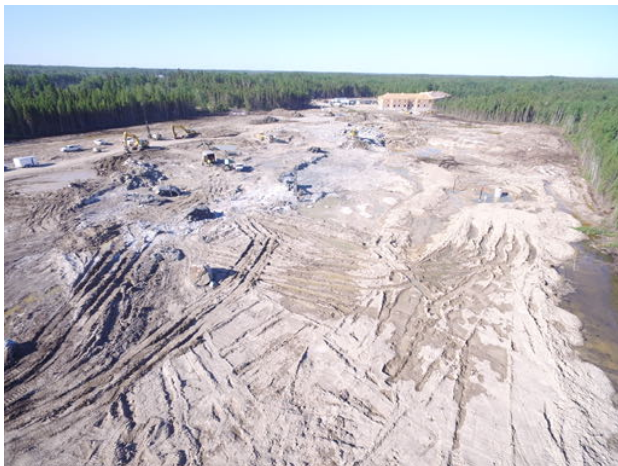

Drone shot of site

David Somerville

Jul 7, 2020 5:29 PM



Drone shot of excavated areas

David Somerville

Jul 7, 2020 5:29 PM



Drone shot of site office setup

David Somerville

Jul 7, 2020 5:29 PM



Dewatering operations

David Somerville

Jul 7, 2020 5:29 PM



Drilling for blast charges

David Somerville

Jul 7, 2020 5:29 PM



Drilling for blast charges

David Somerville

Jul 7, 2020 5:29 PM



Site trailer deck framing
David Somerville
Jul 7, 2020 5:29 PM



Temp mechanical/electrical at trailers
David Somerville
Jul 7, 2020 5:29 PM



Excavation post blasting
David Somerville
Jul 7, 2020 5:29 PM



Site trailer interior finishing
David Somerville
Jul 7, 2020 5:29 PM



Site trailer deck framing

David Somerville

Jul 7, 2020 5:29 PM
