

Weekly Report

Report # 7

Aug 26, 2020

# Norway House Cree Nation

Health Centre of Excellence



Project:

CD4 – Health Centre of Excellence

Aman Chana

JNR Construction

# Weekly Progress Report

Aug 24, 2020

## REPORT DETAILS

**Description** Weekly Progress report # 7

**Created by** Aman Chana

**Status** Draft

**Last update** Aug 26, 2020 2:28 PM

**Last updated by** Aman Chana

### 1. WORK LOG

Crew	# Workers	# Total hours	Work performed
JNR	13	854	See Below
Totals	13	854	

### 2. CREW ONSITE

2.1 The following crews were active in this report period

- ☒ JNR
- ☐ Mechanical
- ☐ Electrical

### 3. ARCHITECTURAL

3.1 Ongoing Work  
N/A

3.2 Completed Work

N/A

## 4. STRUCTURAL

4.1 Ongoing Work

- Formwork preparation.
- Laying out rebar for footings.
- Removal of footing at higher elevation.
- Dewatering.
- Prefab cages for piers
- Cutting, chipping and drilling surface under pad footings.
- Making pad footing surface under acceptable limits via track mounted drill
- Layout of footings and pier.
- Prep. for pour.
- Concrete pouring, finishing and covering for footings.
- Screed during pour.
- Stripping forms, building footing boxes, installing footing rebar drilling for dowels, and blowing off excess debris for markings.

4.2 Completed Work

N/A

## 5. MECHANICAL

5.1 Ongoing Work

N/A

5.2 Completed Work

N/A

## 6. ELECTRICAL

6.1 Ongoing Work

N/A

6.2 Completed Work

N/A

## 7. CIVIL

### 7.1 Ongoing Work

- Removal/Hauling of Blast Rock from Div. B. for future use.
- Mark out corners of footings, level and square footing forms, mark out areas for excavation of excess material in building footprint and access ramps.
- Digging a ditch to divert water from Div. A and to reduce pooling.

### 7.2 Completed Work

N/A

## 8. SAFETY AND COVID-19 SCREENING

### 8.1 Number of Covid Screening reports completed

- 93 Covid screening reports completed on site this week.
- As cases continue to spike province wide new travel protocols have been established for the community. All JNR staff and visitors to site are adhering to the new policy's in place and are exercising social distancing and safe hygiene practices to decrease the risk of possible transmission.
- M.Block and Eng Tech testing agencies were on site this week. All individual were screened,temperature checked ad deemed safe to be on site.

## 9. SITE VISIT SCHEDULE

### 9.1 Next scheduled site visit

Next site visit is scheduled for Wednesday Aug 26 2020  
Next Bi weekly site meeting will be Sept 9th 2020

## NOTES

Footings inspection are being carried out on regular basis.  
Inspection of footings carried out by Roel Raquin (M. Block and Associates) Aug 22nd 2020  
10 cubic m. concrete was poured in 41 footings.

Concrete testing was carried out by Eric Baert (Eng. Tech)  
Tested concrete for Air Content Test, Slump Cone Test and made concrete cylinders.

Manitoba Hydro visits on site for review of temporary/permanent power supply. Aug 21st 2020

Schedule update:

71 footings poured over the weekend.  
Concrete phasing plan update has been provided.

## PHOTOS (29)



20200824\_090600\_photo\_20200824\_040600

**Aman Chana**

Aug 24, 2020 9:06 AM



20200824\_090049\_photo\_20200824\_040000

**Aman Chana**

Aug 24, 2020 9:00 AM



IMG\_0436\_20200823\_091200

**Aman Chana**

Aug 23, 2020 2:12 PM



IMG\_0435\_20200823\_090900

**Aman Chana**

Aug 23, 2020 2:09 PM





IMG\_0434\_20200823\_034200

**Aman Chana**

Aug 23, 2020 8:42 AM



IMG\_0433\_20200823\_034100

**Aman Chana**

Aug 23, 2020 8:41 AM



IMG\_0432\_20200823\_034000

**Aman Chana**

Aug 23, 2020 8:40 AM



IMG\_0428\_20200822\_095100

**Aman Chana**

Aug 22, 2020 2:51 PM



20200822\_095209\_photo\_20200822\_045200

**Aman Chana**

Aug 22, 2020 9:52 AM



20200821\_180409\_photo\_20200821\_130400

**Aman Chana**

Aug 21, 2020 6:04 PM





20200821\_174300\_photo\_20200821\_124300

**Aman Chana**


Aug 21, 2020 5:43 PM



20200821\_174151\_photo\_20200821\_124100

**Aman Chana**


Aug 21, 2020 5:41 PM

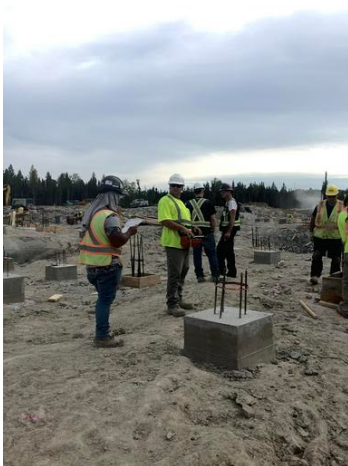

20200821\_173915\_photo\_20200821\_123900

**Aman Chana**

Aug 21, 2020 5:39 PM

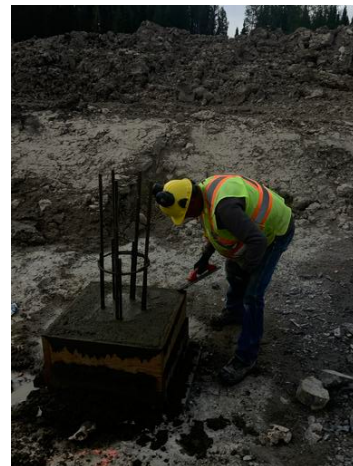

20200821\_173904\_photo\_20200821\_123900

**Aman Chana**

Aug 21, 2020 5:39 PM





20200821\_173855\_photo\_20200821\_123800

**Aman Chana**

Aug 21, 2020 5:38 PM



20200821\_173758\_photo\_20200821\_123700

**Aman Chana**

Aug 21, 2020 5:37 PM



20200821\_173708\_photo\_20200821\_123700

**Aman Chana**

Aug 21, 2020 5:37 PM



concrete testing\_20200821\_123200

**Aman Chana**

Aug 21, 2020 5:32 PM



Concrete pump line\_20200821\_123100

**Aman Chana**

Aug 21, 2020 5:31 PM



20200821\_092426\_photo\_20200821\_042400

**Aman Chana**

Aug 21, 2020 9:24 AM



20200821\_090340\_photo\_20200821\_040300

**Aman Chana**

Aug 21, 2020 9:03 AM



20200821\_084053\_photo\_20200821\_034000

**Aman Chana**

Aug 21, 2020 8:40 AM



20200821\_083956\_photo\_20200821\_033900

**Aman Chana**

Aug 21, 2020 8:39 AM



20200821\_033200\_photo\_20200821\_033200

**Aman Chana**

Aug 21, 2020 8:32 AM



Dewatering\_20200821\_033200

**Aman Chana**

Aug 21, 2020 8:32 AM



survey\_20200821\_033200

**Aman Chana**

Aug 21, 2020 8:32 AM





20200820\_130549\_photo\_20200820\_080500

**Aman Chana**

Aug 20, 2020 1:05 PM



20200820\_130500\_photo\_20200820\_080500

**Aman Chana**

Aug 20, 2020 1:05 PM



20200819\_141931\_photo\_20200819\_091900

**Aman Chana**

Aug 19, 2020 2:19 PM
