

Weekly Report

Report # 34

September 26, 2020

Norway House Cree Nation

Health Centre of Excellence



Project:

- CD3 – Professional Accommodations

Larry Cove

JNR Construction

Project Name: Professional Accommodations		Project Number: CD3 – 19015B	
Safety Statistics			
Description	Previously Reported	This Period	Project to Date
Man Hours	39340	521	39861
Sub trades	5507	691	6198
FLHAs	5606	115	5721
First Aides	14	0	14
Incidents	10	0	10
Daily Covid-19 Screenings	1989	128	2117
Quality/Engineering			
Items	Submitted	Resolved	Outstanding
RFIs	73	72	1
Shop Drawings	90	87	3
Green Globes	5	4	1

Outstanding Concerns:

- RFIs
 - RFI068 – Mechanical Chase Relocation – September 24/20
- Shop Drawings
 - SD 067 – Mould Remediation Products – September 10/20
 - SD 072 – Fire Extinguisher – September 23/20
 - SD 073 – Gypsum Concrete Underlayment – Repair – September 28/20
- Green Globes
 - GG005 – Intumescent Paint– September 09/20

Completed This Period	Comments or Concerns
Wing Wall Construction	
Soffit Framing	
Exterior Insulation Installation	
Batt Insulation Install on Second and Main Floors Interior Walls	
Gypsum Board Install on Second Floor and Stairwell's	
Steed Stud Installation on Second Floor	
Spray Foam Insulation Applied to Cavities Between Second Floor Trusses	
Blown-in Insulation in Attic	
Mechanical Rough-Ins	
Sprinkler Rough-Ins	
To Complete Next Period	To complete the following Period
Steel Stud Framing on Second Floor	Install backing in Steel Studs on Second Floor
Soffit Framing	Soffit Framing
Exterior Insulation Install	Exterior Insulation Install
Sprinkler Rough-Ins	Sprinkler Rough-Ins
Electrical Rough-Ins	Electrical Rough-Ins
Mechanical Rough-Ins	

Progress Photos



Exterior View – South West Wing



Exterior View – North West Wing



Exterior View – South East Wing



Exterior View – North East Wing

Progress Photos



Wing Wall Construction – West Wing



Soffit Framing – South West Wing



Exterior Rigid Insulation Install
– North East Wing



Batt Insulation Install on Second Floor
Corridor Wall - South East Wing

Progress Photos



Gypsum Board Install in Second Floor Suites – West Wing



Steel Stud Install in Second Floor Suites – East Wing



Spray Foam Insulation Applied to Cavities Between Second Floor Trusses - West Wing



Blown-in Insulation in Attic – East Wing

Progress Photos



Duct Work Installation on Second Floor Suite Ceilings – East Wing




Duct Work Installation on Second Floor Suite Ceilings - West Wing



Plumbing Sanitary Line Install to Second Floor – West Wing




Plumbing Sanitary Line Install in Crawlspace – East Wing



Progress Photos



Sprinkler Line Install in Corridor on
Second Floor – West Wing

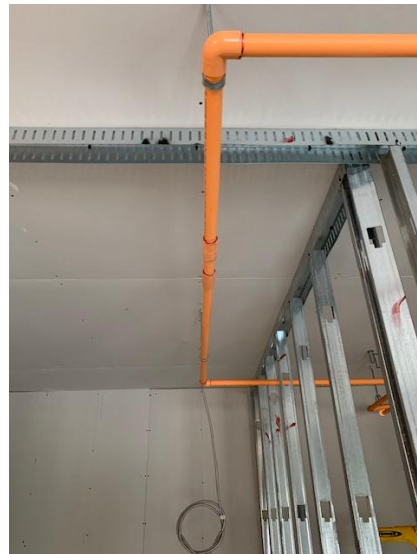

Sprinkler Line Install in Suites on Second
Floor – East Wing
