

Weekly Report

FEB 22nd - 28th

2021 Report # 30

Norway House Cree Nation

Health Centre of Excellence



Project:

CD4 – Health Centre of Excellence

Aman Chana

JNR Construction

Weekly Progress Report

Mar 2, 2021, ID #253

REPORT DETAILS

Description

Created by Aman Chana

Status Draft

Last update Mar 3, 2021 12:01 AM

Last updated by Aman Chana

1. WORK LOG

Crew	# Workers	# Total hours	Work performed
JNR	40	2360	See below for discriptions
Totals	40	2360	

2. CREW ONSITE

2.1 The following crews were active in this report period

- ☒ JNR
- ☐ Mechanical
- ☒ Electrical
- ☐ Masonry
- ☒ Structural Steel

3. ARCHITECTURAL

3.1 Ongoing Work

N/A

3.2 Completed Work

N/A

4. STRUCTURAL

4.1 Ongoing Work

Structural Steel

B1 Roof Level

-Opening framing / girts bracing / wind bracing / bridging / -torqueing / decking / deck angle/ curtain wall support

-electrical cable tray supports.

A3 Main Floor

-Erection of beams, columns, owsj

-Removing snow from Q deck roof level

4.2 Completed Work

Concrete

-Layout of Grade Beam (C2)

-Building formwork for grade beam (C2)

-General site clean up and snow removal.

-Poured concrete in remaining Grade Beam (A2 / GL 9e-22e)

-Cleaning leftover material after stripping grade beam from
GL Ke to GL 9e

-HSS grouting under Q-Deck (A1)

-Continued stripping formwork from Grade Beam (A2)

5. MECHANICAL

5.1 Ongoing Work

Producing required shop drawing submittals -Ongoing

5.2 Completed Work

Wescan Mechanical off Site for Turn around schedule

6. ELECTRICAL

6.1 Ongoing Work

Producing required shop drawing submittals -Ongoing

6.2 Completed Work

- General site work.
- Installing conduit work packages in A1 crawlspace
- Working on temp service sea cans
- Piping in A3 crawl space
- Putting sleeves in A1

7. CIVIL

7.1 Ongoing Work

General site Cleanup

- Digging for sump installation (C2)
- Installing weeping tiles (C2)
- Surveyor
- Bolt spacing drawings
- Drafting and data management
- Reading specifications.

7.2 Completed Work

8. SAFETY AND COVID-19 SCREENING

8.1 Number of Covid Screening reports completed

**JNR is continuing screening all visitors and staff daily who report to site.
240 Covid screening reports completed on site last week.**

9. SITE VISIT SCHEDULE

9.1 Next scheduled site visit

Next scheduled visit to site TBD

PHOTOS (56)



Formwork GB C2
Anmol Kang
Feb 27, 2021 4:57 PM



Formwork GB C2
Anmol Kang
Feb 27, 2021 4:57 PM



Erecting steel structure B1
Anmol Kang
Feb 27, 2021 4:57 PM



Formwork GB C2
Anmol Kang
Feb 27, 2021 4:57 PM



Erecting steel structure B1
Anmol Kang
Feb 27, 2021 4:56 PM



Erecting steel structure B1
Anmol Kang
Feb 27, 2021 4:56 PM



Formwork GB C2
Anmol Kang
Feb 27, 2021 4:56 PM



Stripping GB A2
Anmol Kang
Feb 27, 2021 4:55 PM



IMG_0317

Anmol Kang

Feb 27, 2021 4:55 PM



Heating under Q deck A1

Anmol Kang

Feb 27, 2021 4:54 PM



Formwork GB C2

Anmol Kang

Feb 27, 2021 4:53 PM



Crane working on B1 steel structure

Anmol Kang

Feb 27, 2021 4:53 PM



Heating and hoarding over masonry A1

Anmol Kang

Feb 27, 2021 4:53 PM



Heat in trailer

Anmol Kang

Feb 27, 2021 4:53 PM



Erecting steel structure B1

Anmol Kang

Feb 27, 2021 4:52 PM



B1- Steel erection

Anmol Kang

Feb 26, 2021 3:39 PM



IMG_0295

Anmol Kang

Feb 26, 2021 3:39 PM



A2- Stripped grade beam

Anmol Kang

Feb 26, 2021 3:39 PM



IMG_0304

Anmol Kang

Feb 26, 2021 3:39 PM



A2- Stripped grade beam

Anmol Kang

Feb 26, 2021 3:39 PM



Steel lay down area
Anmol Kang
Feb 26, 2021 3:39 PM



Setting up total station
Anmol Kang
Feb 26, 2021 3:37 PM



B1- Placing Q-Deck
Anmol Kang
Feb 26, 2021 3:37 PM



IMG_0309
Anmol Kang
Feb 26, 2021 3:37 PM



IMG_0305

Anmol Kang

Feb 26, 2021 3:37 PM



A2- Stripped grade beam

Anmol Kang

Feb 26, 2021 3:36 PM



A1- Heaters waring up crawlspace

Anmol Kang

Feb 26, 2021 3:36 PM



A2- Compacting concrete in Grade Beam

Arshdeep Grewal

Feb 26, 2021 11:43 AM



A2- Pouring concrete in Grade Beam
Arshdeep Grewal
Feb 26, 2021 11:43 AM




Concrete pump and truck
Arshdeep Grewal
Feb 26, 2021 11:43 AM



A2- Heating and Hoarding Grade Beam
Arshdeep Grewal
Feb 26, 2021 11:43 AM



A2- Concrete pour in grade beam
Arshdeep Grewal
Feb 26, 2021 11:43 AM

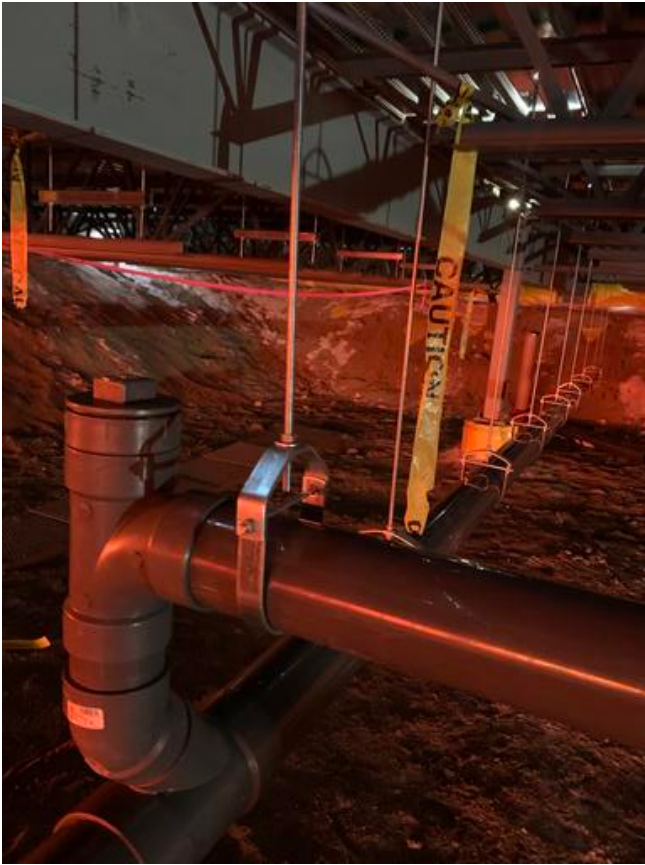

A1- SAN lines

Arshdeep Grewal

Feb 26, 2021 11:43 AM



A1- Electrical Conduits

Arshdeep Grewal

Feb 26, 2021 11:43 AM



A1/A2- Spreading sand over poly
Arshdeep Grewal
Feb 26, 2021 11:43 AM



A1/A2- Spreading sand over poly
Arshdeep Grewal
Feb 26, 2021 11:43 AM



B1- Torqueing
Arshdeep Grewal
Feb 26, 2021 11:43 AM



A2- Checking Grade Beam
Arshdeep Grewal
Feb 26, 2021 11:43 AM



A1- Sleeves over Q-Deck
Anmol Kang
Feb 25, 2021 4:01 PM



A2- Removed hoarding from grade beam
Anmol Kang
Feb 25, 2021 3:58 PM



A1- Heaters warming up crawlspace
Anmol Kang
Feb 25, 2021 3:57 PM



A2- Stripping formwork from grade beam
Anmol Kang
Feb 25, 2021 3:54 PM



B1- Structural steel
Wayne Dee
Feb 24, 2021 5:27 PM



B1- Structural steel
Wayne Dee
Feb 24, 2021 5:27 PM



A1/A2 - Main floor structural steel

Wayne Dee

Feb 24, 2021 5:23 PM



A1- Grouting under HSS

Wayne Dee

Feb 24, 2021 5:23 PM



A1- Grouting under HSS

Wayne Dee

Feb 24, 2021 5:23 PM



A1- Water lines

Wayne Dee

Feb 24, 2021 5:23 PM



A1- Water / SAN lines

Wayne Dee

Feb 24, 2021 5:23 PM



A1- Water lines in crawlspace

Wayne Dee

Feb 24, 2021 5:23 PM



C2- Aerial view of grade beam formwork

Wayne Dee

Feb 24, 2021 5:19 PM



Aerial View of Site

Wayne Dee

Feb 24, 2021 5:19 PM



Aerial View of site

Wayne Dee

Feb 24, 2021 5:19 PM



B1- Aerial View of Q-Deck

Wayne Dee

Feb 24, 2021 5:19 PM



B1/A3 - Aerial View of structural steel

Wayne Dee


Feb 24, 2021 5:19 PM




A3 - Aerial View of structural steel

Wayne Dee


Feb 24, 2021 5:19 PM

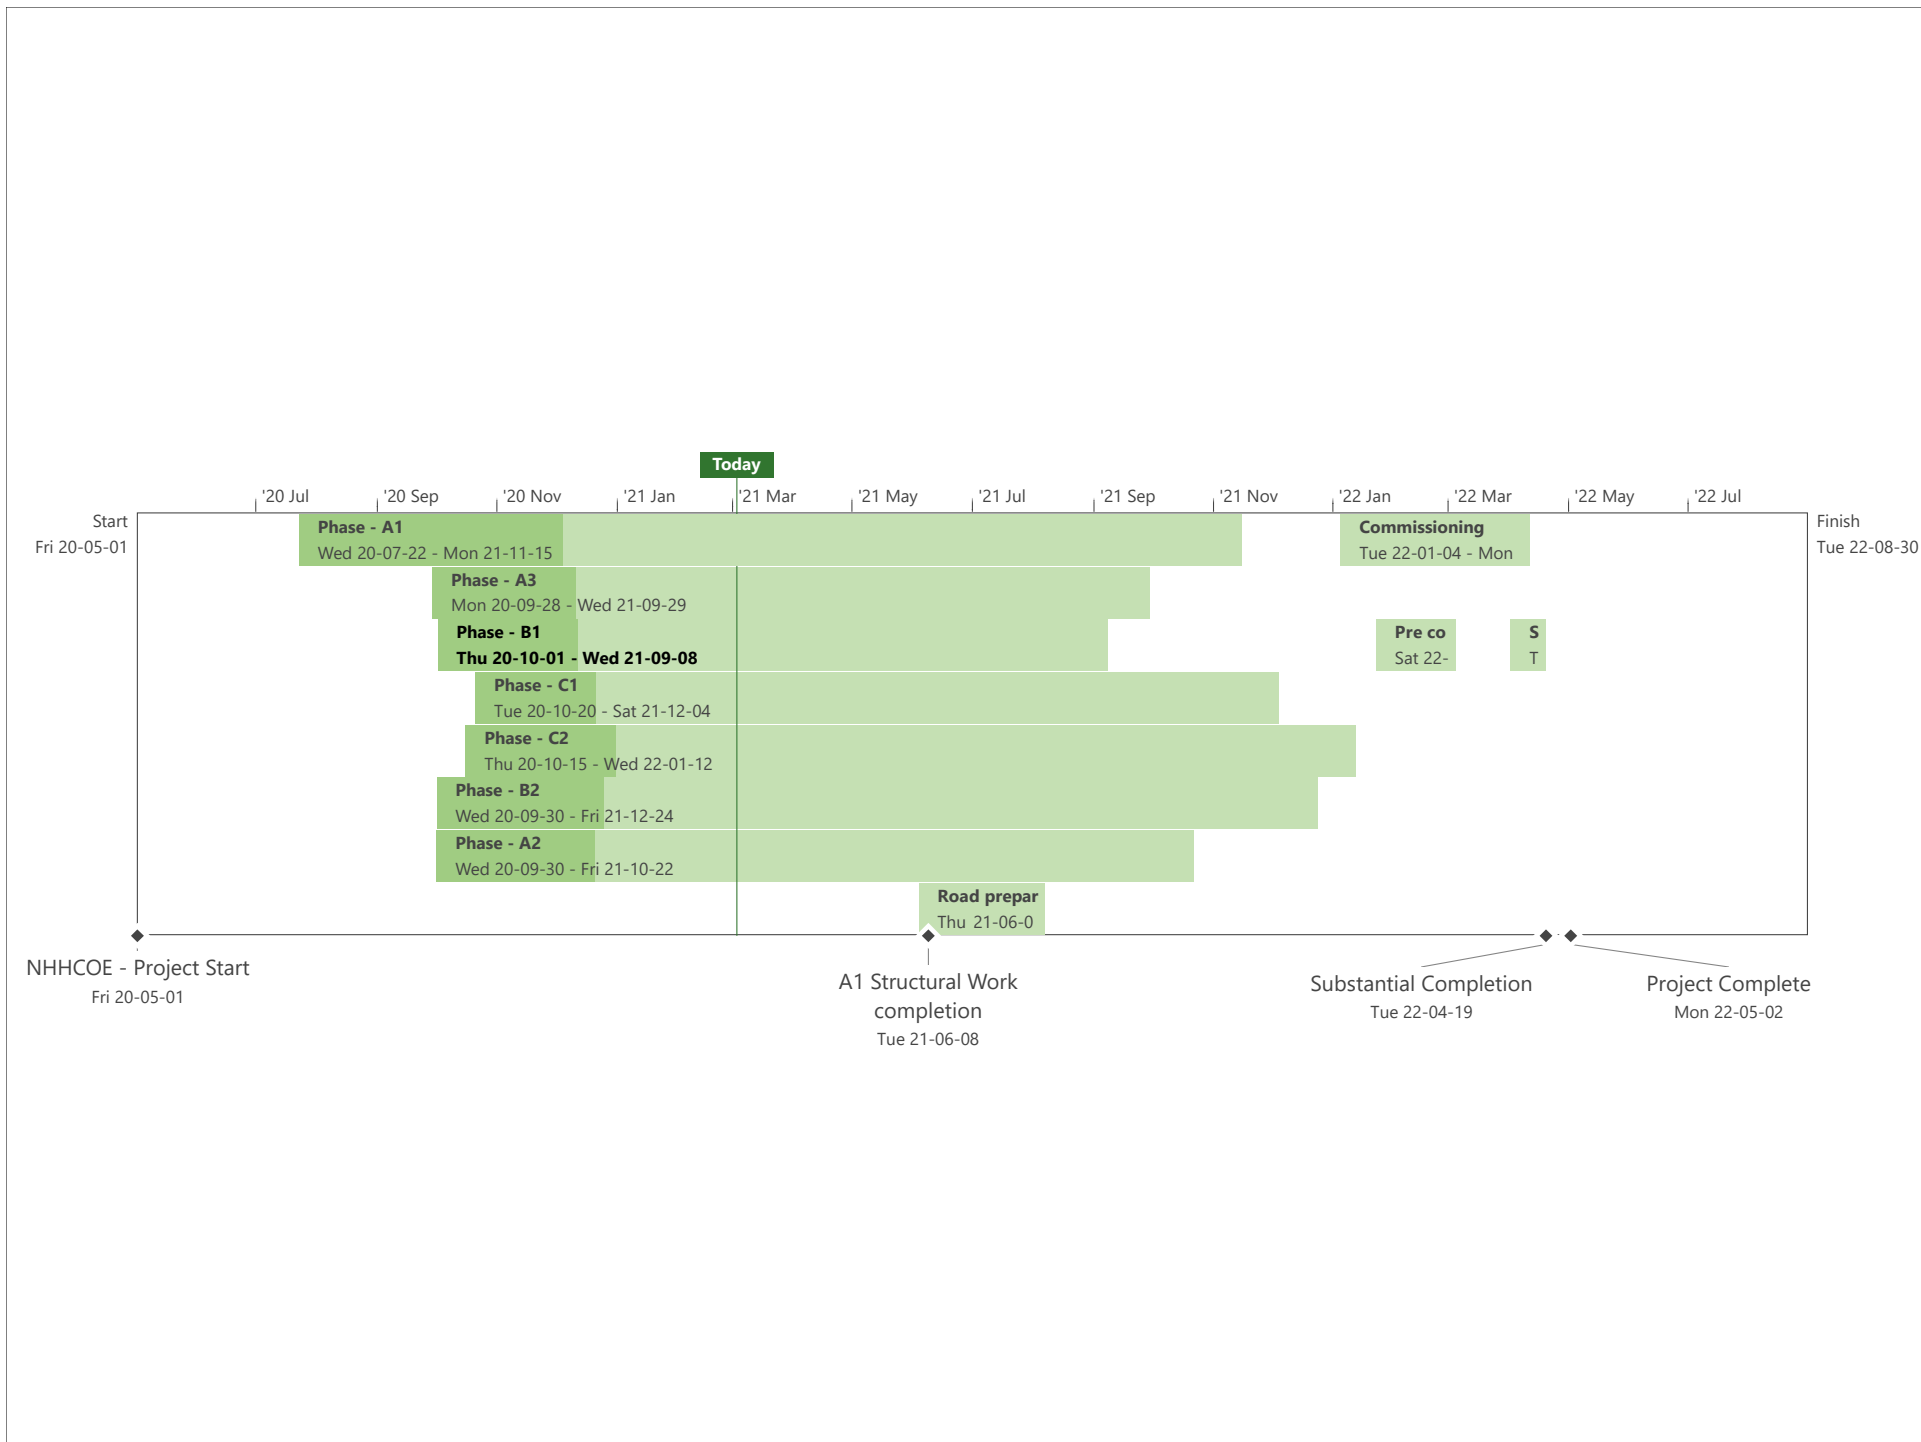


BACKFILL ACTIVITY

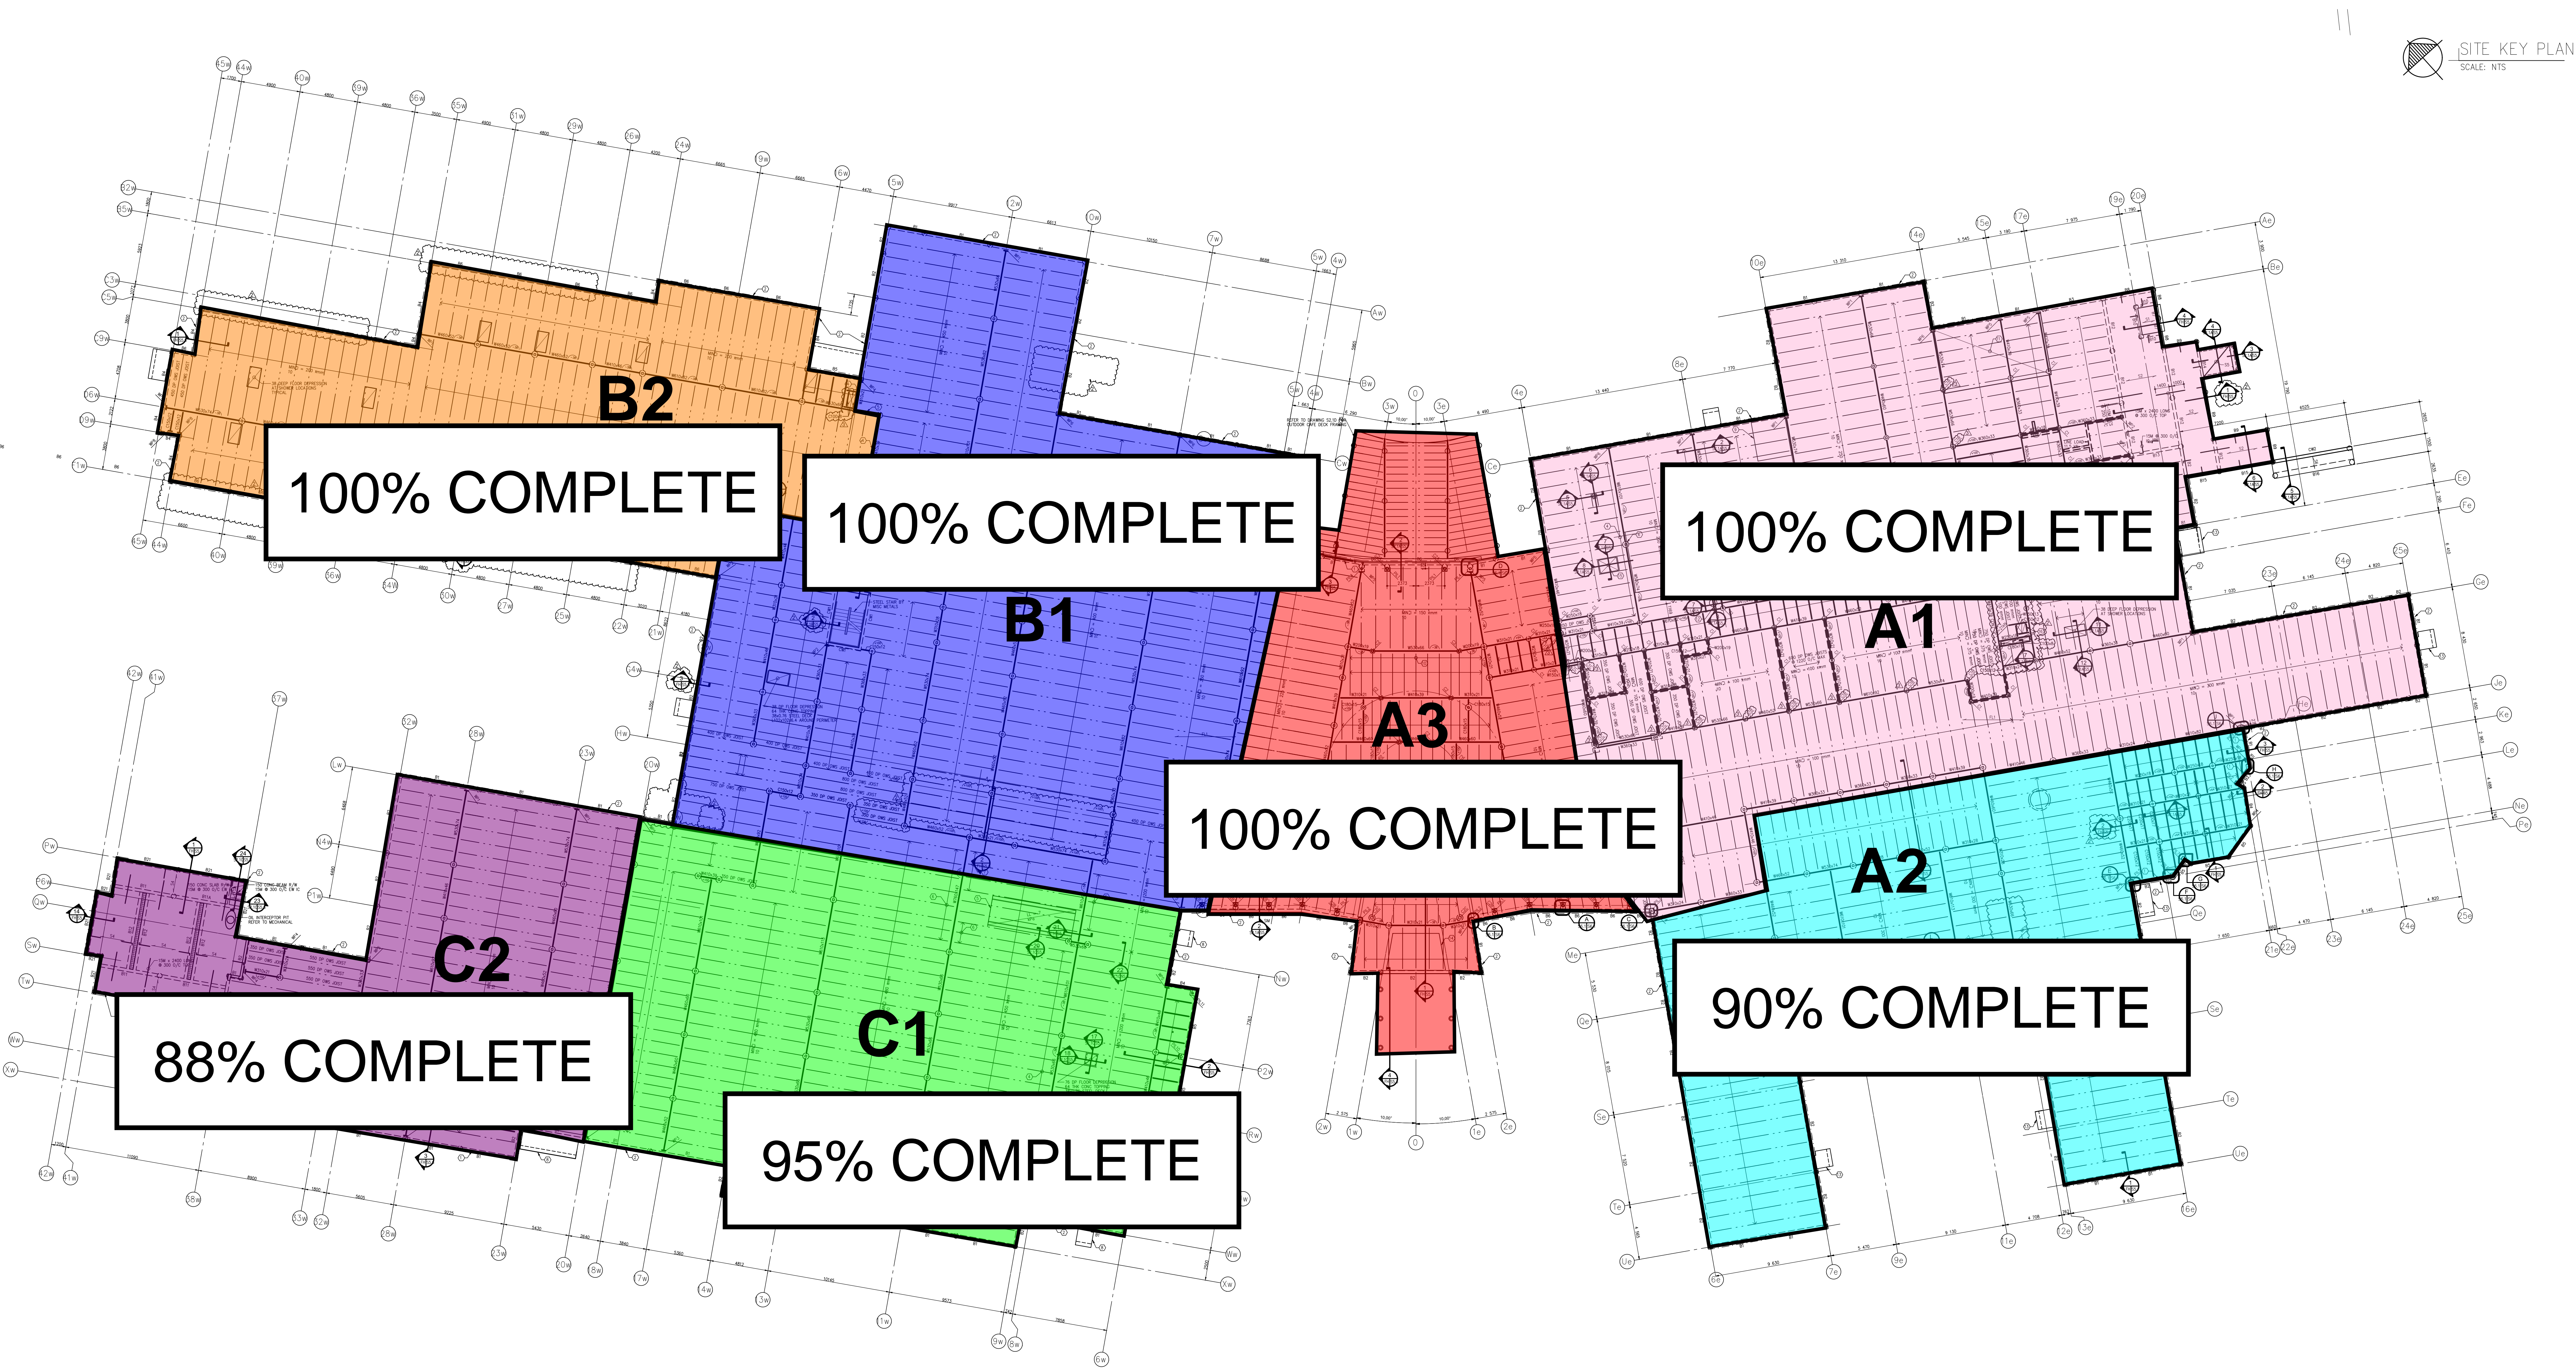


FORMWORK & CONCRETE ACTIVITY - 1

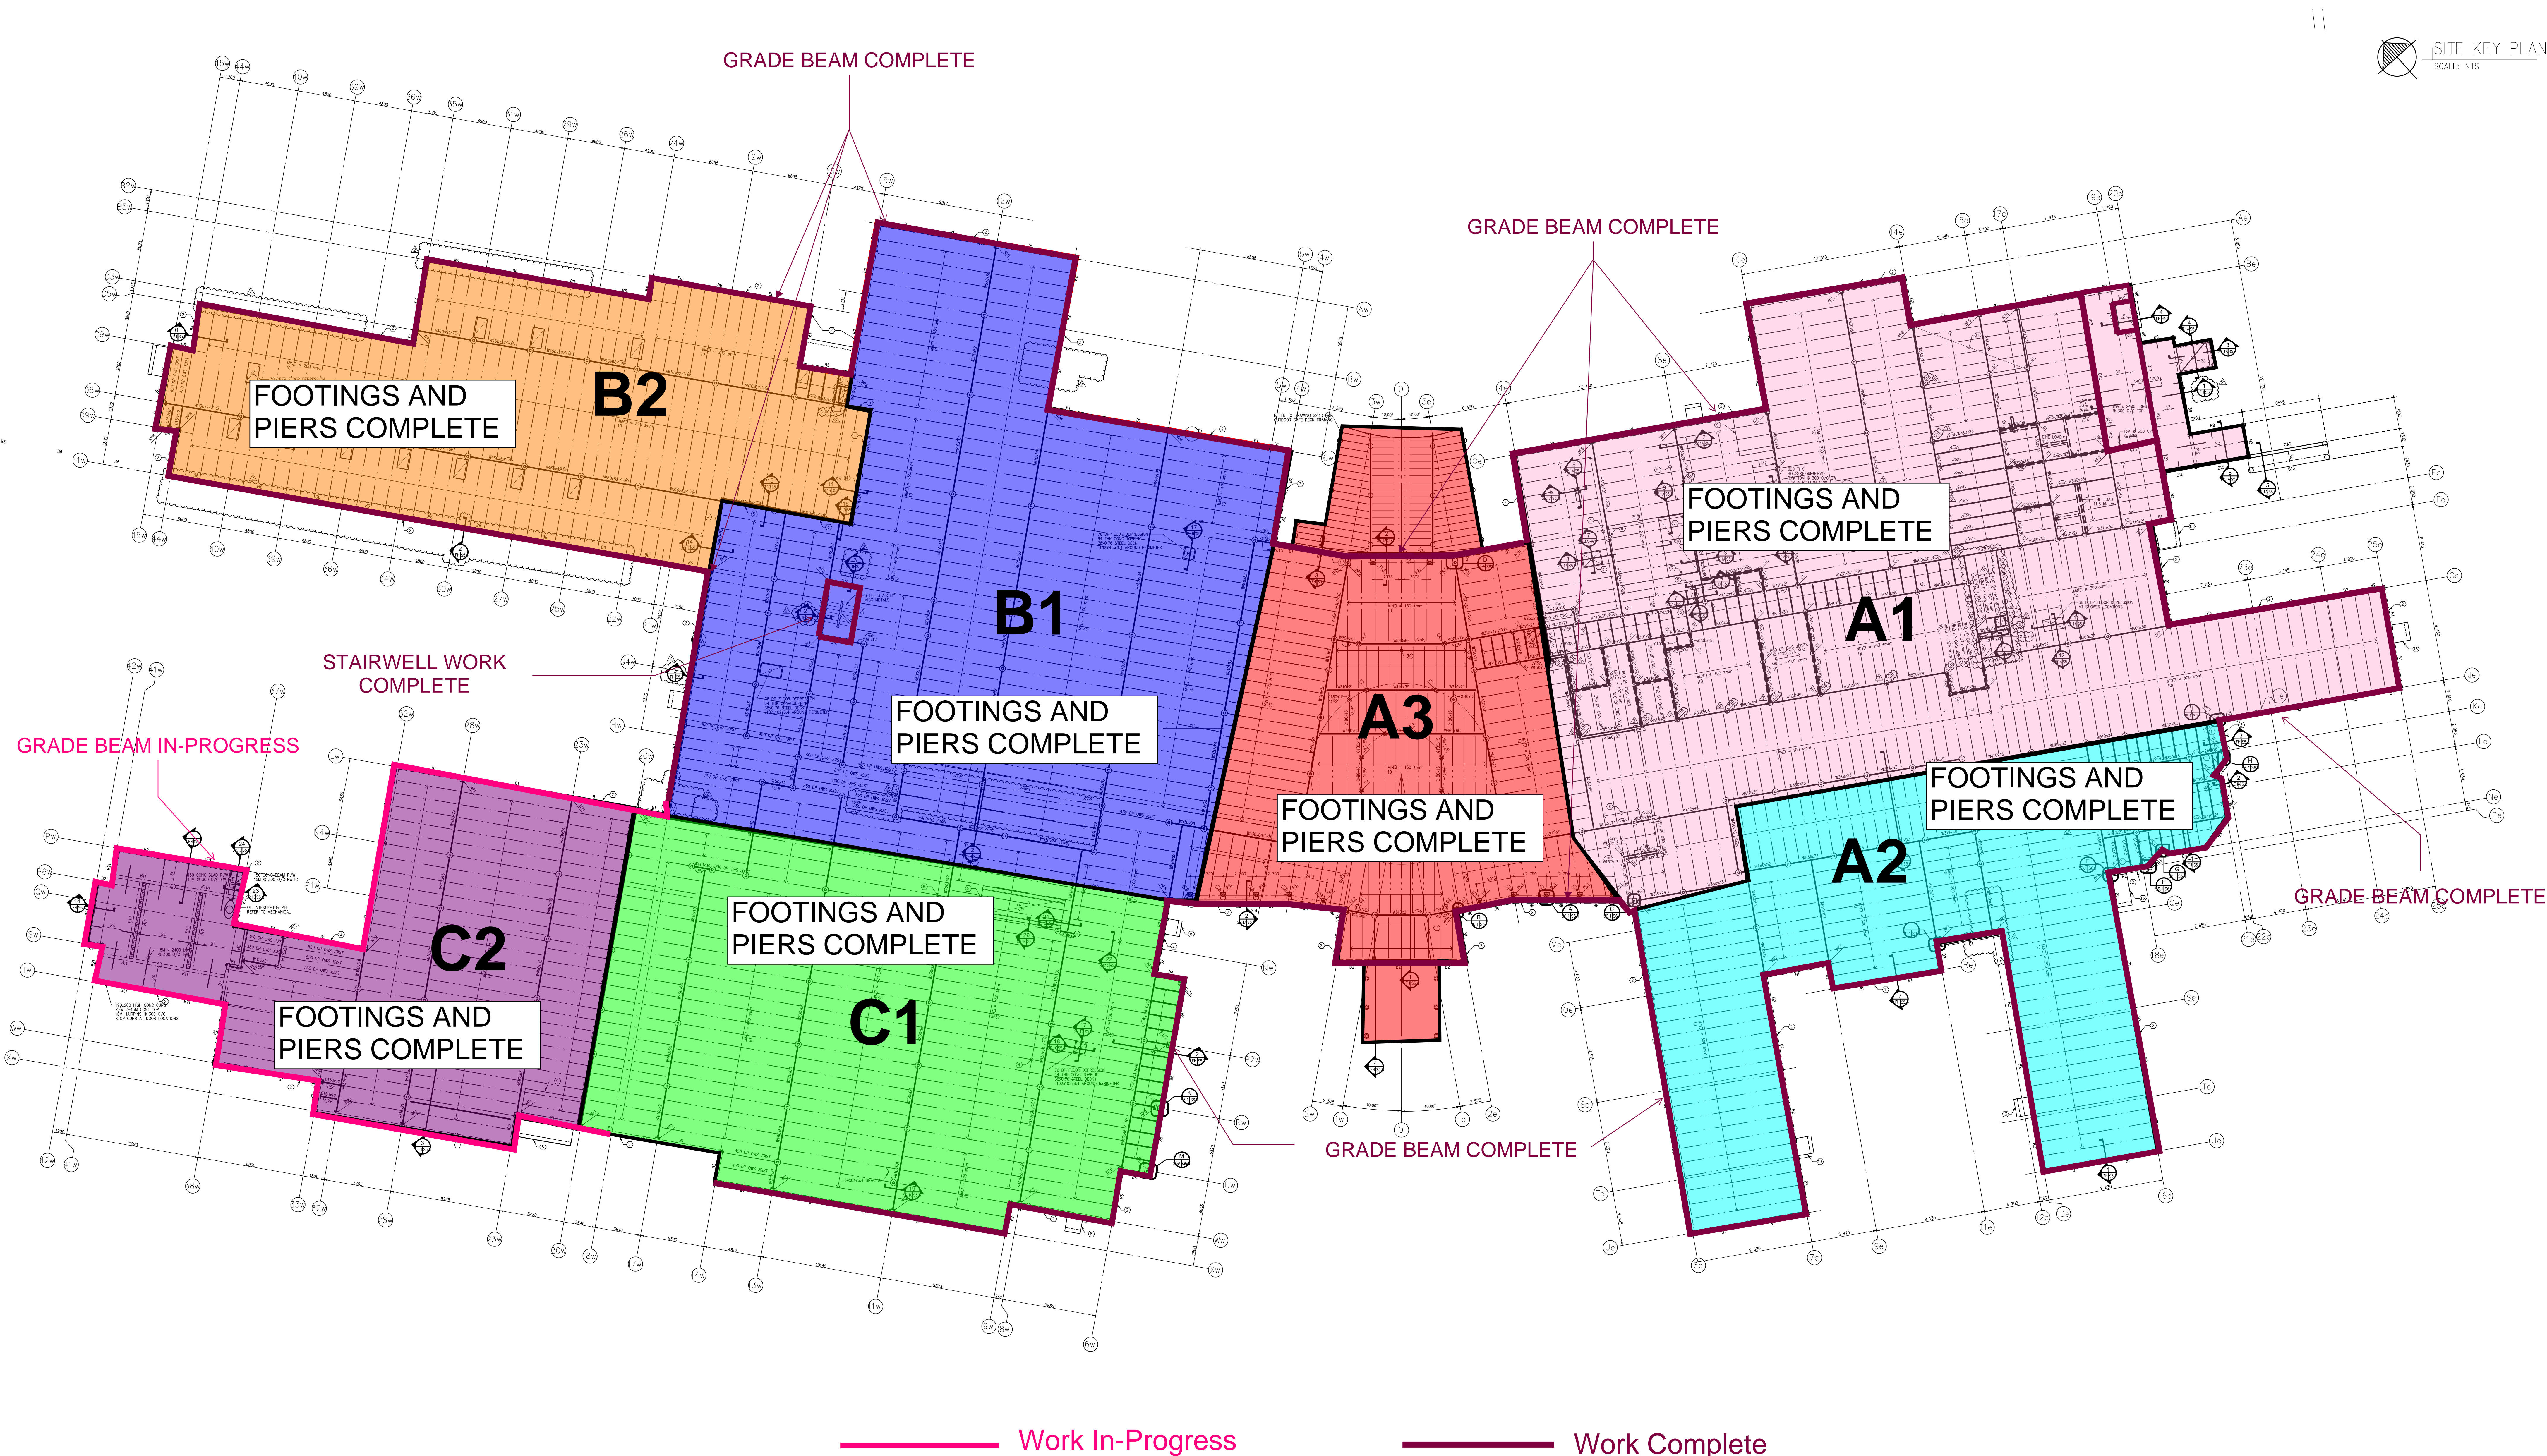


FORMWORK & CONCRETE ACTIVITY - 2

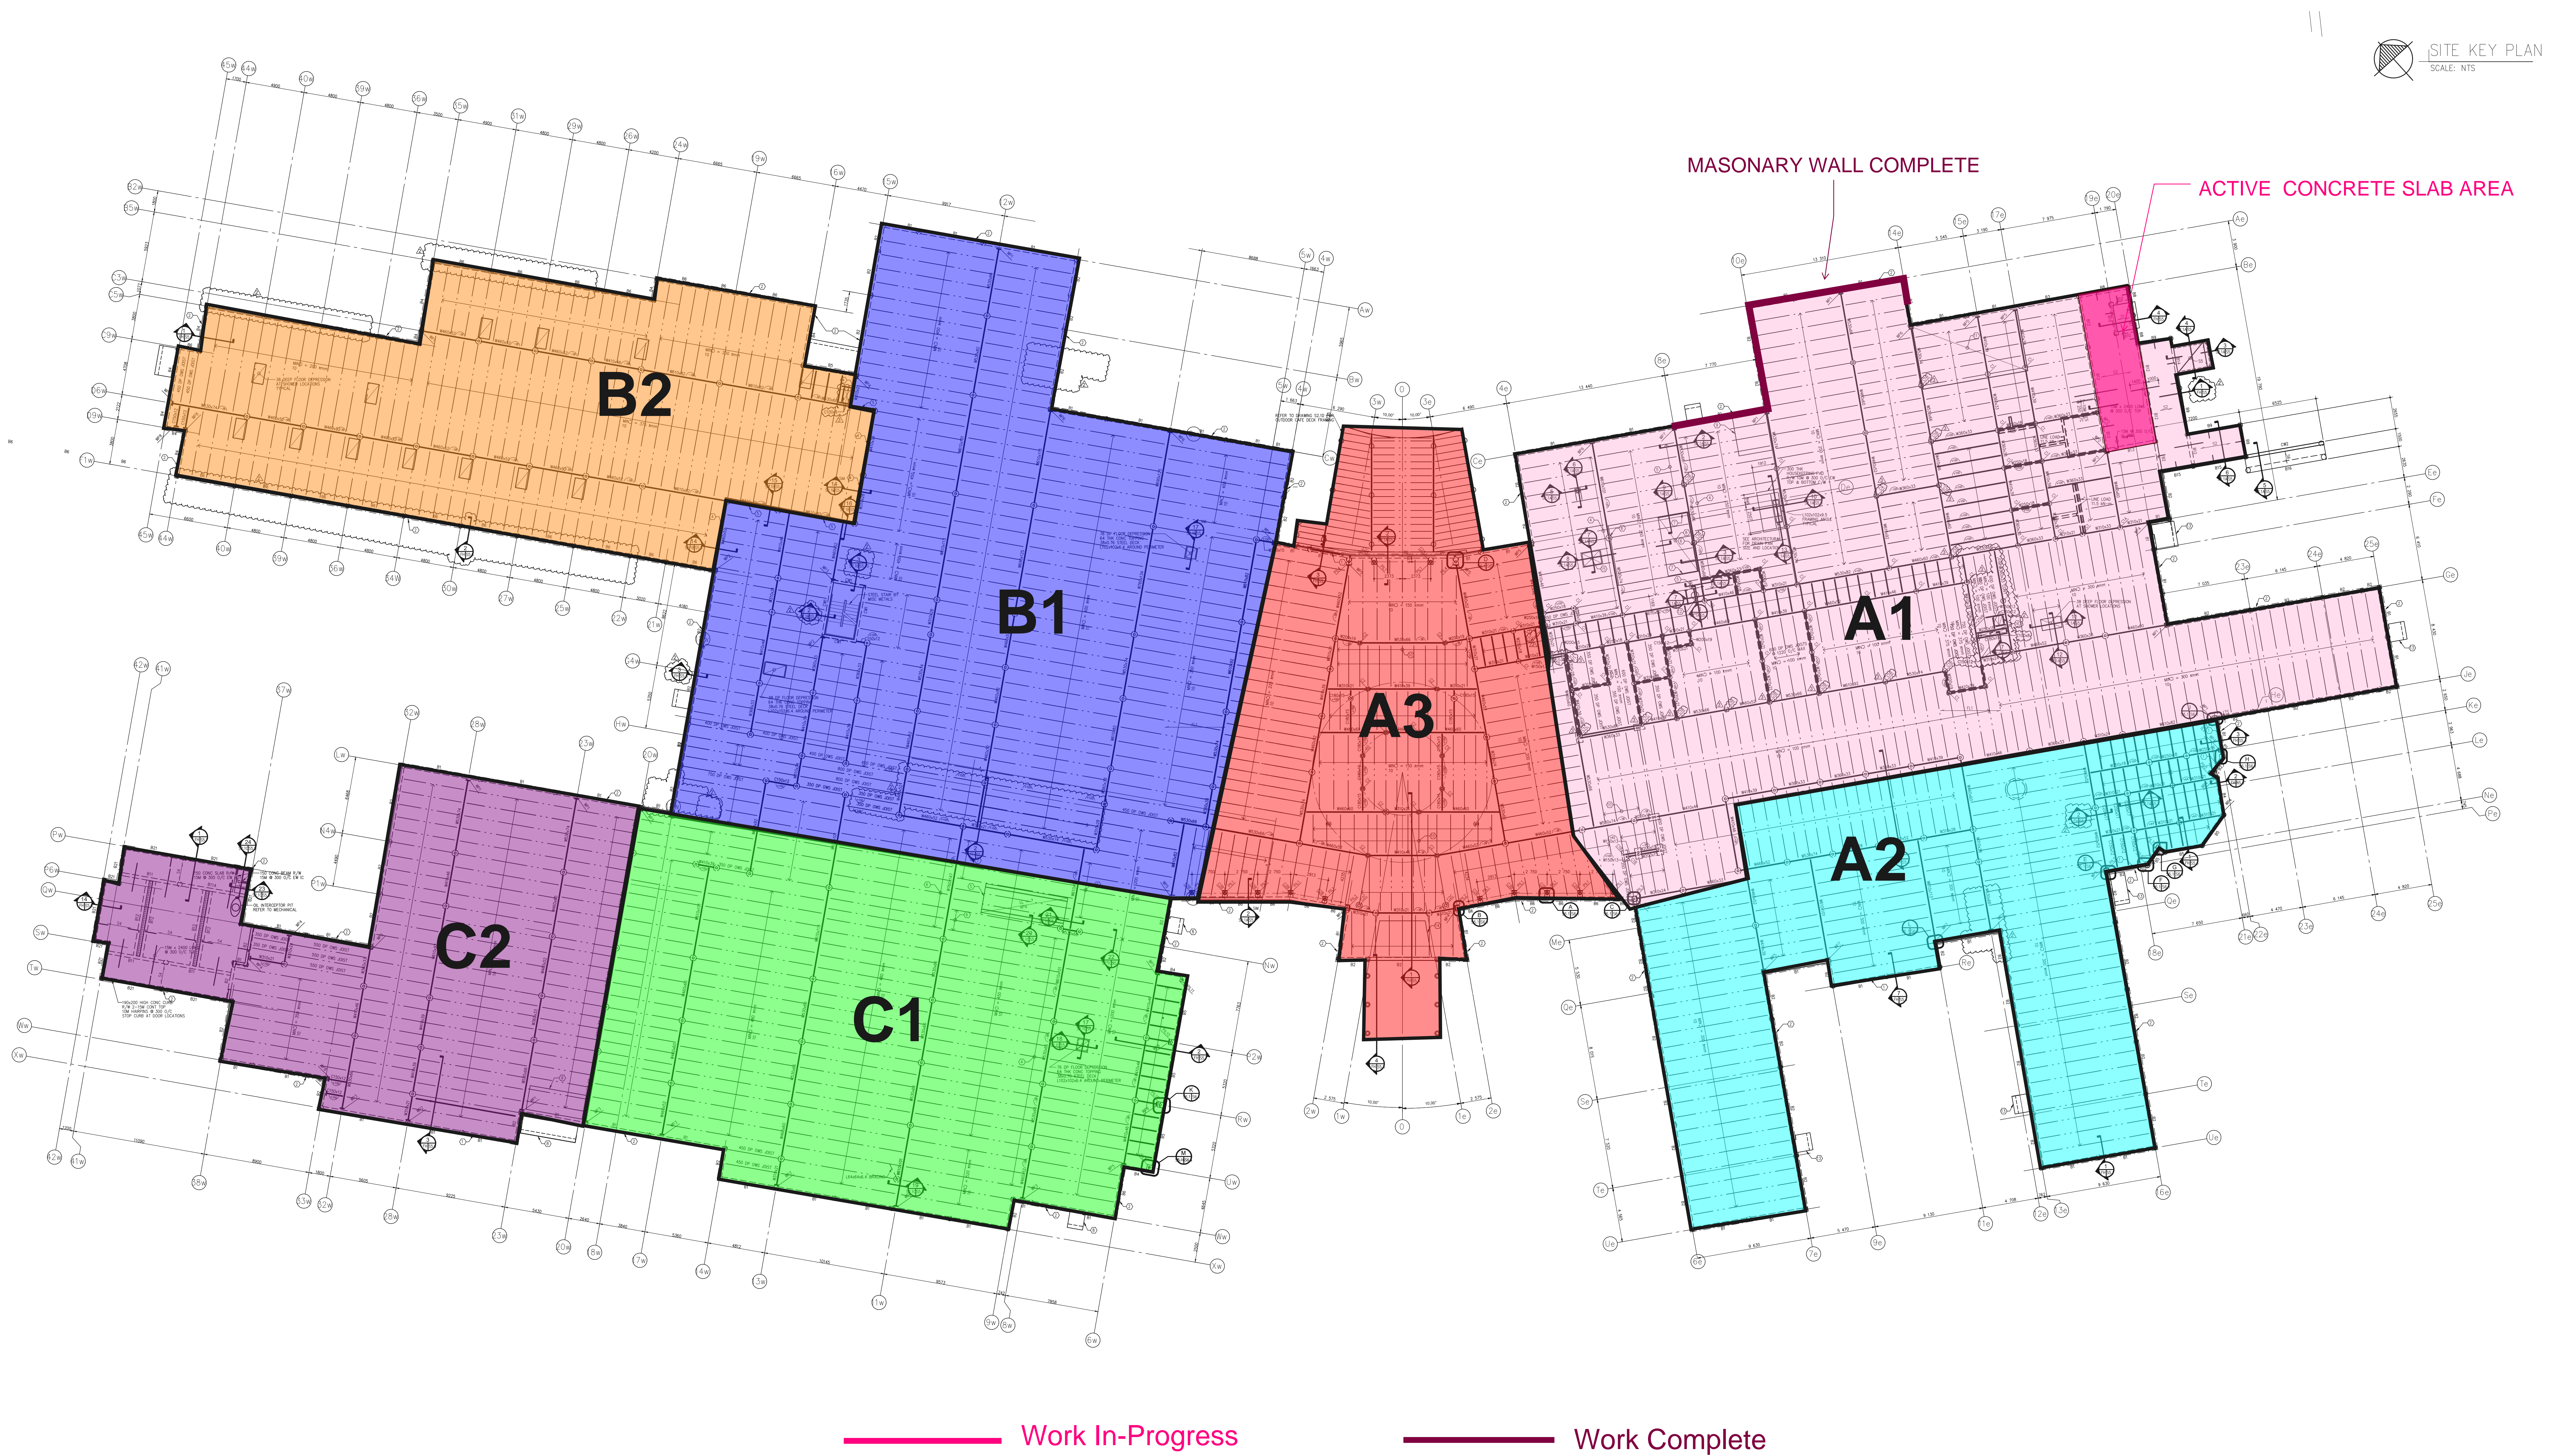

STRUCTURAL STEEL

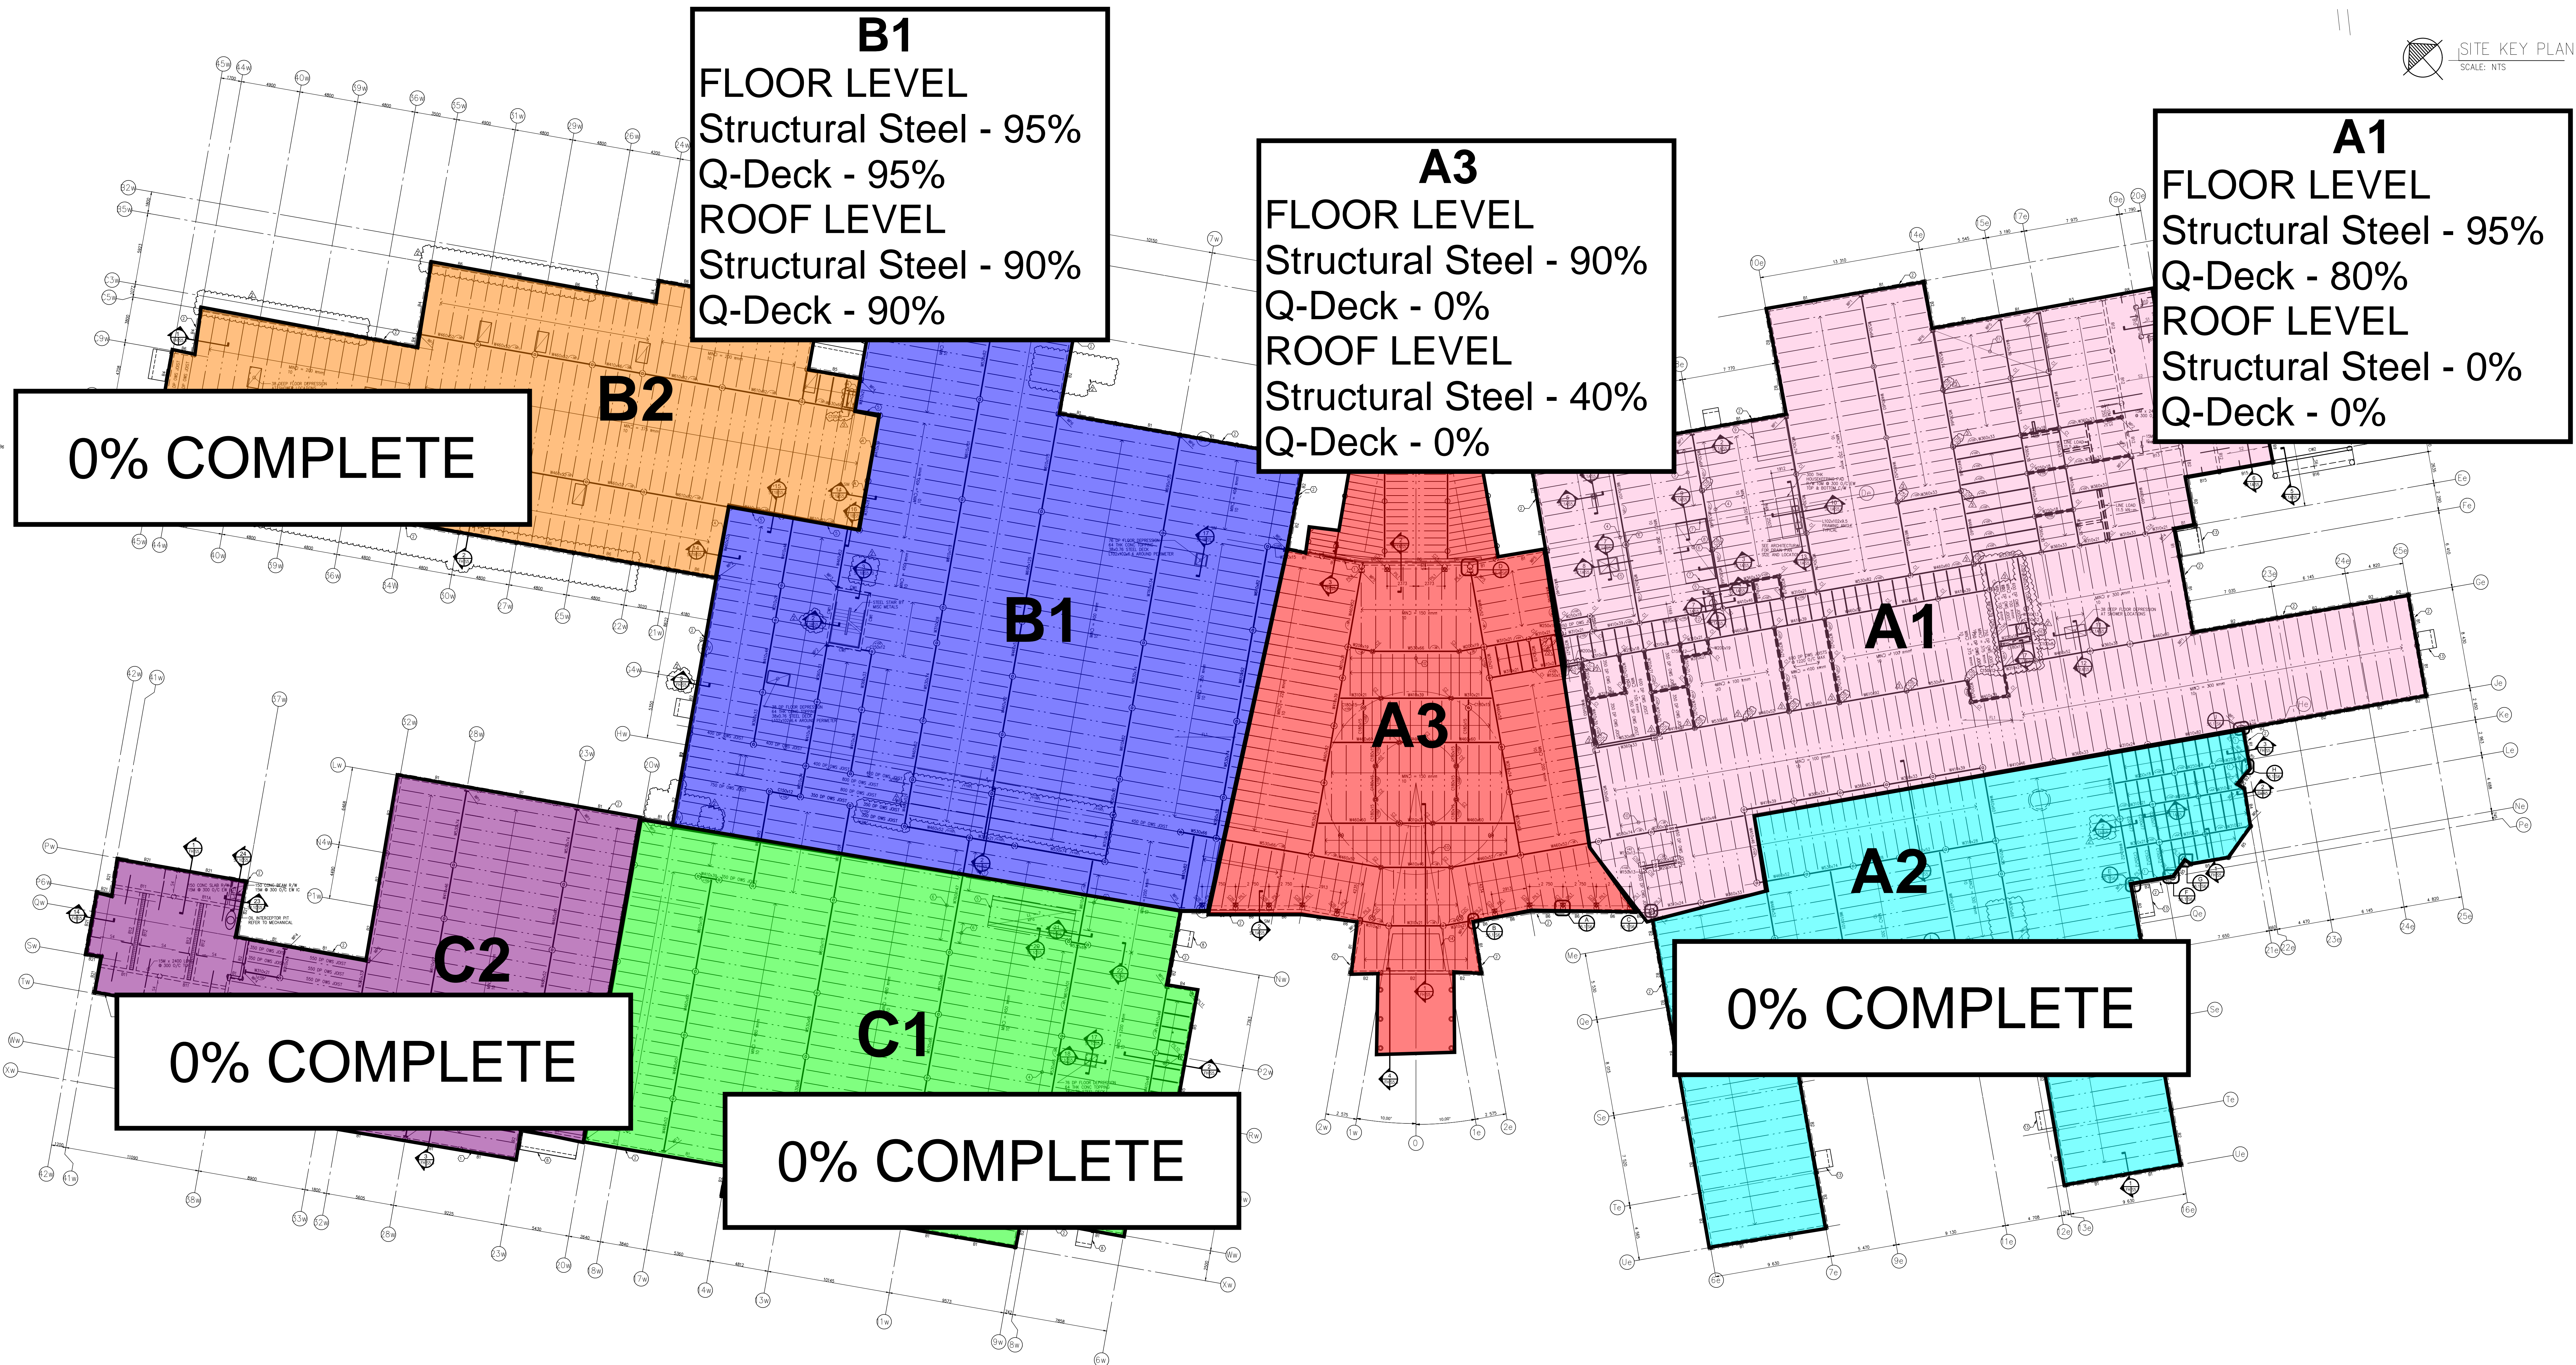

WEEPING TILE UPDATE

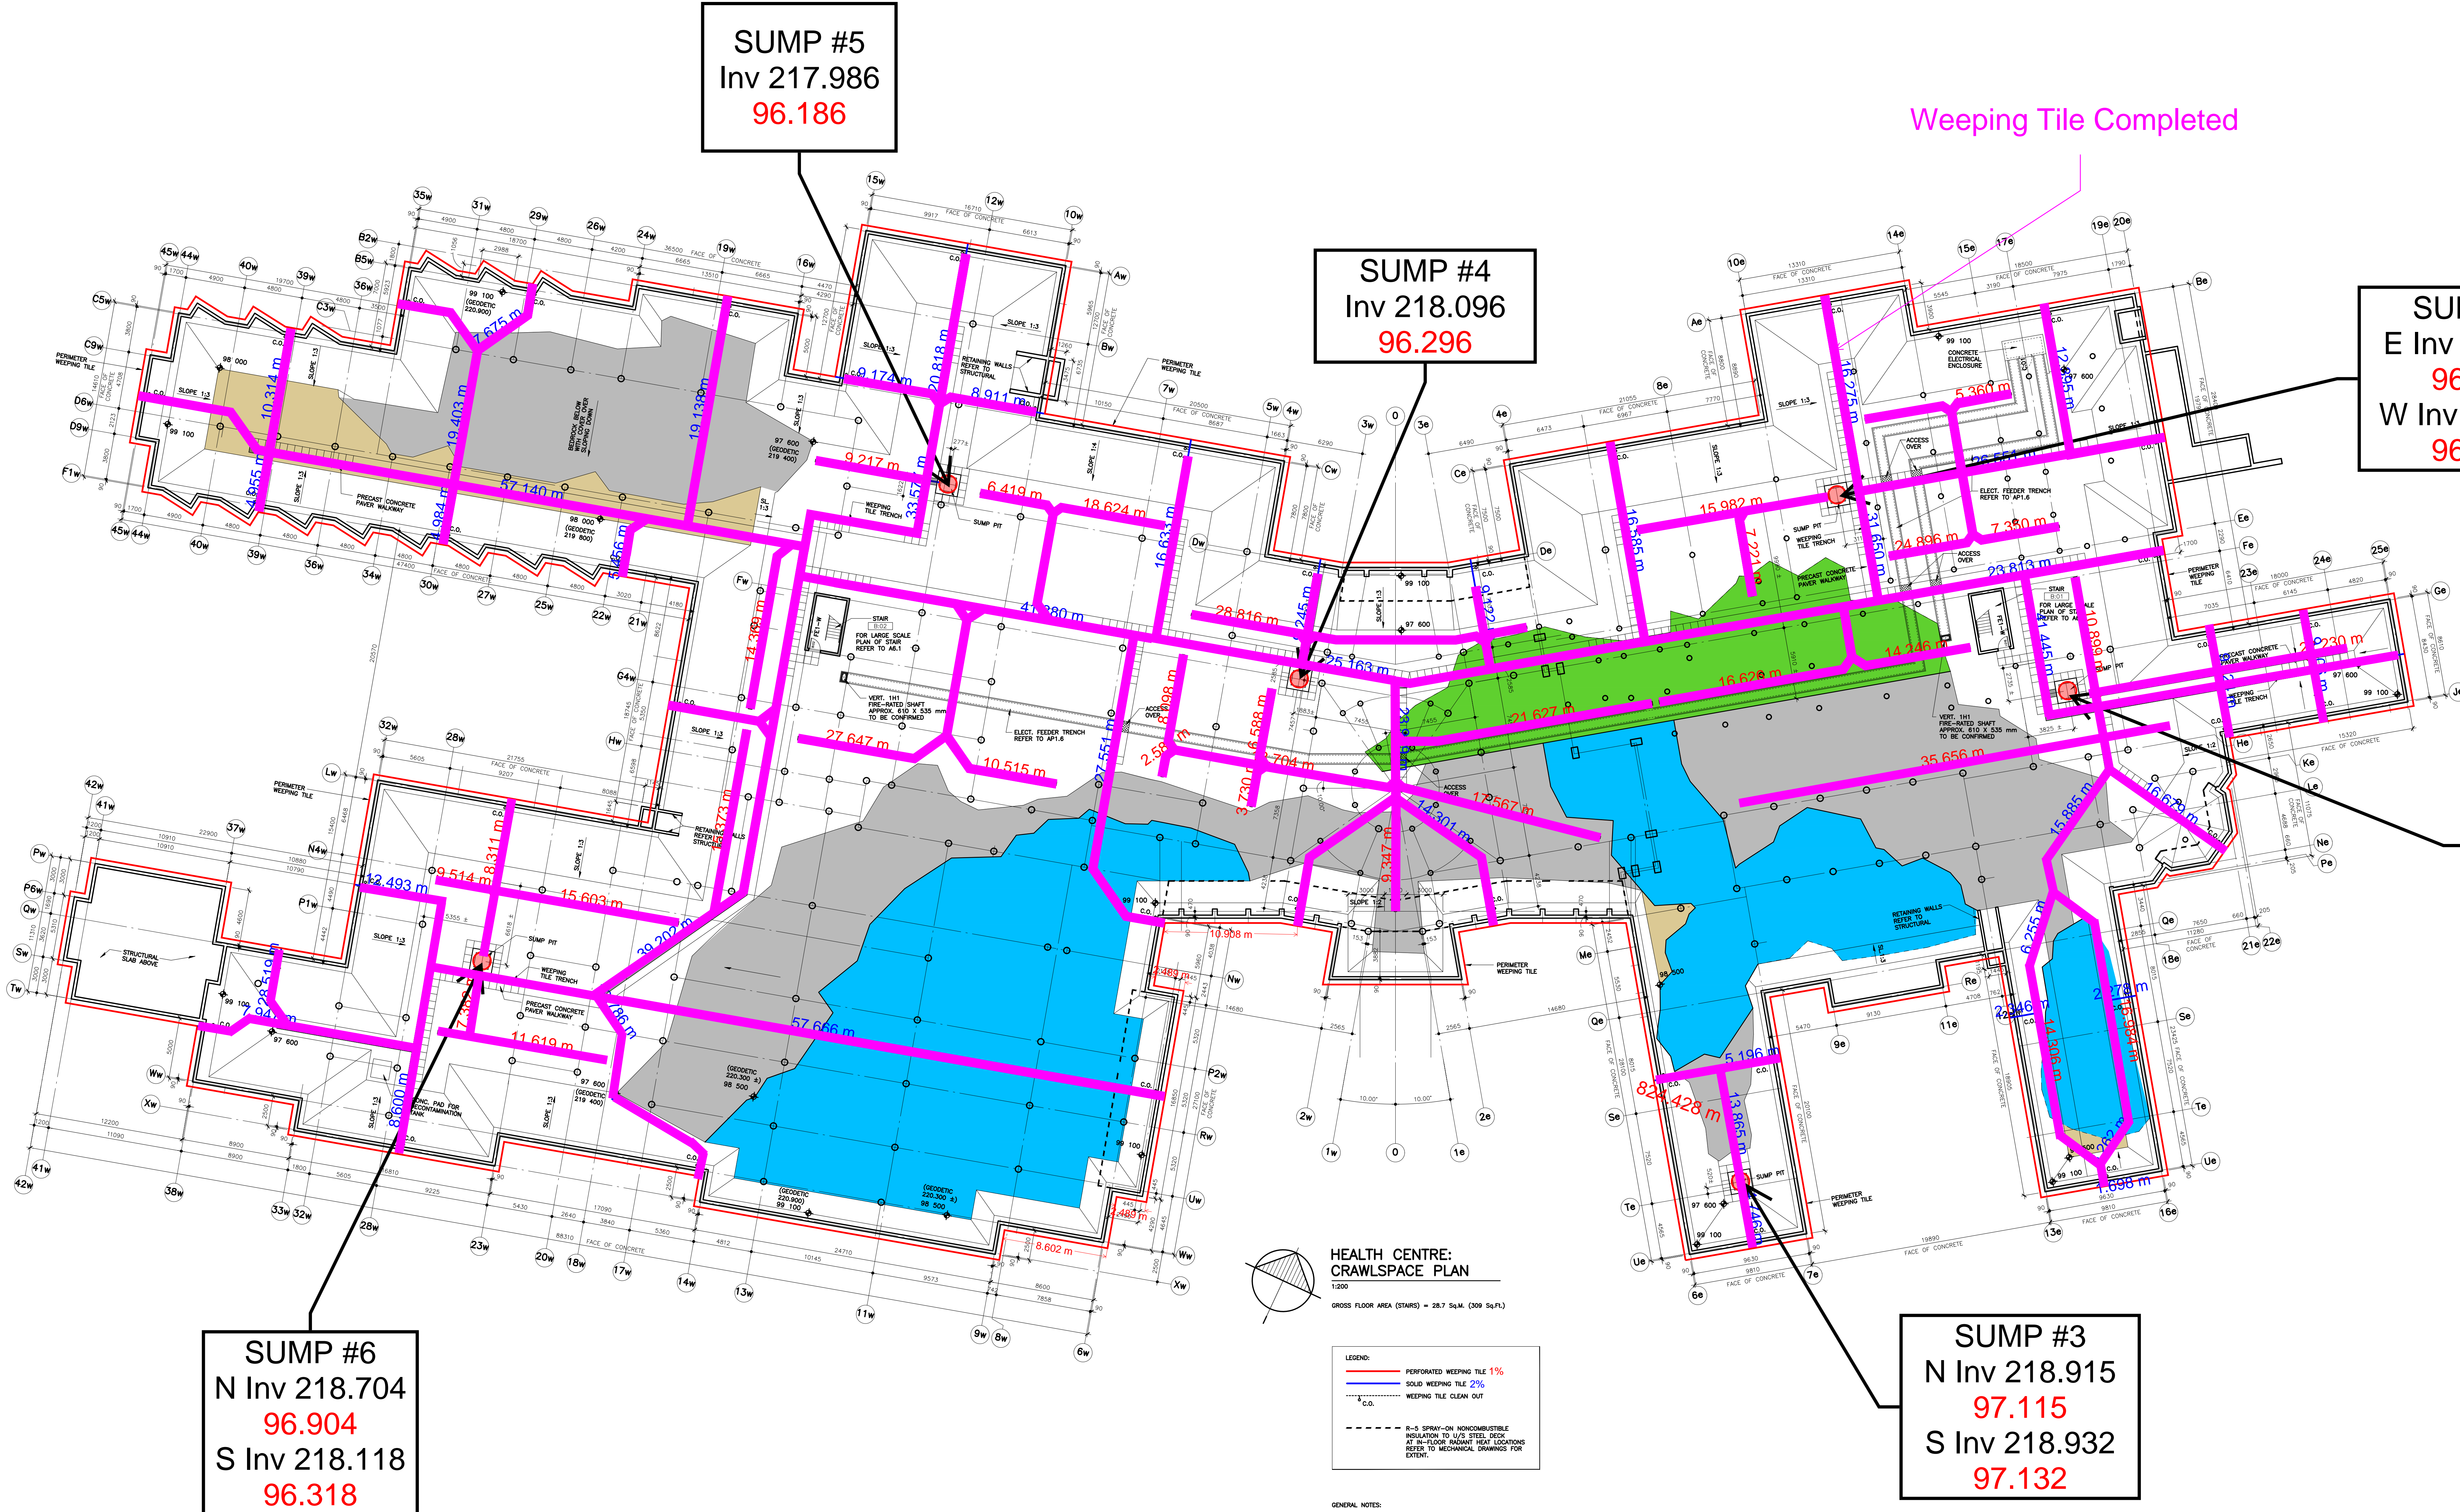

Work Completed
