

Weekly Report

Mar 23th -29nd

2021 Report # 34

Norway House Cree Nation

Health Centre of Excellence



Project:

CD4 – Health Centre of Excellence

Aman Chana

JNR Construction

Weekly Progress Report

Mar 30, 2021, ID #285

REPORT DETAILS

Description

Created by Aman Chana

1. WORK LOG

Crew	# Workers	# Total hours	Work performed
JNR	30	1800	See below for discriptions
Totals	30	1800	

2. CREW ONSITE

2.1 The following crews were active in this report period



JNR



Mechanical



Electrical



Masonry



Structural Steel



Oakwood Roofing Mobilized to site
General site review & setting up C-can & office trailer

3. ARCHITECTURAL

3.1 Ongoing Work

N/A

3.2 Completed Work

N/A

4. STRUCTURAL

4.1 Ongoing Work

Erection of roof structure
Cross bracing in A2
Straightening and torqueing steel structure in A2
Placing Q-deck / Welding (A2)
Erection of Glulam Structure (A3)
Warping up exposed Glulam (A3)

4.2 Completed Work

Concrete
A1 Structural slab rebar install
B1 Main Floor securing hoardings
Building hoardings for grade beam (C2)
Concrete Pour (Structural Slab (A1) / Penthouse (B1) / Stair Slab (B1) - Ref attached drawing)
Preparing for concrete pour (A1-Structural Slab)
Poured concrete in Grade Beam (C2)
Maintenance of Concrete Pump

5. MECHANICAL

5.1 Ongoing Work

Producing required shop drawing submittals -Ongoing

5.2 Completed Work

Off Site for Turn Around

6. ELECTRICAL

6.1 Ongoing Work

Producing required shop drawing submittals -Ongoing

6.2 Completed Work

**Working on temporary power hookup.
Install hanger work packages in area A1, A2
Install work packages in area A1, A2 crawlspace**

7. CIVIL

7.1 Ongoing Work

**Operating Rock Truck / Excavator / Crawler Tractor
Hauling / stockpiling clay for placing around the hospital**

**Surveyor
Crawlspace topographic survey
B1-1 as build survey of floor elevations.
Drafting & data management**

7.2 Completed Work

8. SAFETY AND COVID-19 SCREENING

8.1 Number of Covid Screening reports completed

**JNR is continuing screening all visitors and staff daily who report to site.
180 Covid screening reports completed on site last week.**

9. SITE VISIT SCHEDULE

9.1 Next scheduled site visit

Next scheduled visit to site is to be determined

NOTES

Concrete Pour Notes:

31.5 Cubic M. (Mix #3 - 12 Cubic M. / Mix #5 - 19.5 Cubic M.) of concrete was poured in (Structural Slab (A1) / Slab-on-deck Penthouse (B1) / Stair Slab (B1) - Slab pour drawing attached for ref.)

40 Cubic M. of concrete was poured in slab-on-deck (B1-1 - Slab pour drawing attached for ref.)

43 Cubic M. (Mix #2) of concrete was poured in Grade Beam (C2 - Pour drawing attached for ref.)

PHOTOS (30)



A3- Wrapping up Glulam beams & column

Arshdeep Grewal

Mar 28, 2021 1:12 PM



A3- Wrapping up Glulam beams & column

Arshdeep Grewal

Mar 28, 2021 1:12 PM



B1 Penthouse - Fixing hoardings
Arshdeep Grewal
Mar 28, 2021 1:12 PM



B1- Surveyor checking elevation
Arshdeep Grewal
Mar 28, 2021 1:12 PM



Oakwood Roofing setting up office trailer

Arshdeep Grewal

Mar 28, 2021 1:12 PM



A2- Erection of Roof Structure

Arshdeep Grewal

Mar 28, 2021 1:12 PM



A2- Erection of roof structure
Arshdeep Grewal
Mar 27, 2021 1:15 PM



Compacting concrete poured in Grade Beam
Arshdeep Grewal
Mar 27, 2021 1:15 PM



C2- Pouring Grade Beam
Arshdeep Grewal
Mar 27, 2021 1:15 PM



C2- Concrete Pump used for pouring concrete
Arshdeep Grewal
Mar 27, 2021 1:15 PM



B1- Stair Slab
Arshdeep Grewal
Mar 27, 2021 1:15 PM



B1-1 - Slab-on-deck
Arshdeep Grewal
Mar 27, 2021 1:15 PM



B1-1 - Slab-on-deck
Arshdeep Grewal
Mar 27, 2021 1:15 PM



Aerial view of site
Wayne Dee
Mar 27, 2021 10:26 AM



Aerial view of site
Wayne Dee
Mar 27, 2021 10:26 AM



A3- Aerial view of Glulam Installed
Wayne Dee
Mar 27, 2021 10:26 AM



B1- Aerial view of hoardings around pouring areas

Wayne Dee

Mar 27, 2021 10:21 AM



Setting up concrete pump for pour

Wayne Dee

Mar 27, 2021 10:16 AM



A2- Structural steel

Wayne Dee

Mar 27, 2021 10:16 AM



Manitoba Hydro stringing cables from pole to C-Can

Arshdeep Grewal

Mar 26, 2021 8:24 AM



A1- Concrete pouring in Structural Slab
Arshdeep Grewal
Mar 26, 2021 8:24 AM



A1- Wescan Electrical installing hangers
Arshdeep Grewal
Mar 26, 2021 8:24 AM



A1- Sump pit cover
Arshdeep Grewal
Mar 26, 2021 8:24 AM



B1- Placing concrete over deck
Arshdeep Grewal
Mar 24, 2021 4:50 PM



A3- Preparing for Glulam installation
Arshdeep Grewal
Mar 24, 2021 4:50 PM



A1- Installing Q-deck
Arshdeep Grewal
Mar 24, 2021 4:50 PM



A2- Erection of roof structure
Arshdeep Grewal
Mar 24, 2021 4:50 PM



B1- Concrete Screenshot
Arshdeep Grewal
Mar 24, 2021 4:50 PM




B1- Smoothing concrete surfaces
Arshdeep Grewal
Mar 24, 2021 4:50 PM




A3- Erection of roof structure
Arshdeep Grewal
Mar 24, 2021 4:42 PM


BACKFILL ACTIVITY

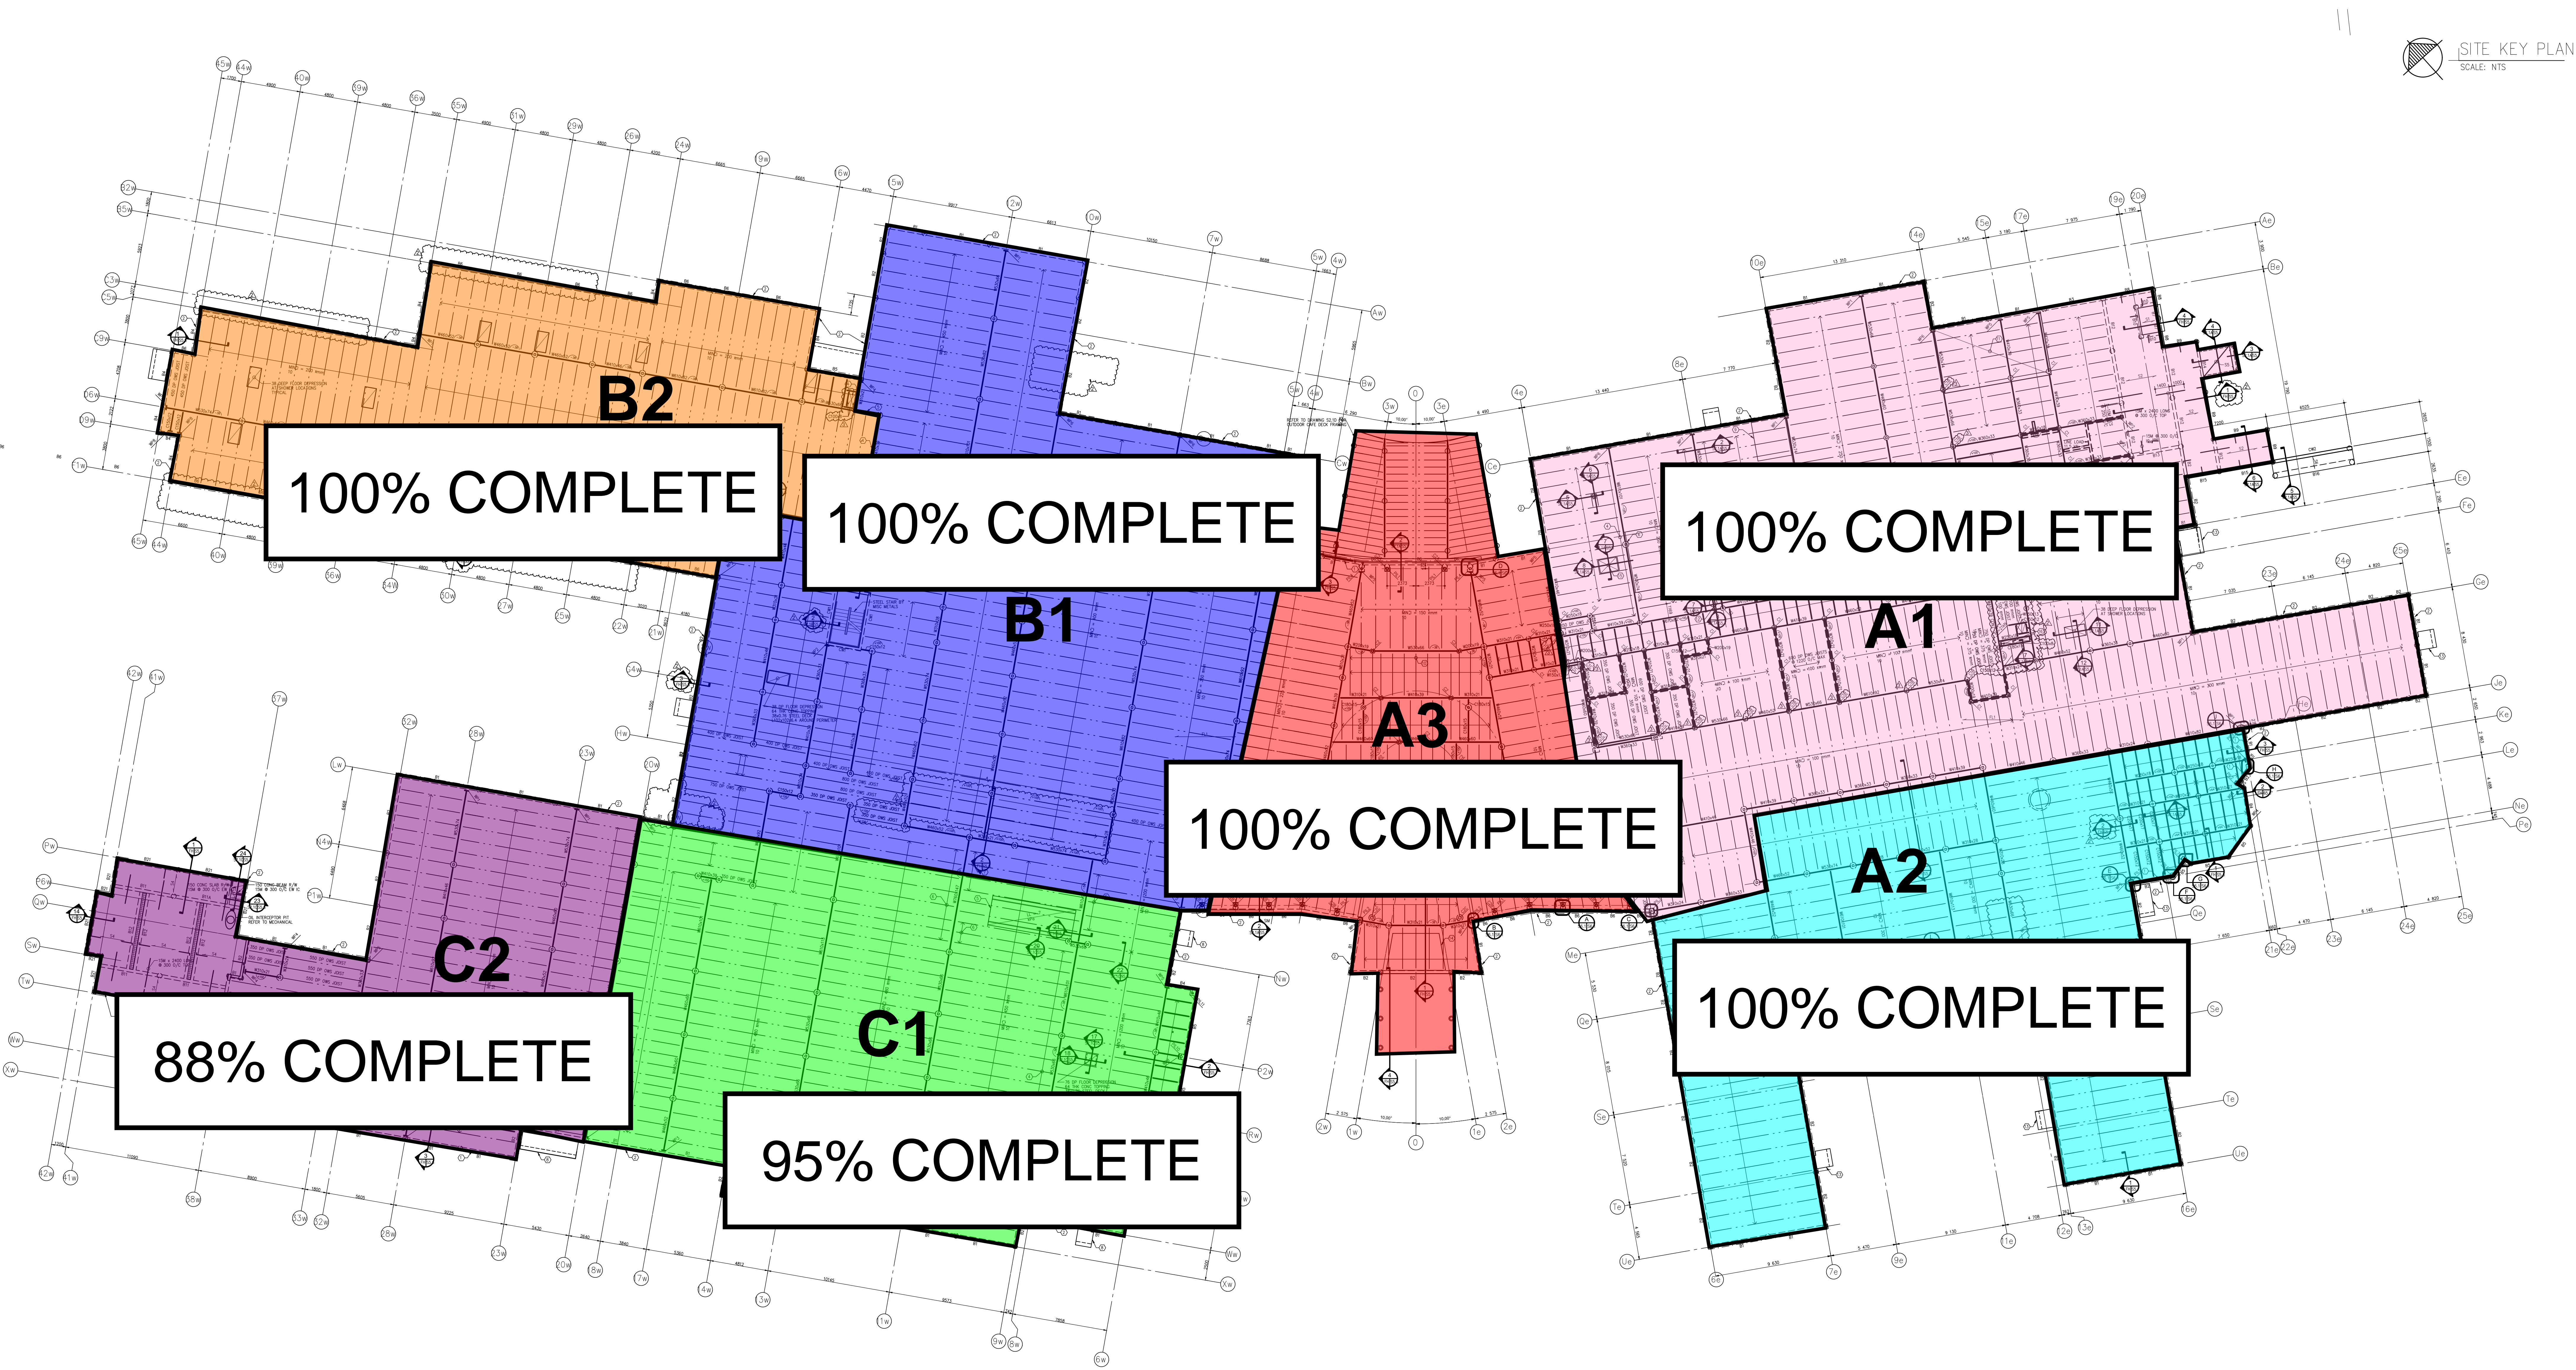


CONCRETE SLAB ACTIVITY

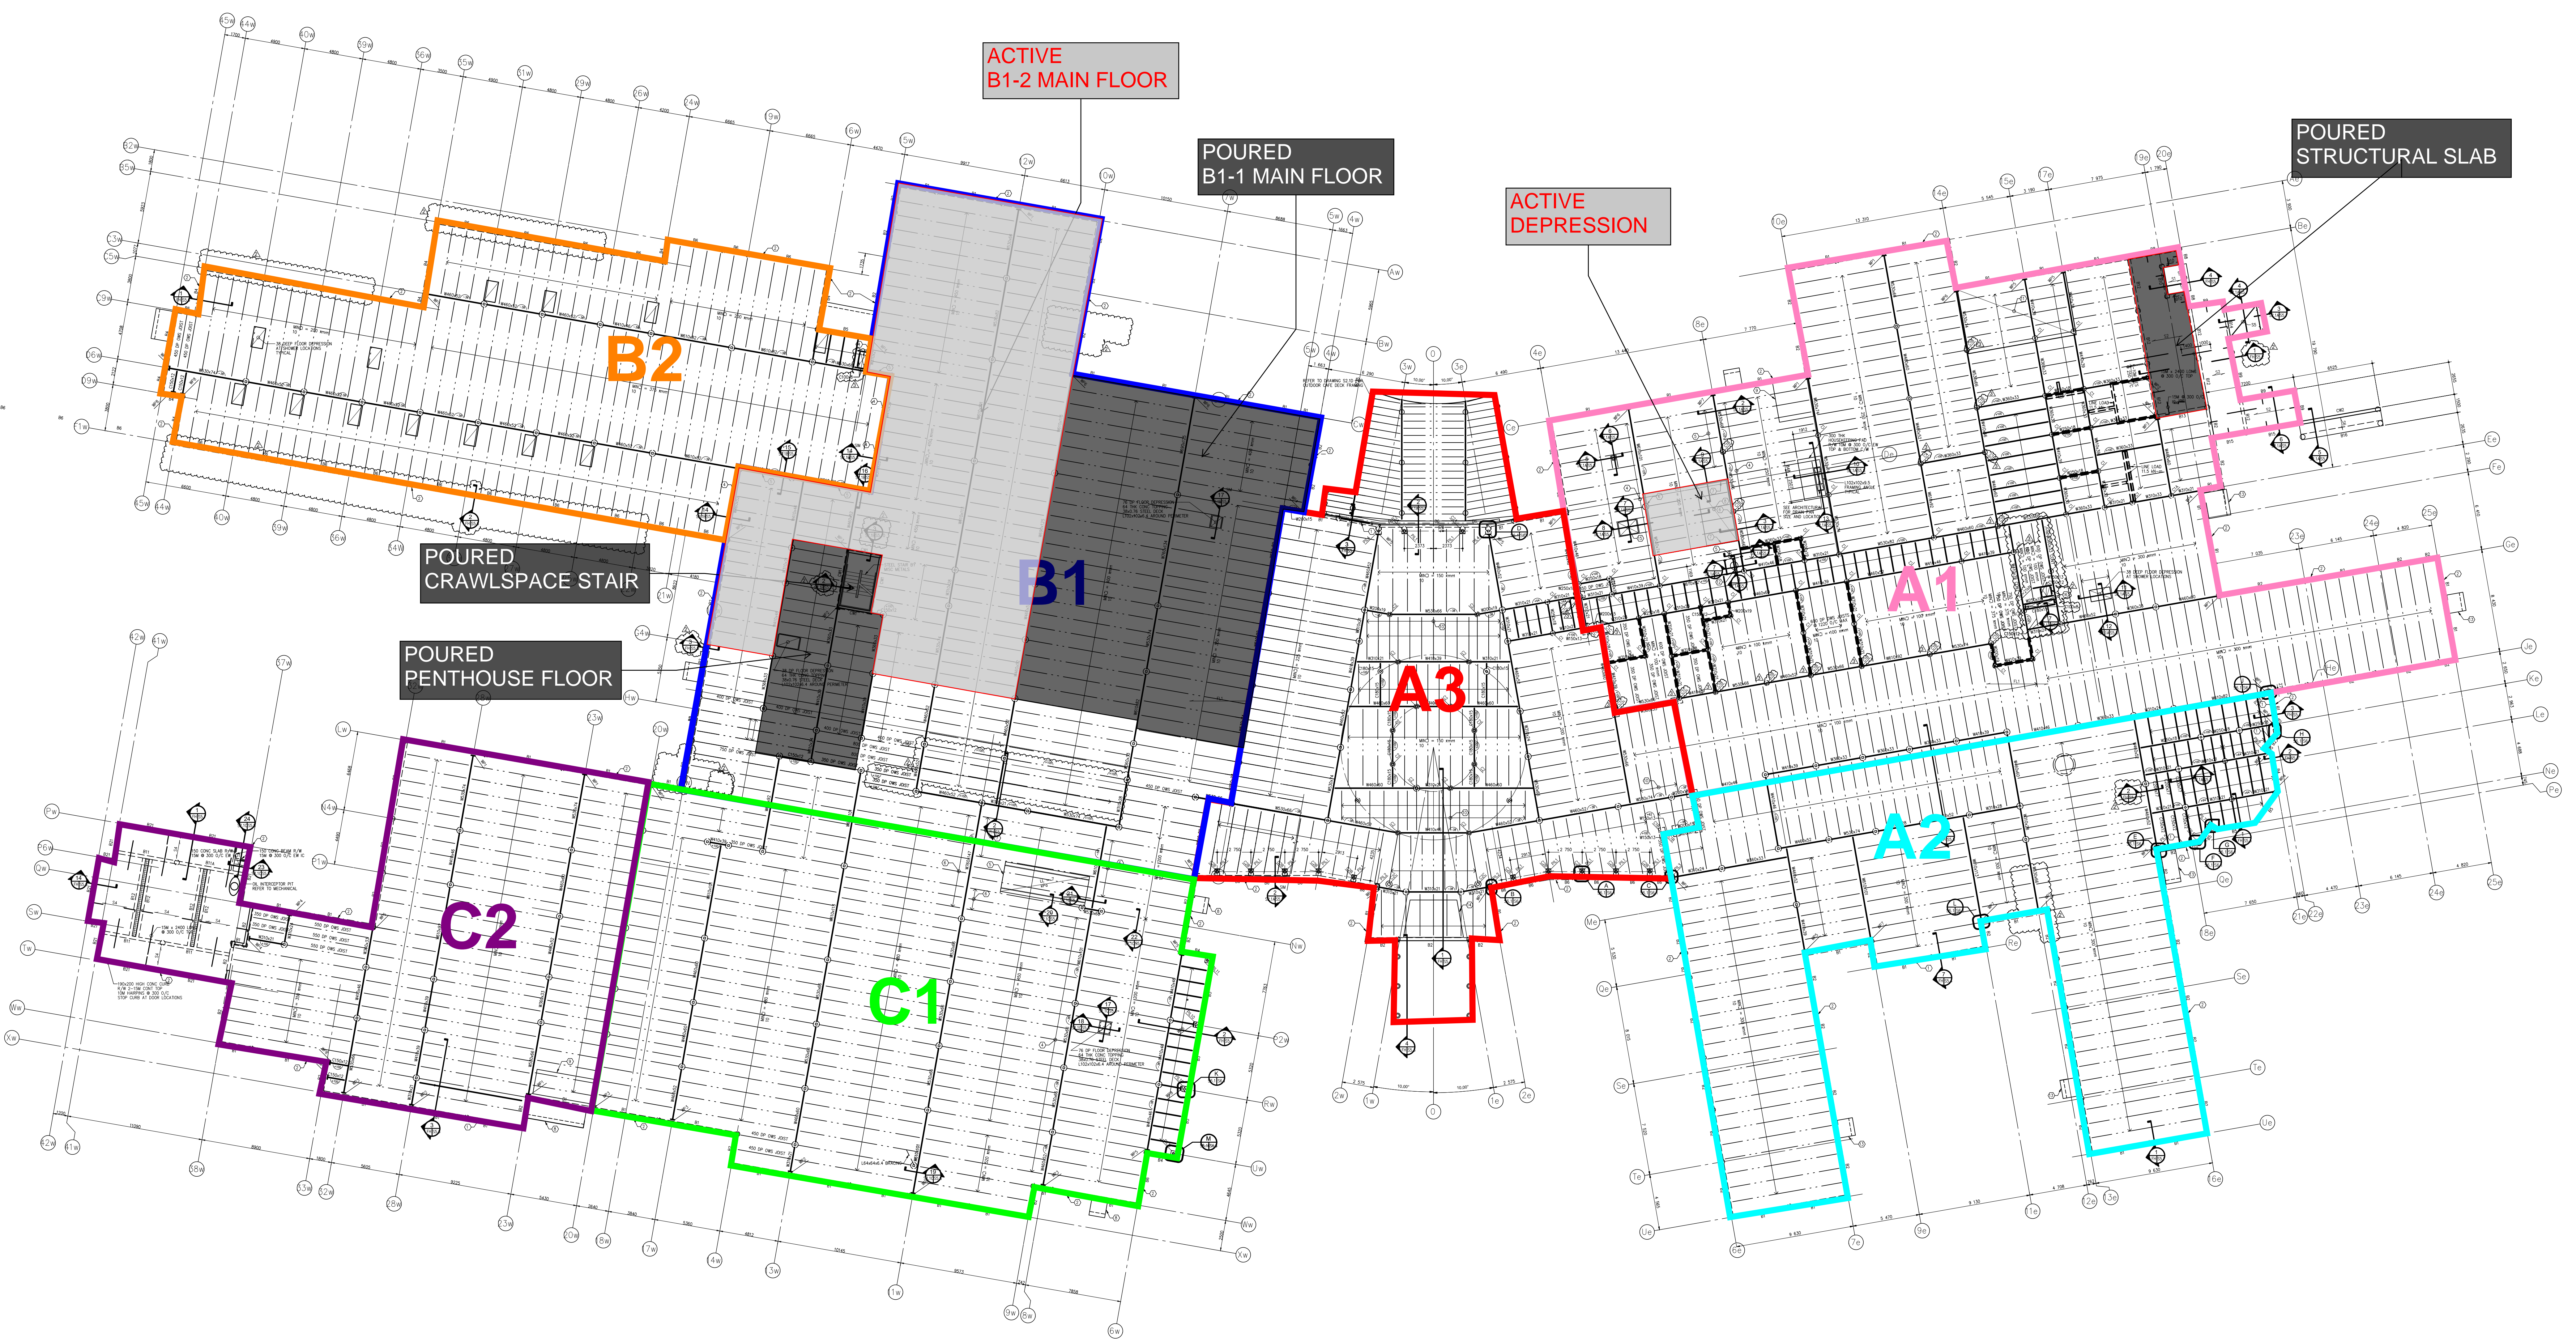


FOOTING, PIER & GRADE BEAM ACTIVITY

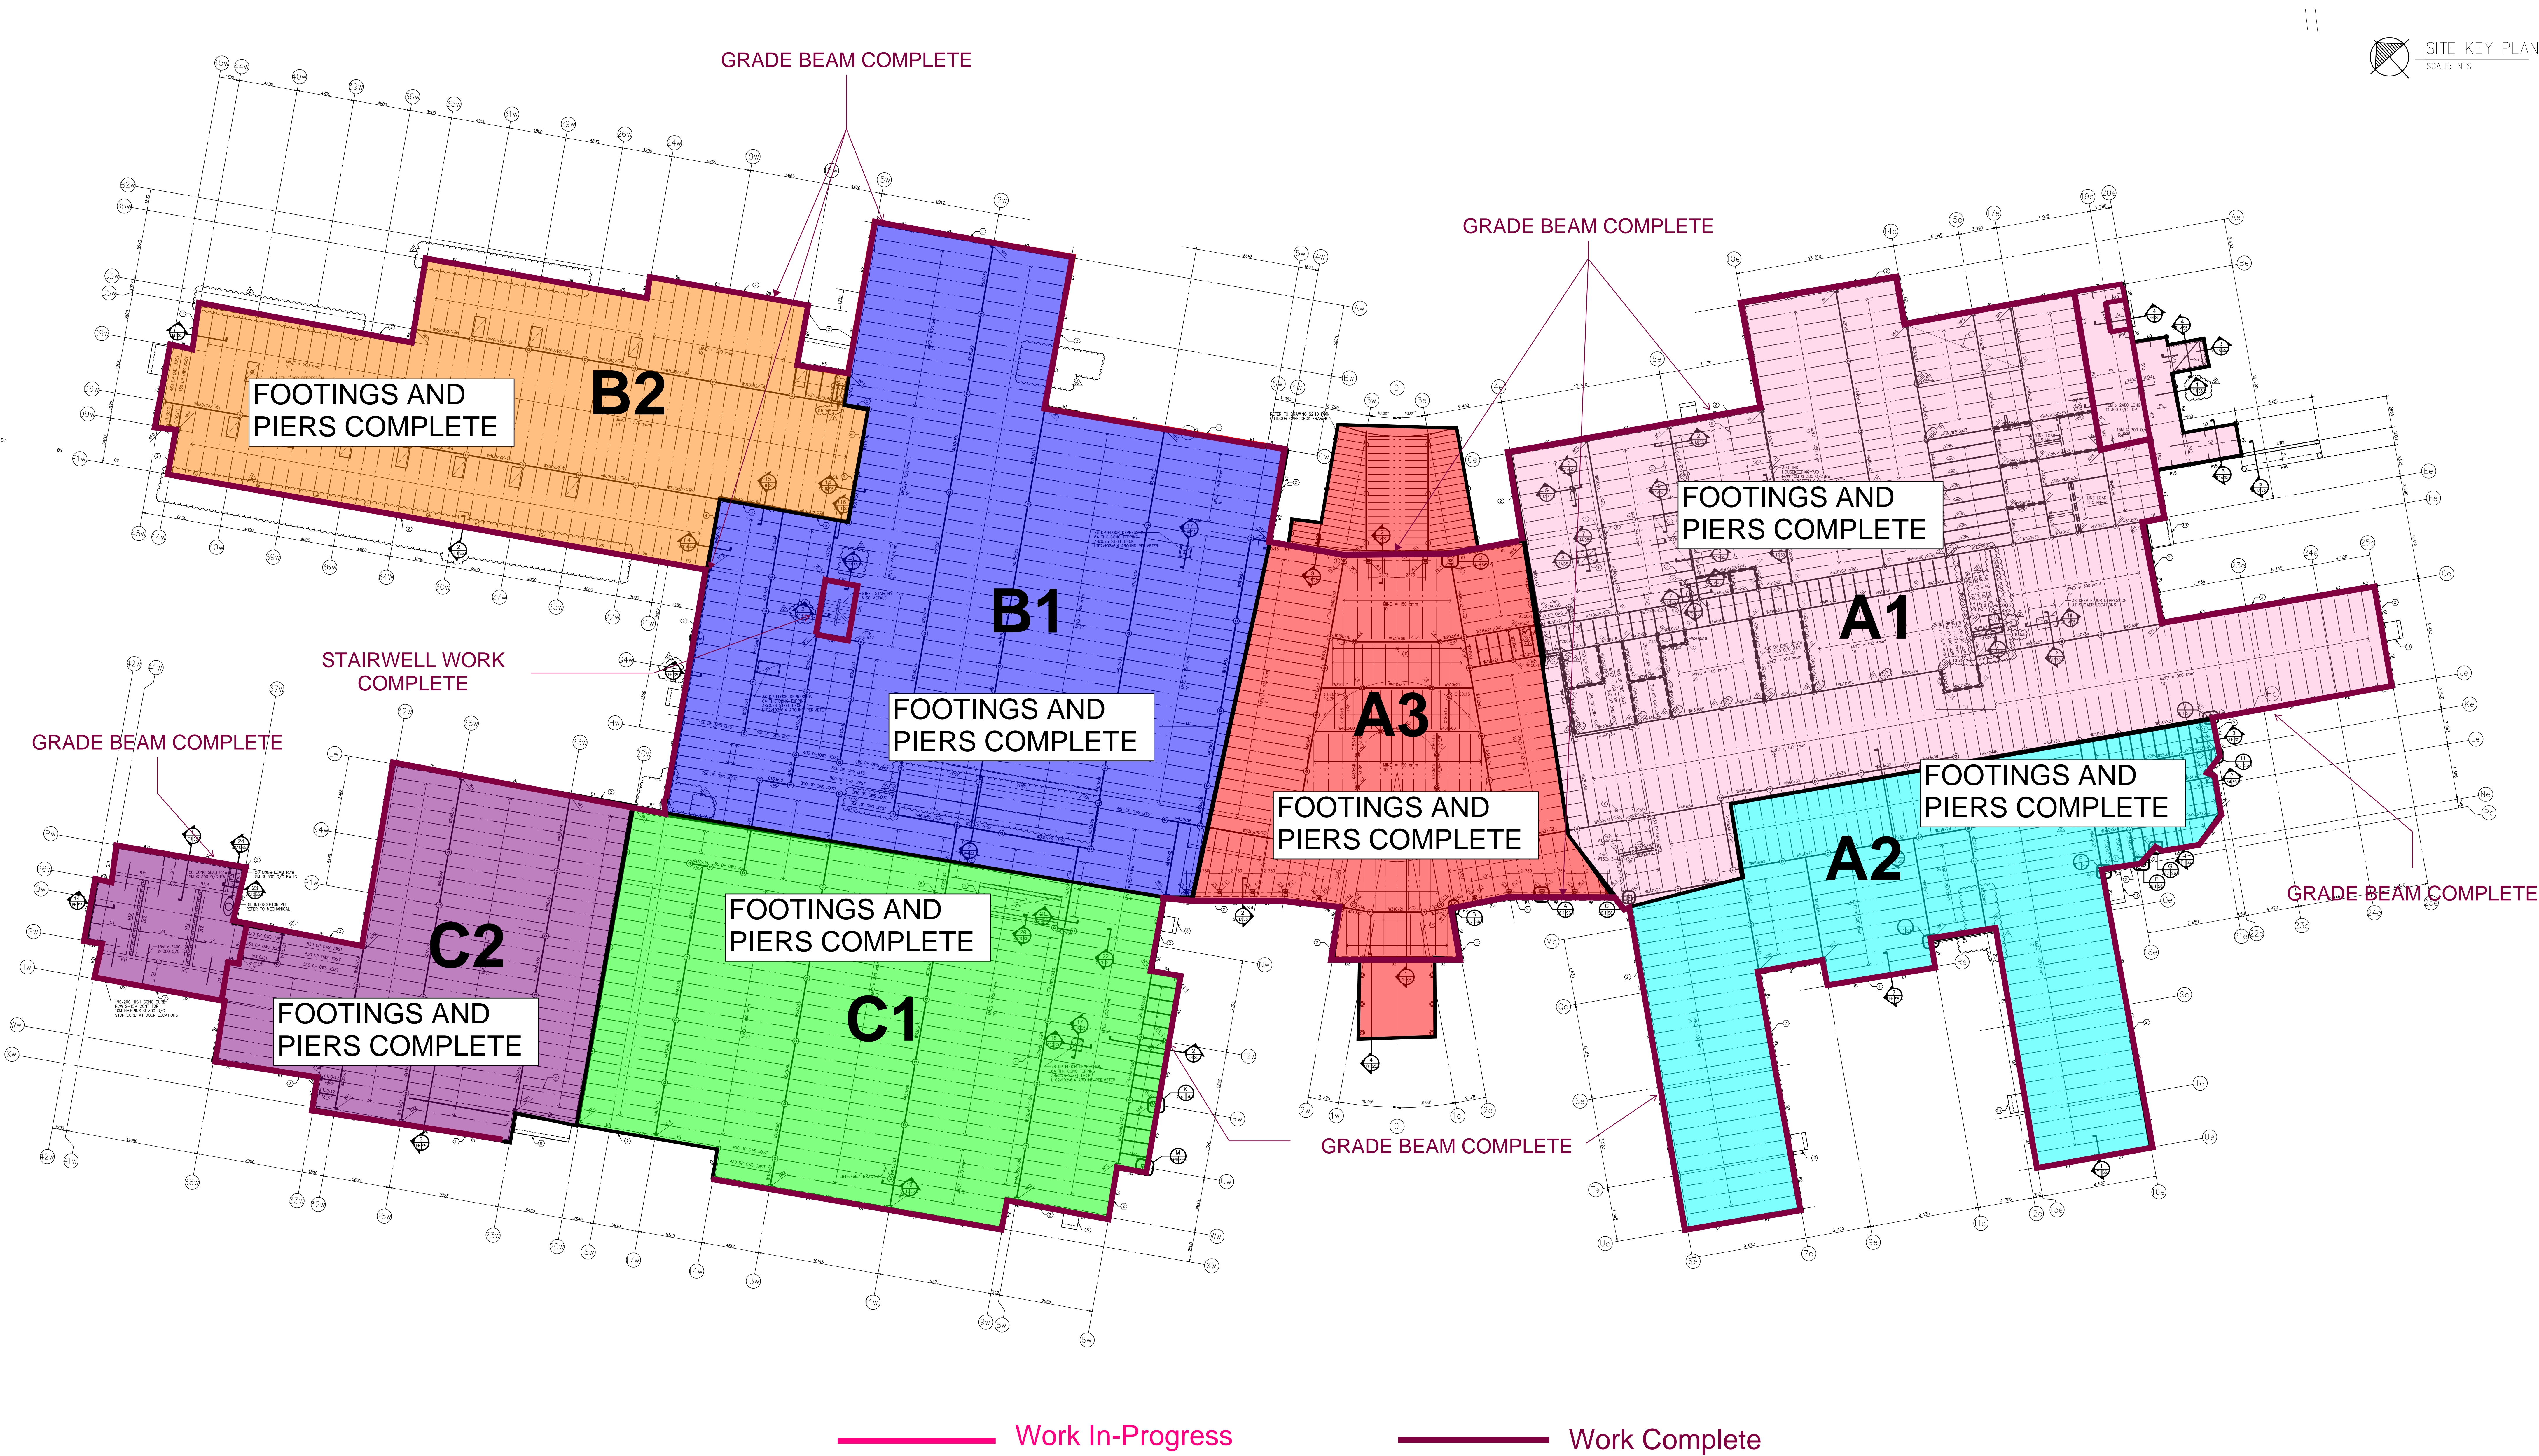


MASONRY ACTIVITY

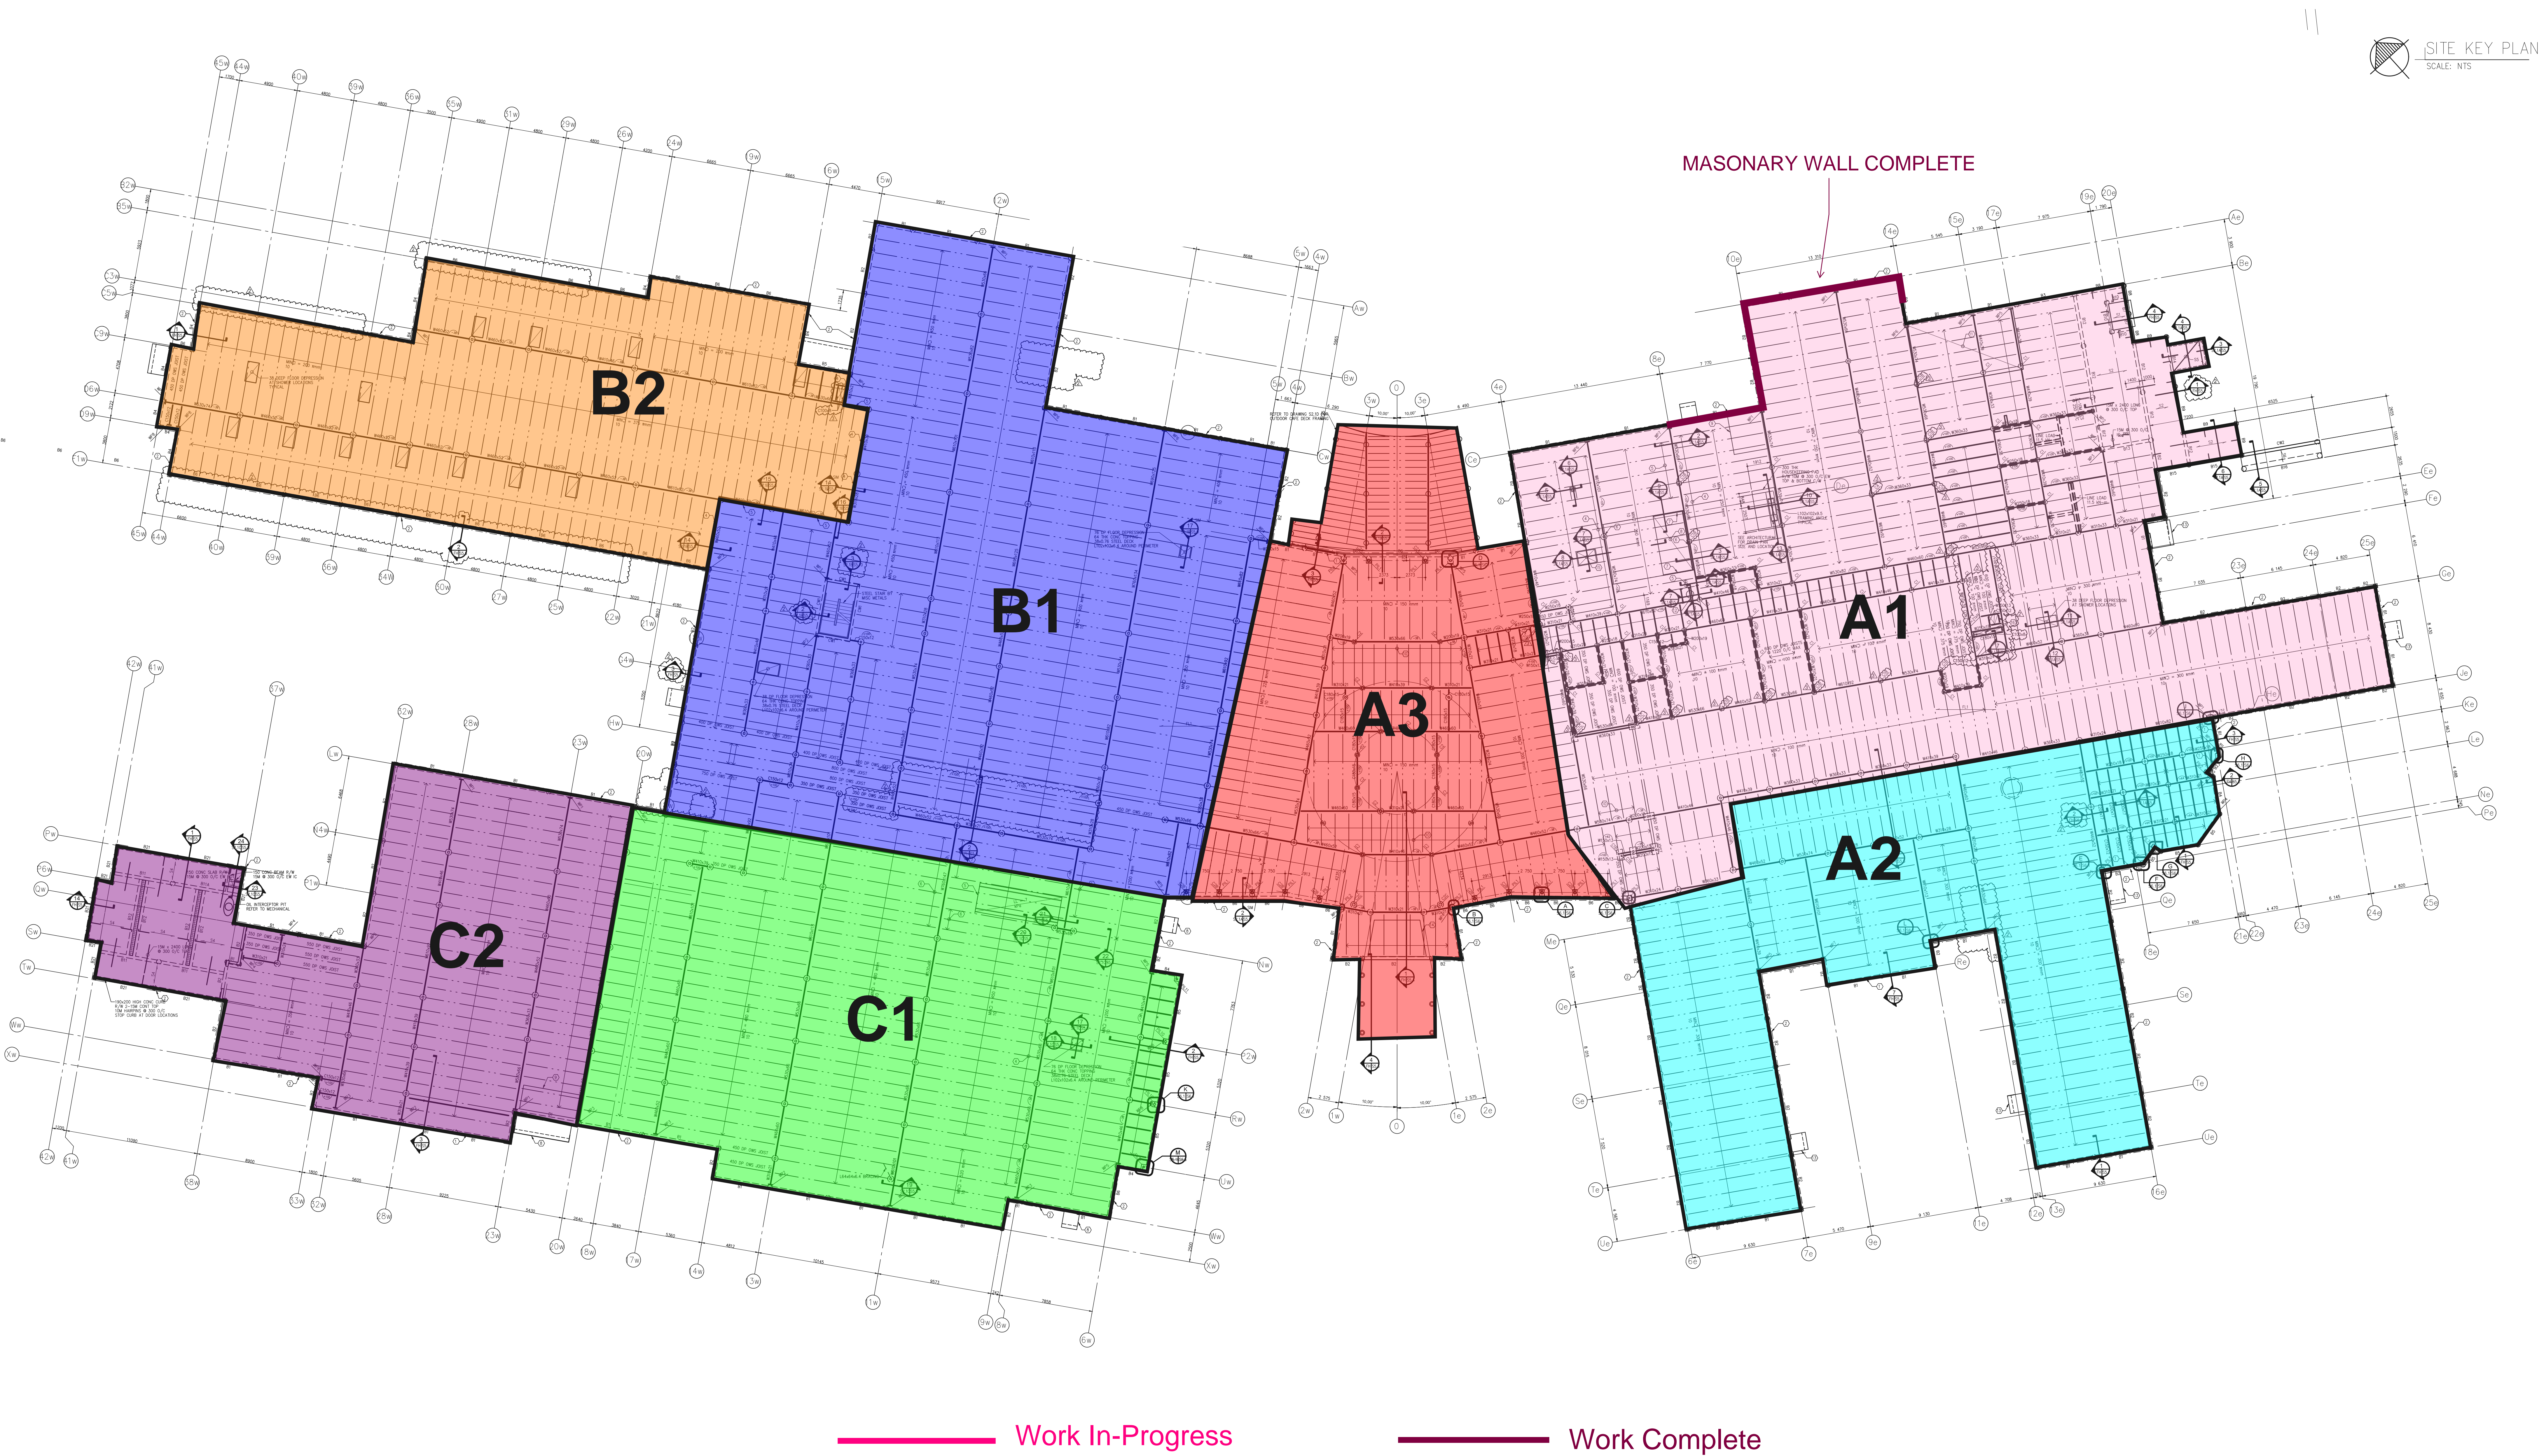

STRUCTURAL STEEL

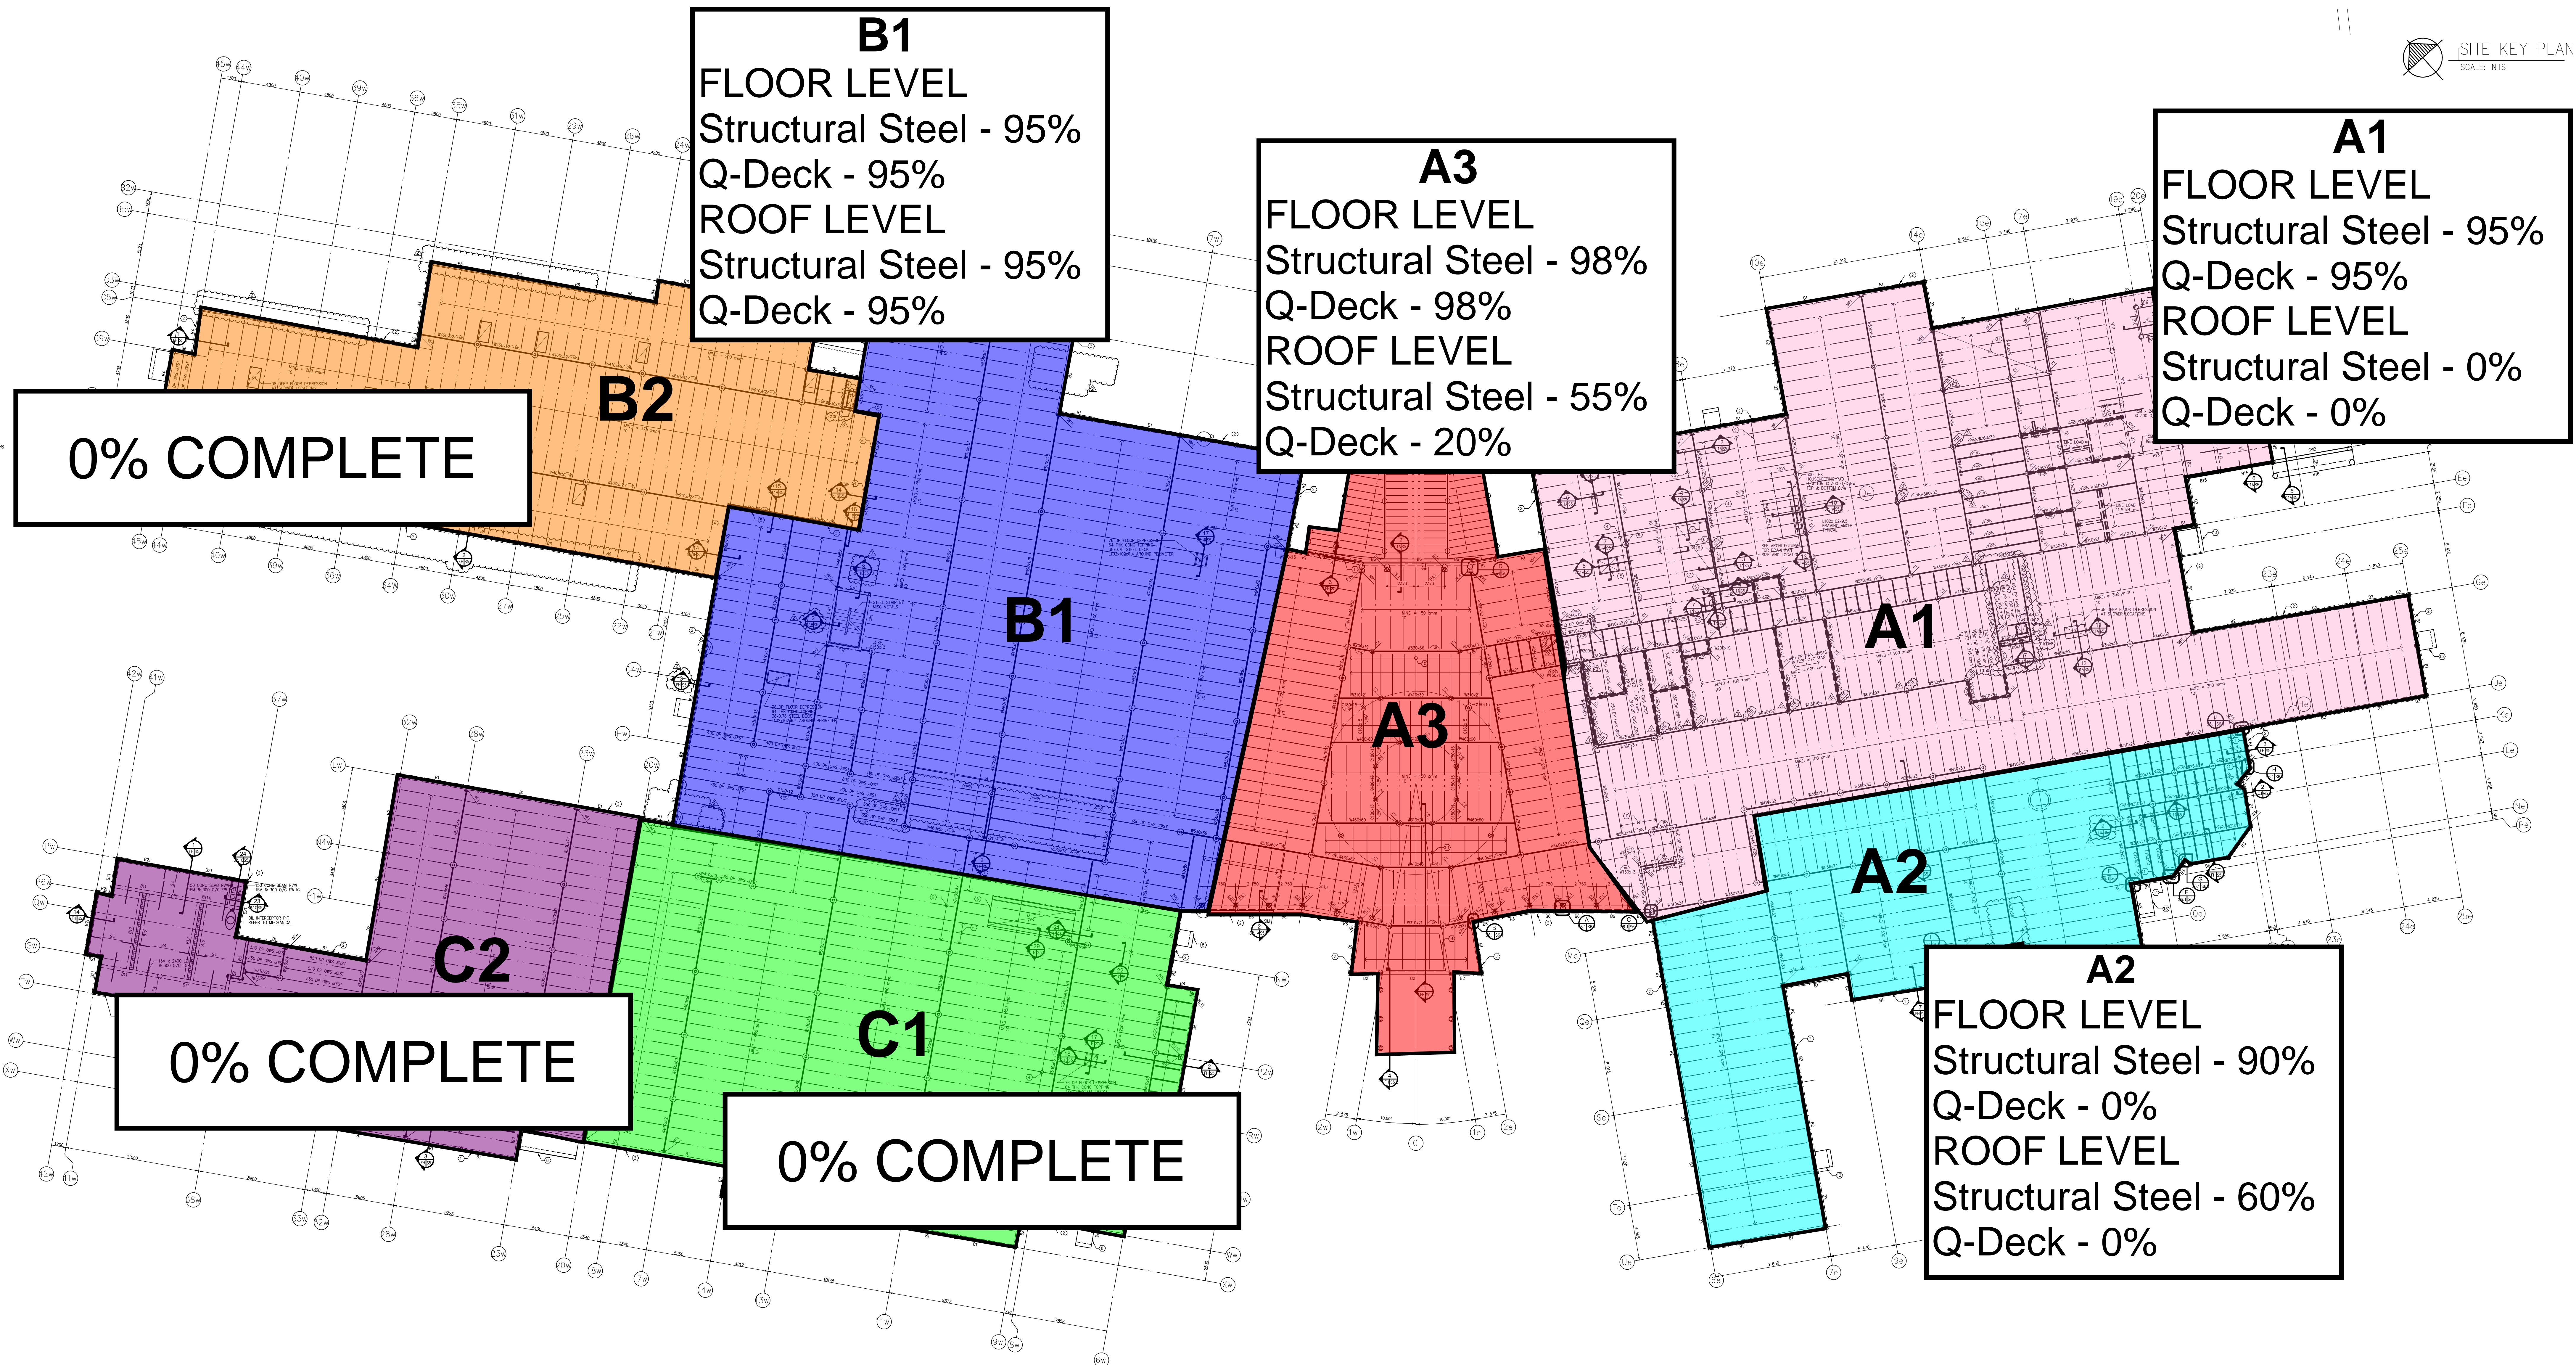

WEEPING TILE UPDATE

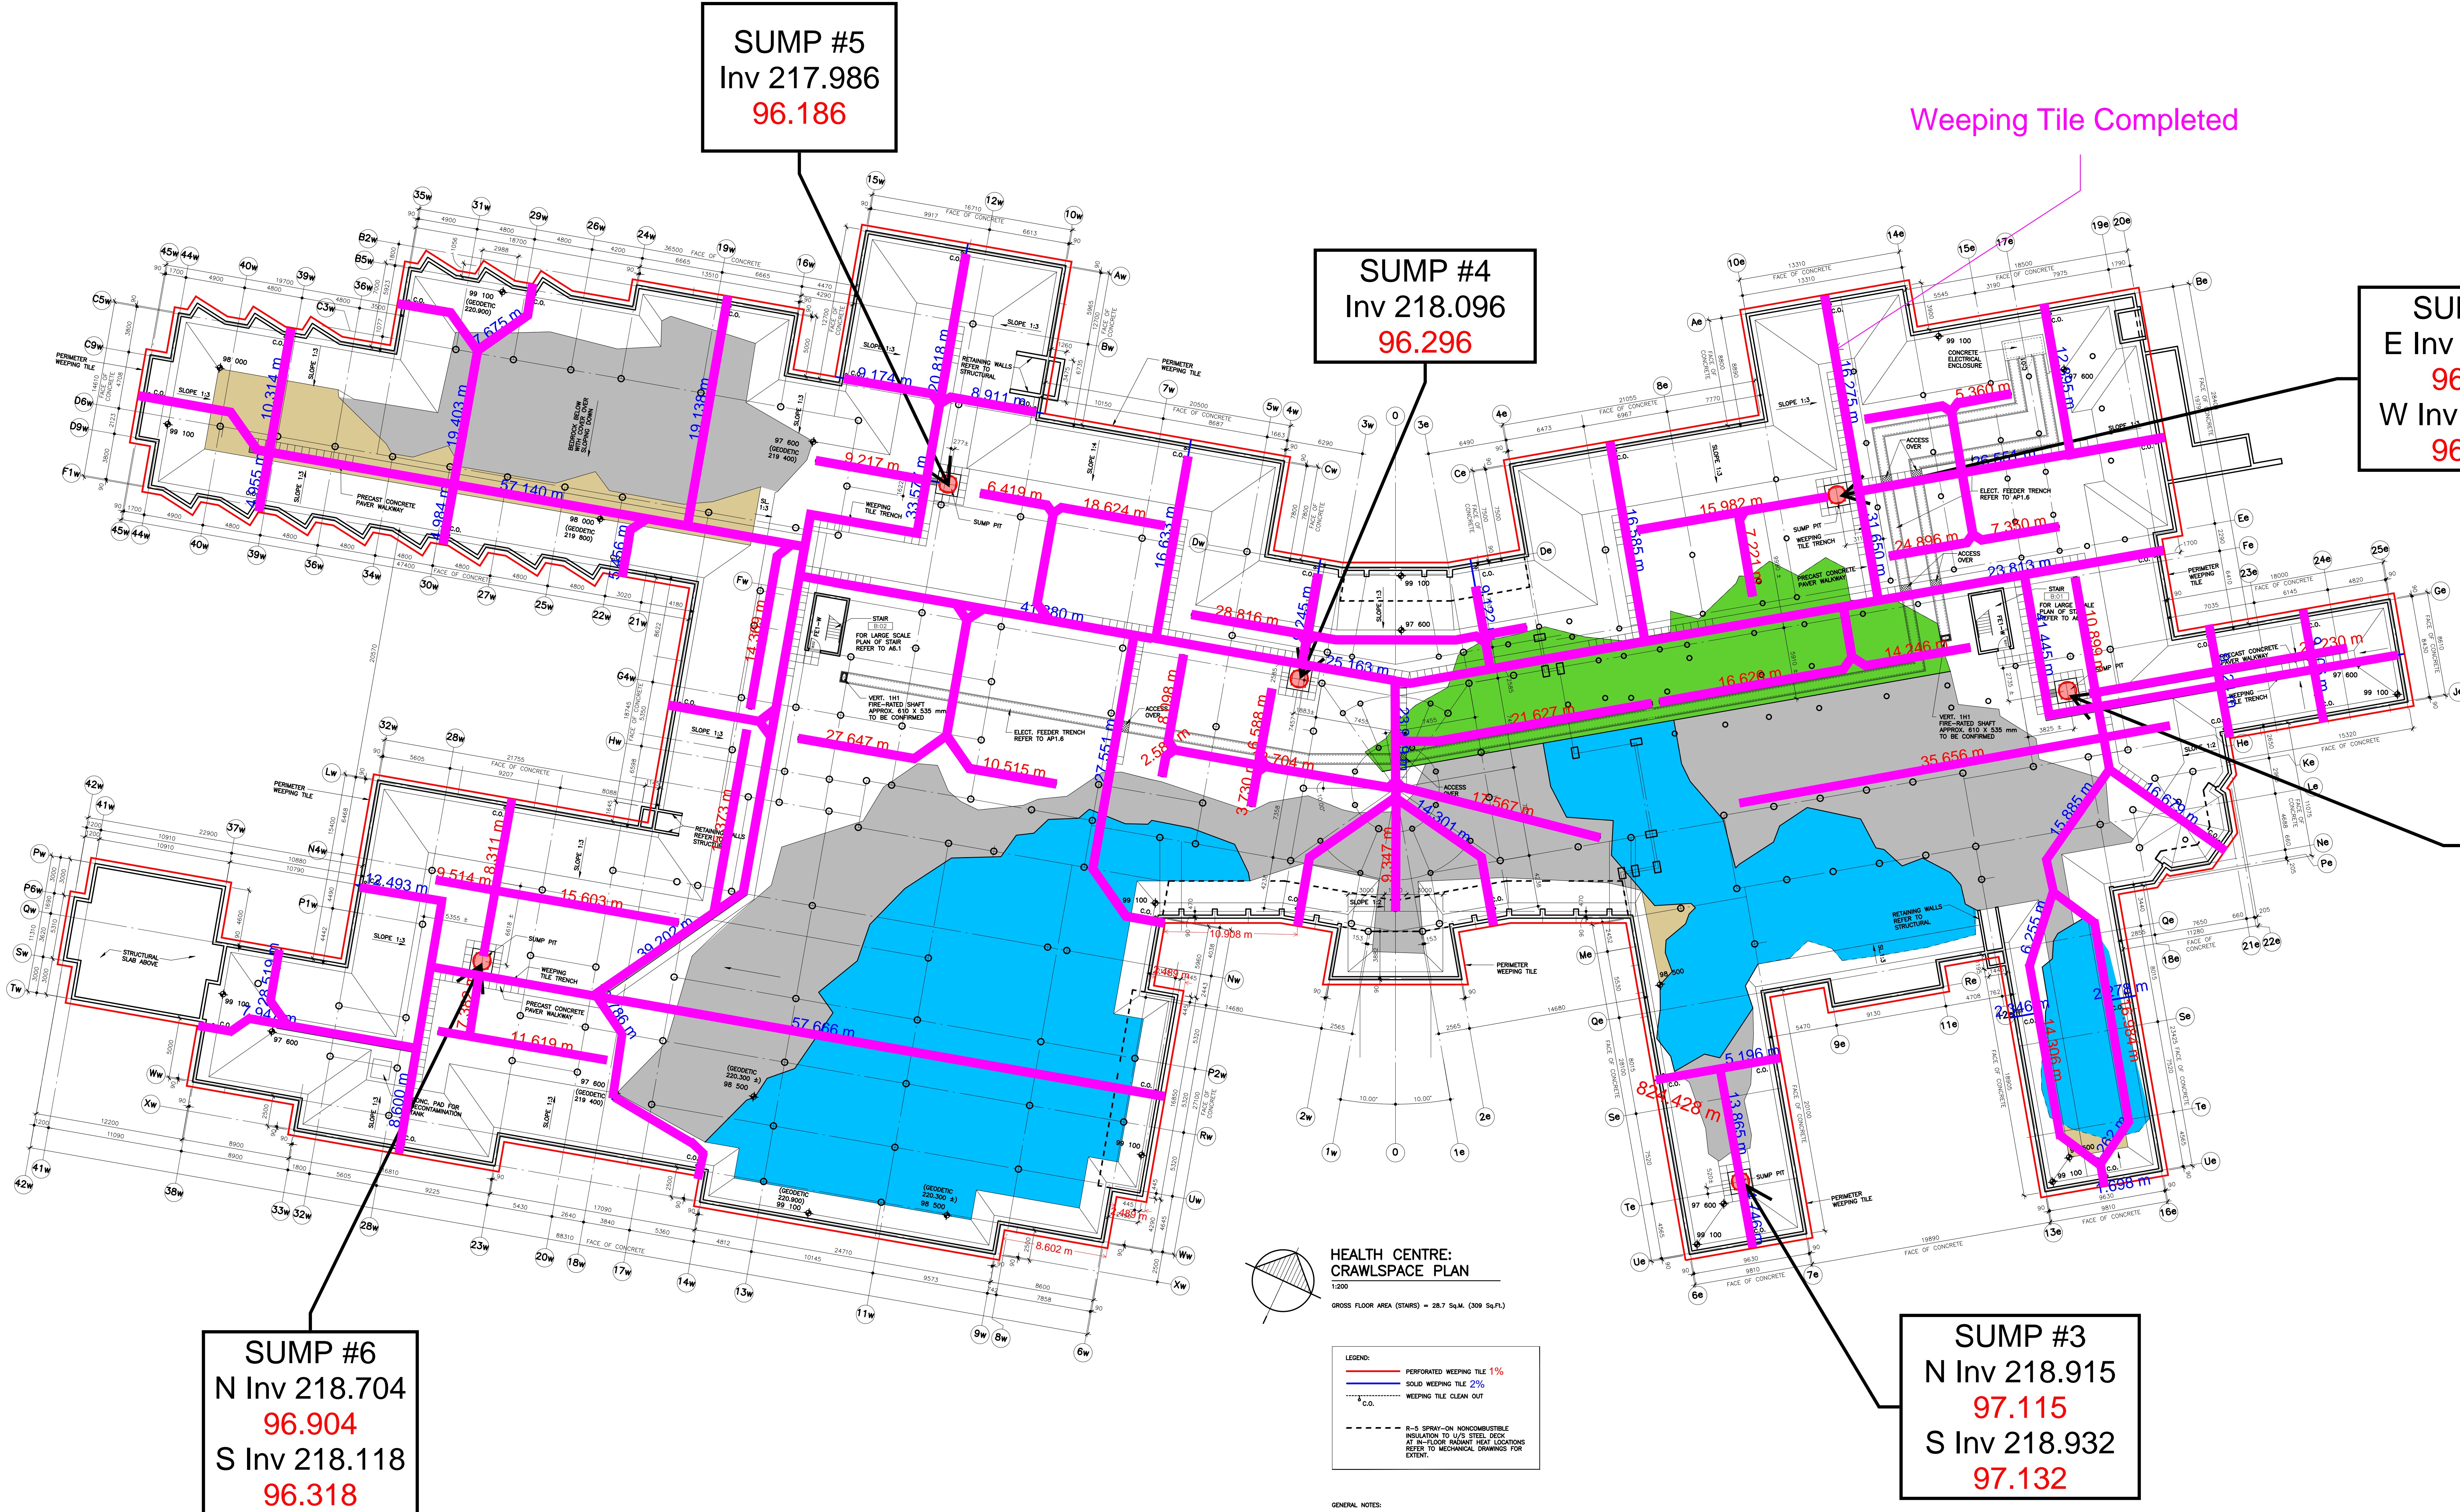

Work Completed
