

Weekly Report

Mar 30th -5th April

2021 Report # 35

# Norway House Cree Nation

Health Centre of Excellence



Project:

CD4 – Health Centre of Excellence

Aman Chana

JNR Construction

# Weekly Progress Report

Apr 6, 2021, ID #293

## REPORT DETAILS

Description

Created by Aman Chana

### 1. WORK LOG

Crew	# Workers	# Total hours	Work performed
JNR	39	2340	See below for discriptions
Totals	39	2340	

### 2. CREW ONSITE

2.1 The following crews were active in this report period



JNR



Mechanical



Electrical



Masonry



Structural Steel



Carlson (Steel Stud Trade) mobilized to site  
General site review & setting up C-can & office trailer

### 3. ARCHITECTURAL

3.1 Ongoing Work

N/A

3.2 Completed Work

N/A

### 4. STRUCTURAL

4.1 Ongoing Work

Buttoning up metal deck A2 roof level.  
Laying deck sheets in A2 roof level  
Welding and cutting in A2/A3  
Straightening and torqueing steel structure in A2, A3

4.2 Completed Work

Concrete  
General site clean up  
Fixing/repairing hoardings in B1-1 and GB (C2)  
Core drilling of concrete samples.  
Chipping/stripping concrete for GB to be removed (C2)  
Removing hoarding and formwork from structural slab.  
Hauling material away from grade beam that was removed

### 5. MECHANICAL

5.1 Ongoing Work

Producing required shop drawing submittals -Ongoing

5.2 Completed Work

Installing sanitary work packages in crawlspace B1  
Prepping for Hydronic installation in A3 crawlspace

### 6. ELECTRICAL

6.1 Ongoing Work

**Producing required shop drawing submittals -Ongoing**

6.2 Completed Work

**Working on temporary power hookup.  
Installing hangers in area A1, A2 & A3 crawlspace  
Setting up temporary power in crawl space.**

## 7. CIVIL

7.1 Ongoing Work

**Working on conduit spots on site roadways  
Hauling clay to stockpile  
Digging & dewatering the trench for waterline**

**Surveyor  
Crawlspace topographic survey A1  
B1-1 as built survey for floor elevations.  
Drafting & data management/reading specifications.**

7.2 Completed Work

## 8. SAFETY AND COVID-19 SCREENING

8.1 Number of Covid Screening reports completed

**JNR is continuing screening all visitors and staff daily who report to site.  
234 Covid screening reports completed on site last week.**

## 9. SITE VISIT SCHEDULE

9.1 Next scheduled site visit

**Next scheduled visit to site is to be determined**

## PHOTOS (35)



Working on GB C2

**Anmol Kang**

Apr 4, 2021 2:44 PM



Welding work in A2 roof level

**Anmol Kang**

Apr 4, 2021 2:44 PM



Laying sheets A2 roof level

**Anmol Kang**

Apr 4, 2021 2:44 PM



Laying deck sheets A2

**Anmol Kang**

Apr 4, 2021 2:44 PM



Installing hangers A1 crawlspace

**Anmol Kang**

Apr 4, 2021 2:44 PM



Structural slab

**Anmol Kang**


Apr 3, 2021 2:11 PM



Straightening & Torqueing Steel structure A2

**Anmol Kang**

Apr 3, 2021 2:11 PM

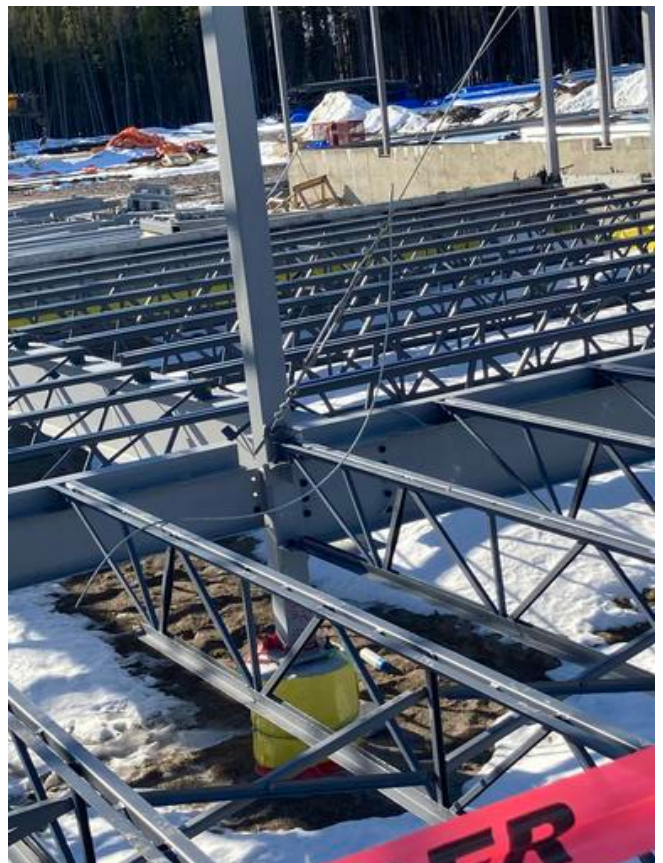

Straightening & Torqueing structure A2

**Anmol Kang**

Apr 3, 2021 2:11 PM



Setting up new control points

**Anmol Kang**

Apr 3, 2021 2:11 PM



Masonry A1

**Anmol Kang**

Apr 3, 2021 2:11 PM



Laying deck sheets A2 roof level

**Anmol Kang**

Apr 3, 2021 2:11 PM



Formwork removal C2 grade beam

**Anmol Kang**

Apr 3, 2021 2:11 PM



B1 crawl space work in progress

**Anmol Kang**

Apr 3, 2021 2:11 PM



A2 cross bracing work in progress

**Anmol Kang**

Apr 3, 2021 2:11 PM



Mesh over deck B1-2

**Anmol Kang**

Apr 1, 2021 2:57 PM



Hoardings over penthouse & B1

**Anmol Kang**

Apr 1, 2021 2:57 PM



Glulam installed A3  
**Anmol Kang**  
Apr 1, 2021 2:57 PM



Fixing hoarding B1-2  
**Anmol Kang**  
Apr 1, 2021 2:57 PM



Chipping GB (C1)  
**Anmol Kang**  
Apr 1, 2021 2:57 PM



Carlson office trailer setup on site  
**Anmol Kang**  
Apr 1, 2021 2:57 PM



A2 steel structure work in progress roof level

**Anmol Kang**

Mar 31, 2021 4:18 PM



B1-2 mesh on Q deck

**Anmol Kang**

Mar 31, 2021 4:18 PM



Straightening and Torqueing in A2

**Anmol Kang**

Mar 31, 2021 4:14 PM



Steel structure A2

**Anmol Kang**

Mar 31, 2021 4:14 PM



Straightening and torquing in A2

**Anmol Kang**

Mar 31, 2021 4:13 PM



Snow removal from site

**Anmol Kang**

Mar 31, 2021 4:13 PM



Fixing hoardings in B1-1  
**Anmol Kang**  
Mar 30, 2021 3:15 PM



Topo survey in A1 & 2 crawl space  
**Anmol Kang**  
Mar 30, 2021 3:14 PM



Heating and hoarding over GB C2  
**Anmol Kang**  
Mar 30, 2021 3:11 PM



A2 steel structure work in progress  
**Anmol Kang**  
Mar 30, 2021 3:11 PM



Steel structure A2  
**Anmol Kang**  
Mar 30, 2021 3:11 PM



Snow removal  
**Anmol Kang**  
Mar 30, 2021 3:09 PM



A3 crawlspace  
**Anmol Kang**  
Mar 30, 2021 3:08 PM




Masonry work A1  
**Anmol Kang**  
Mar 30, 2021 3:07 PM




Heating and hoarding in B1

**Anmol Kang**


Mar 30, 2021 3:06 PM

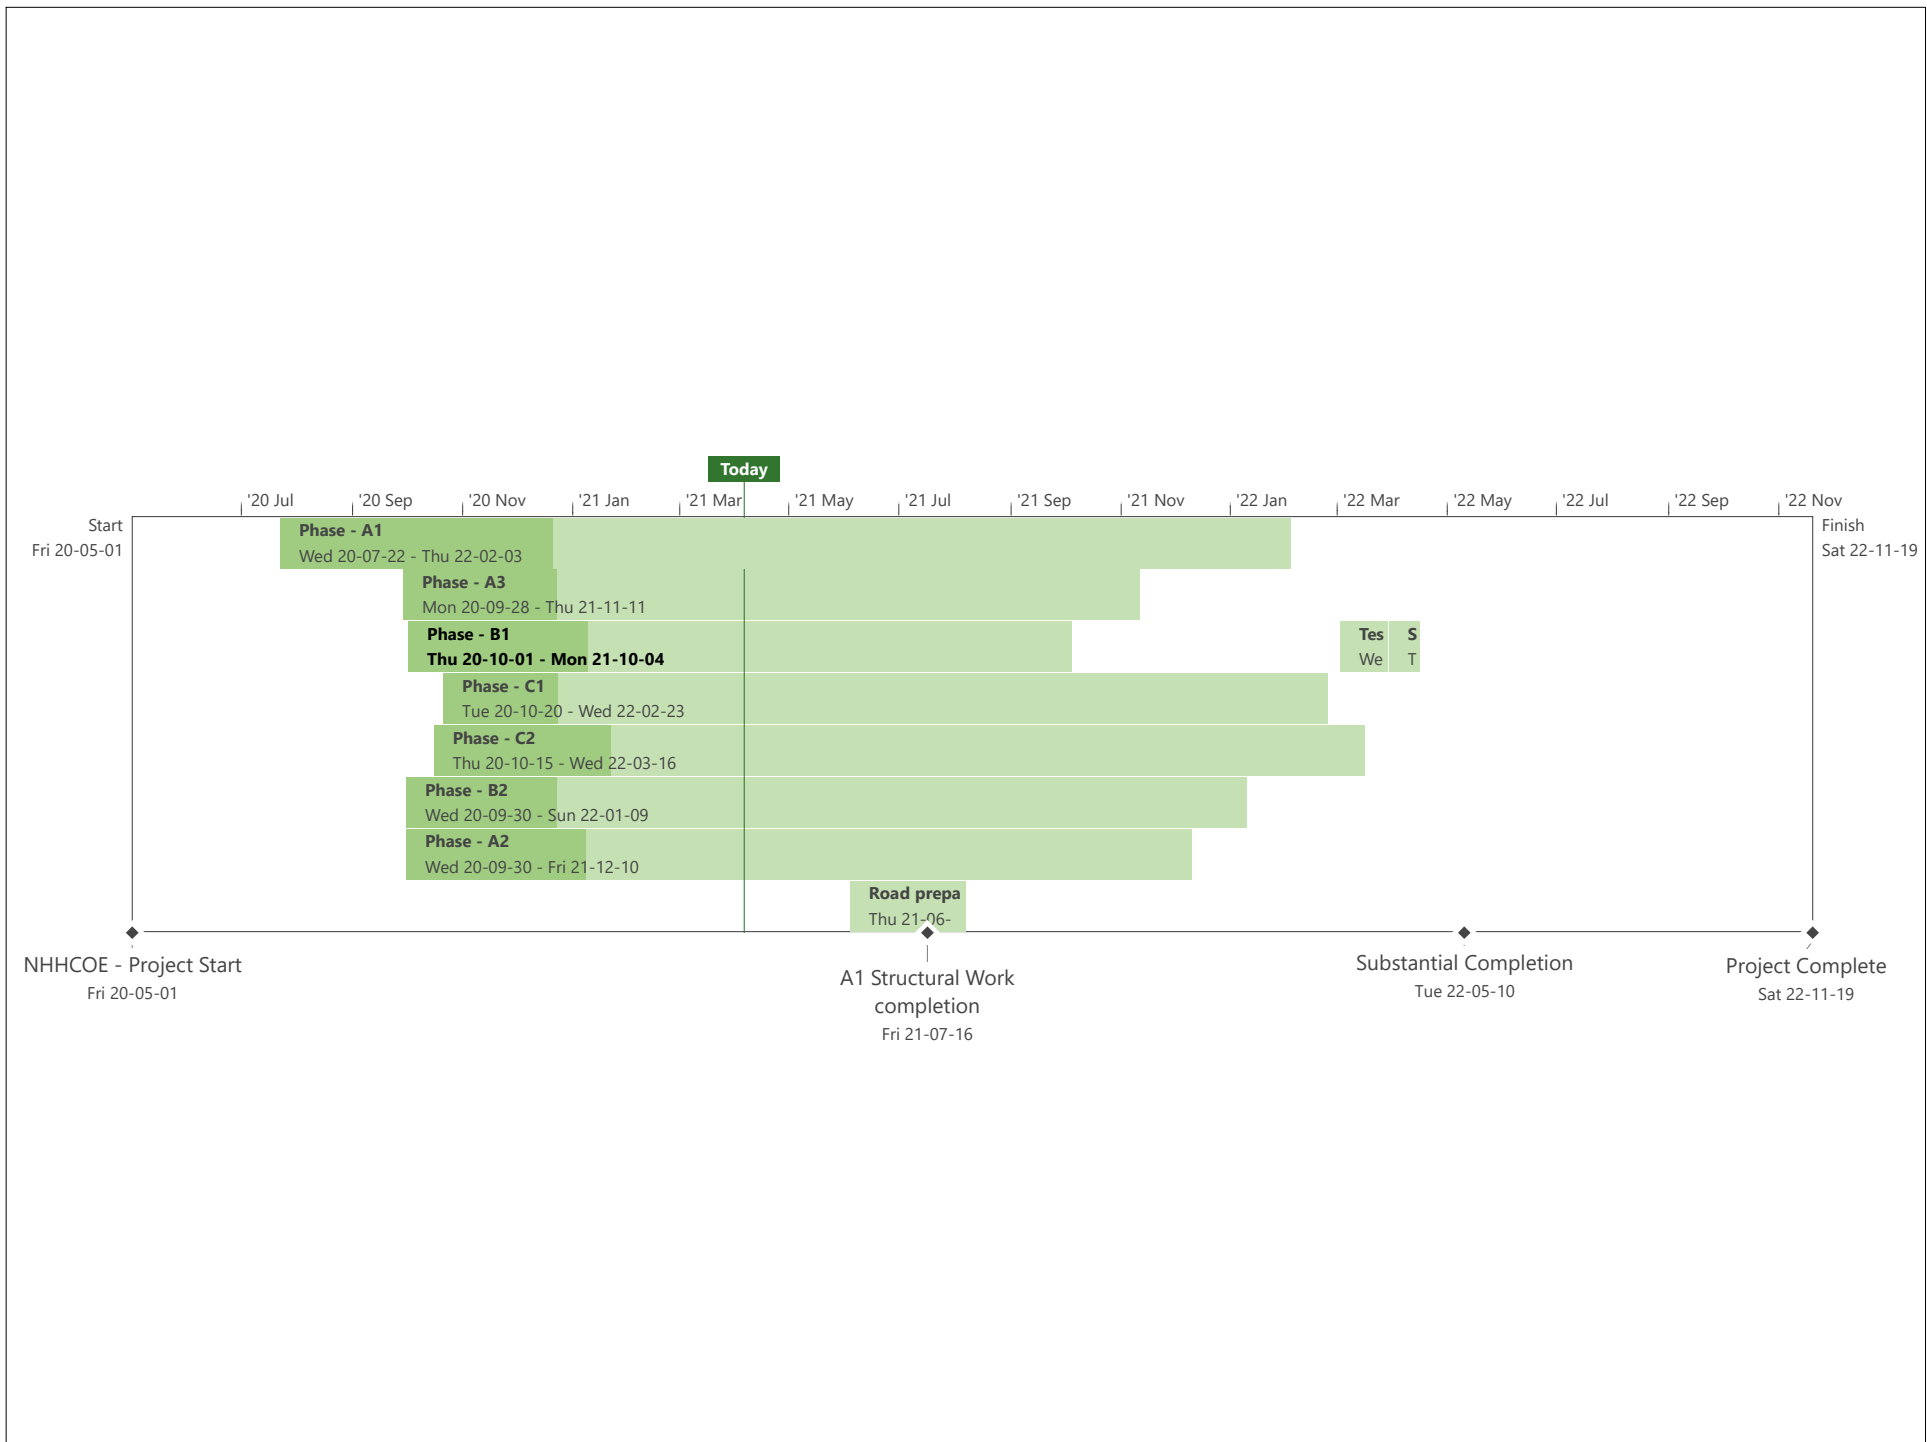

BACKFILL ACTIVITY

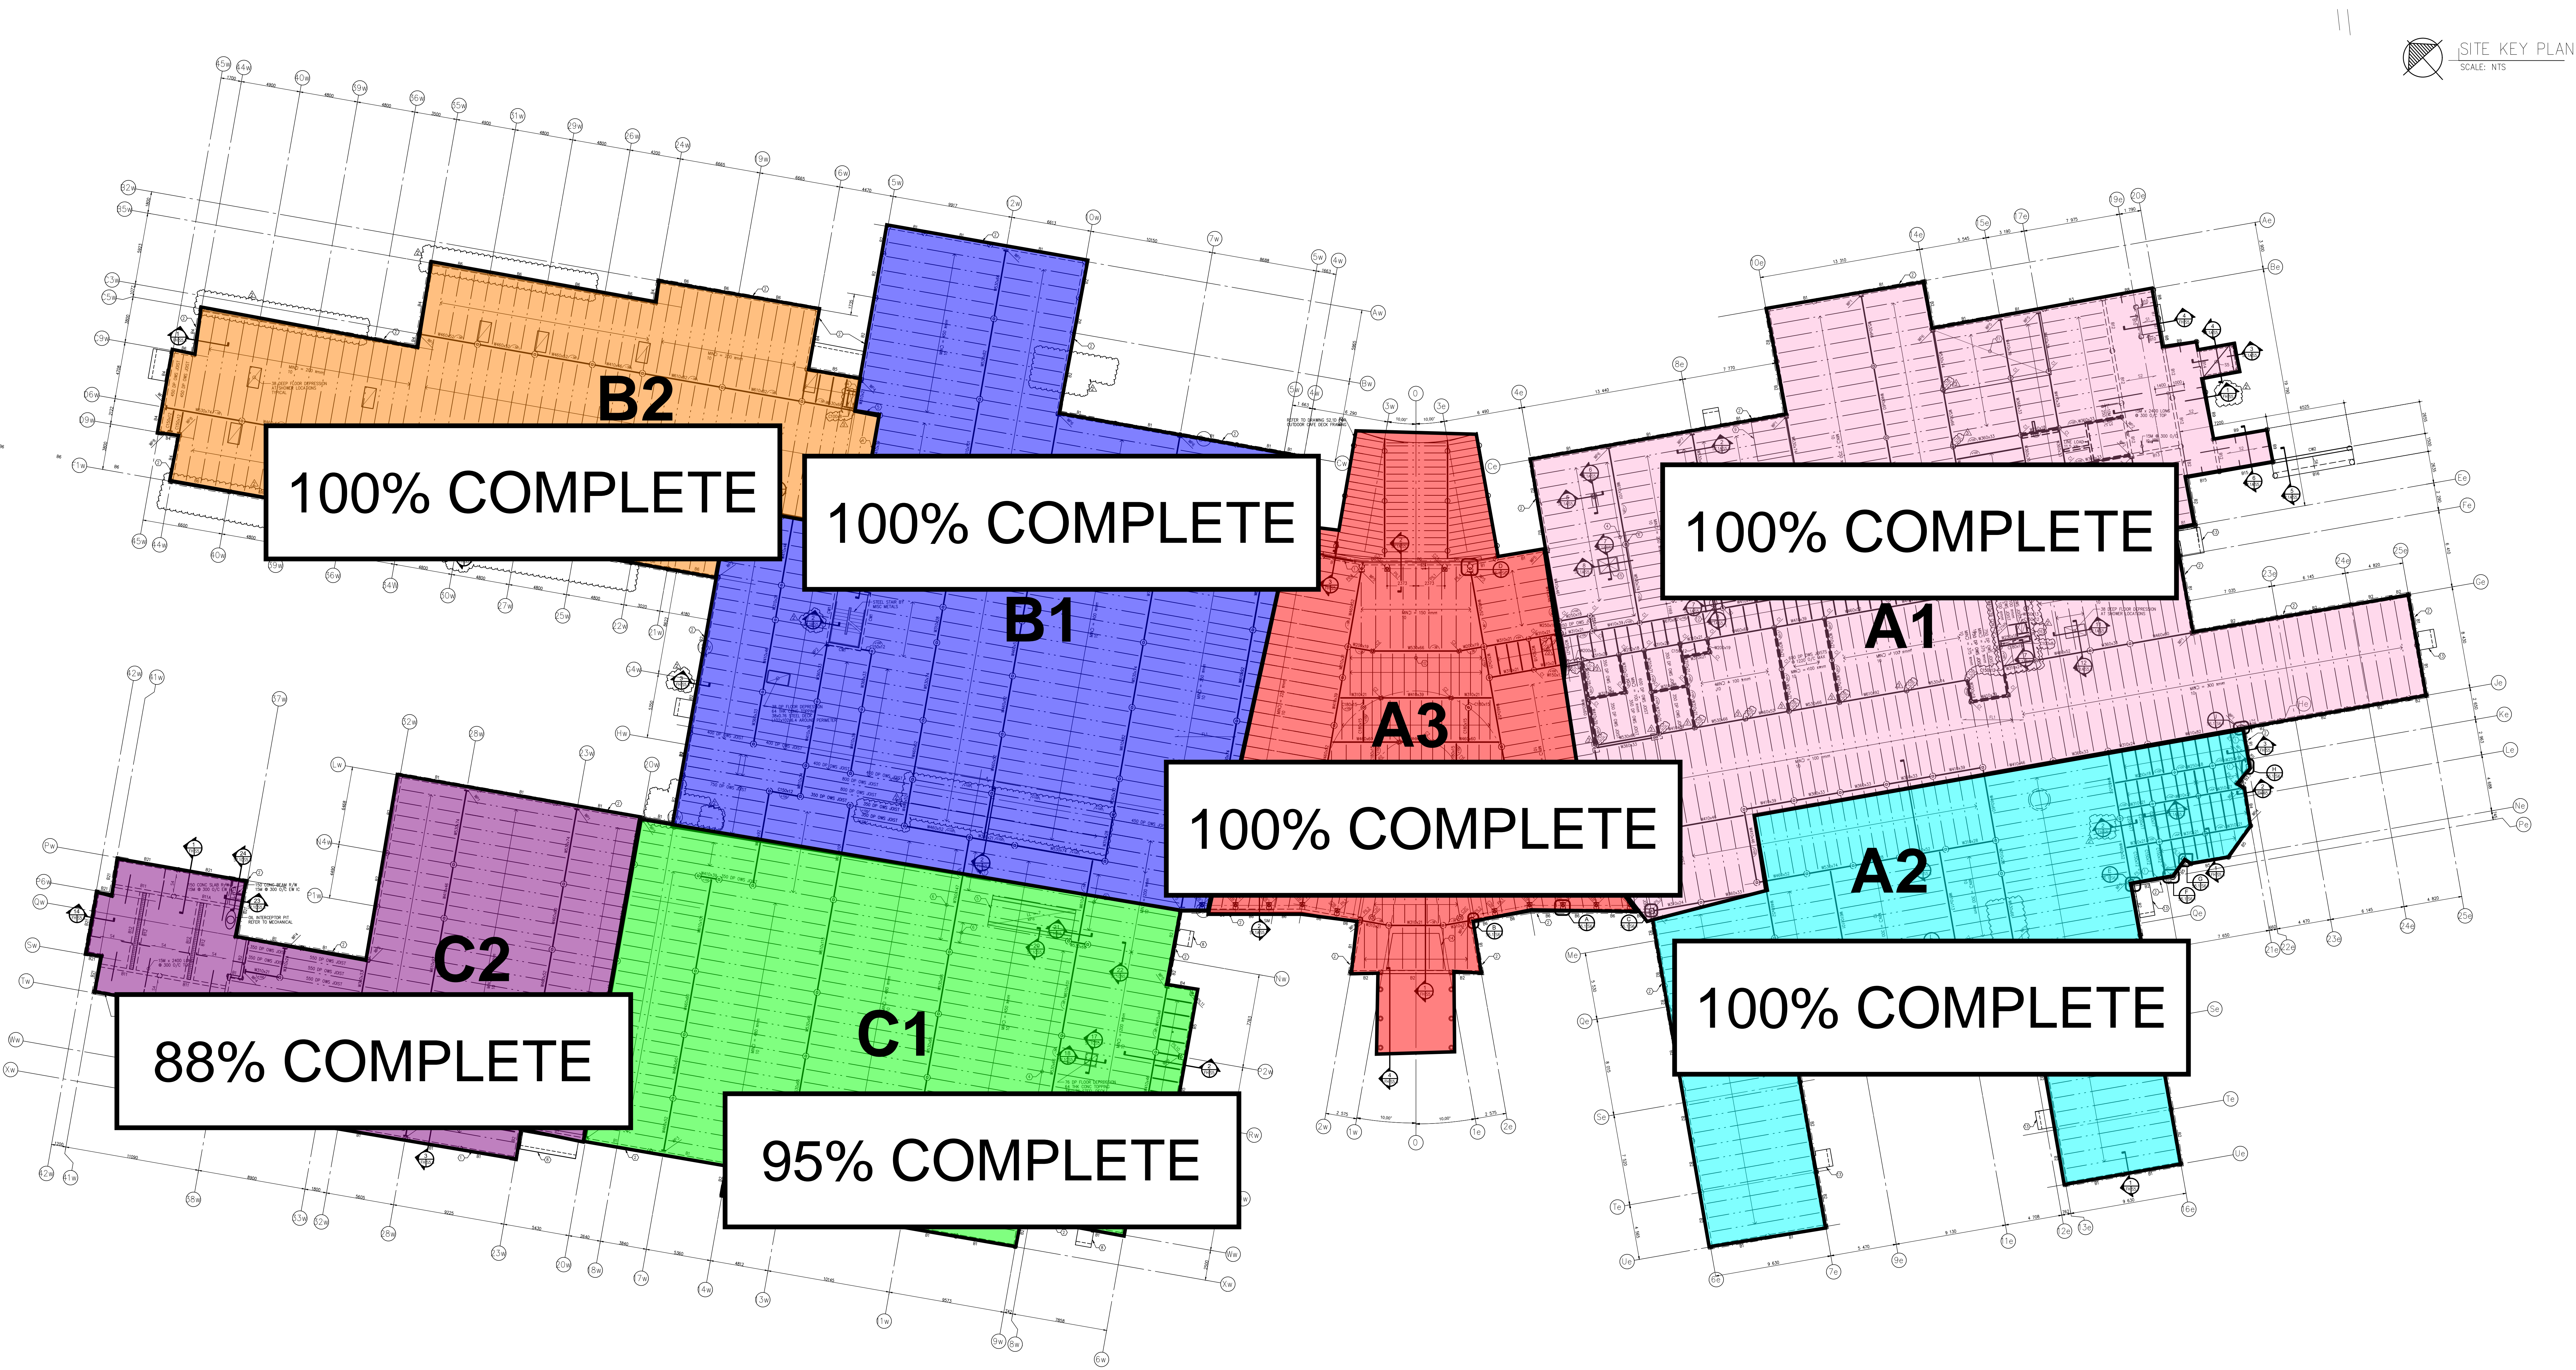

CONCRETE SLAB ACTIVITY

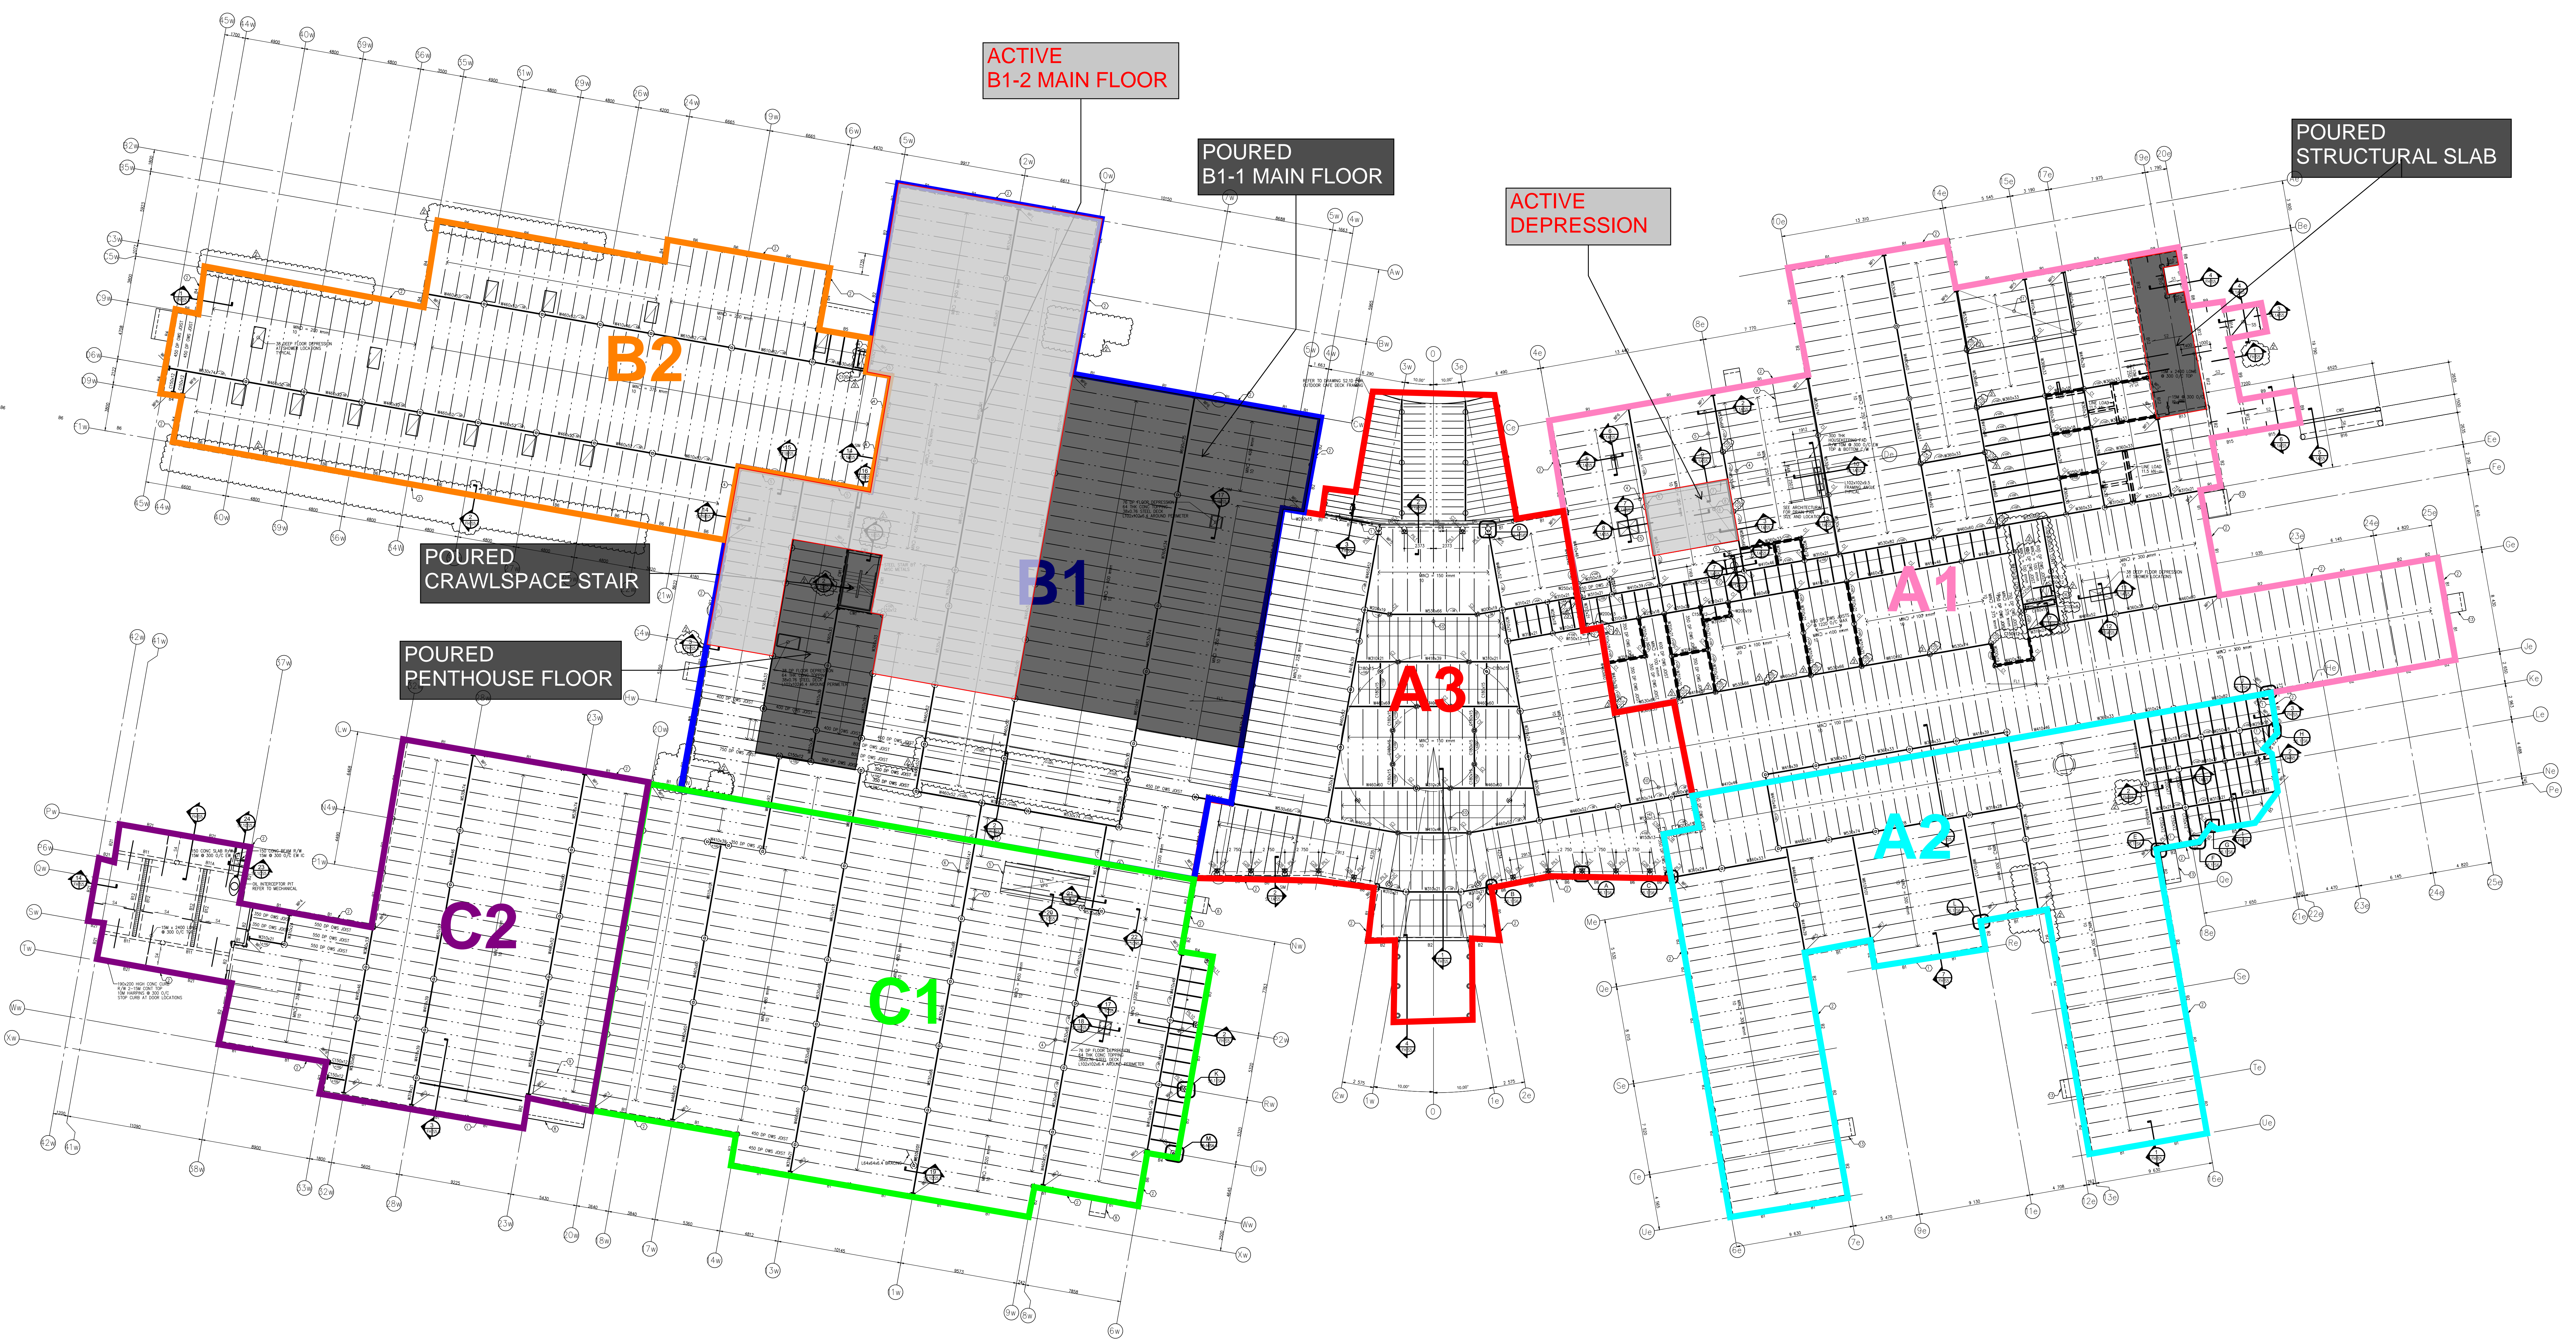


SLAB POURED




SLAB IN-PROCESS


FOOTING, PIER & GRADE BEAM ACTIVITY

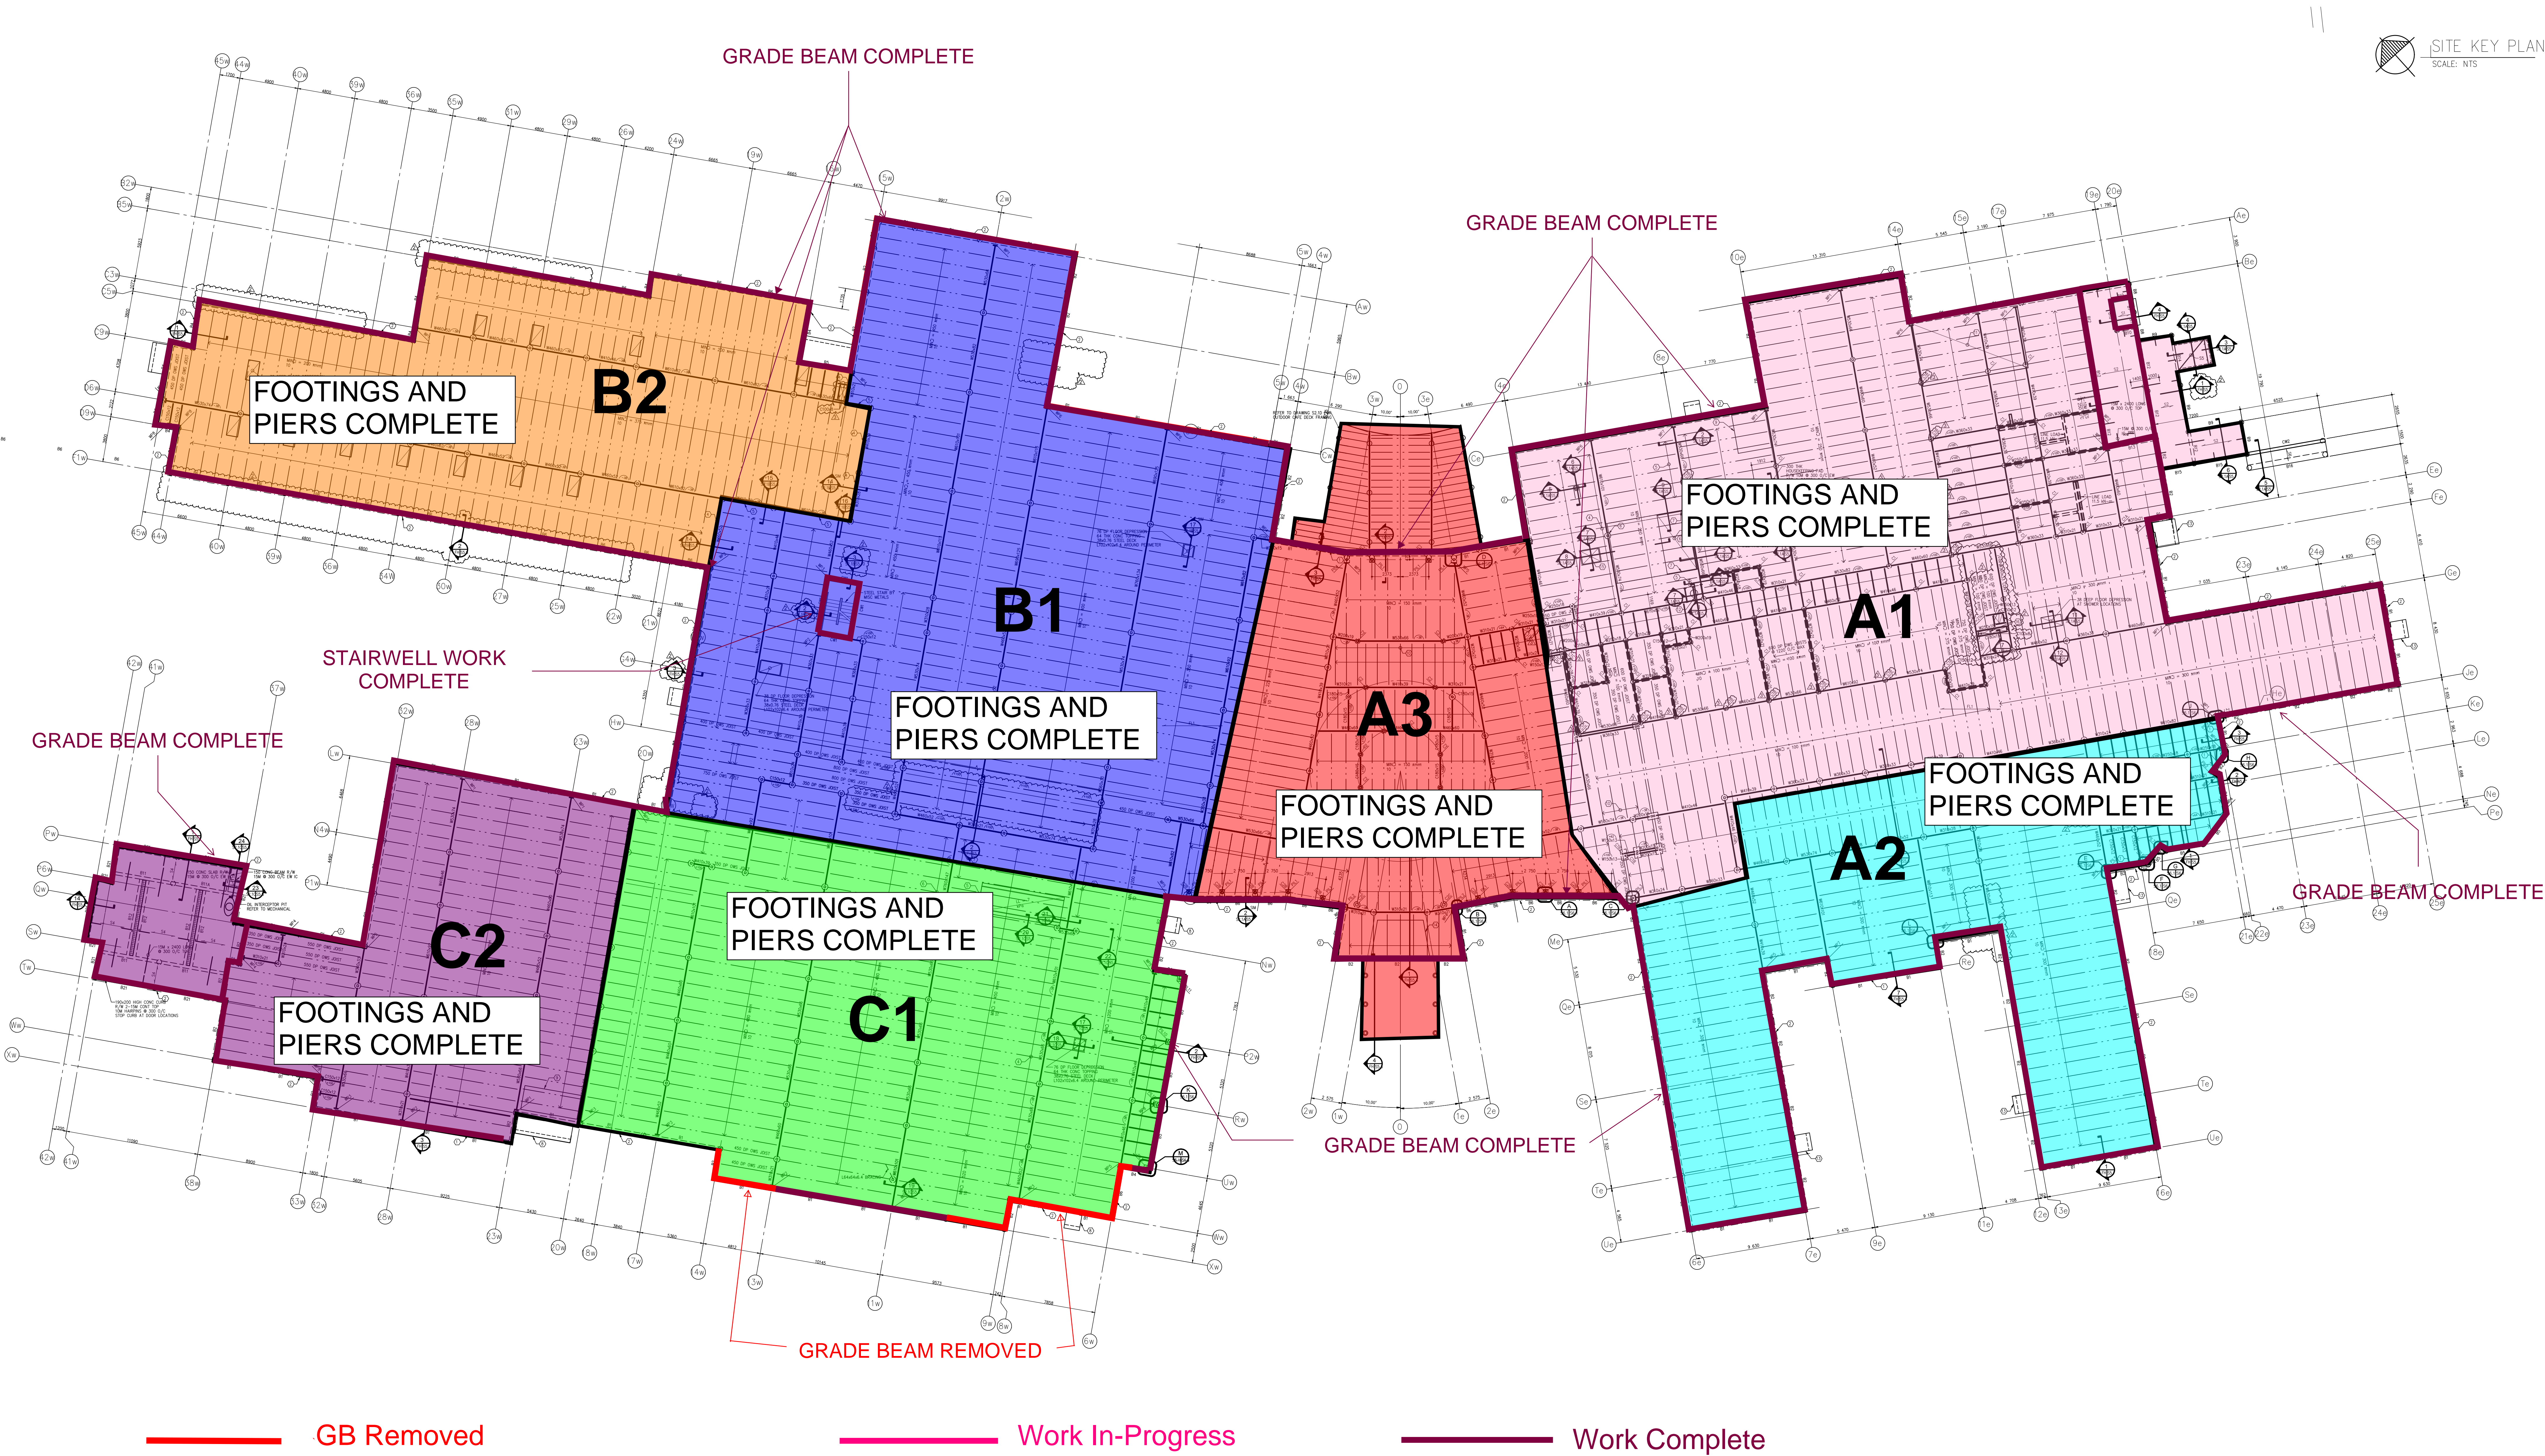

MASONRY ACTIVITY

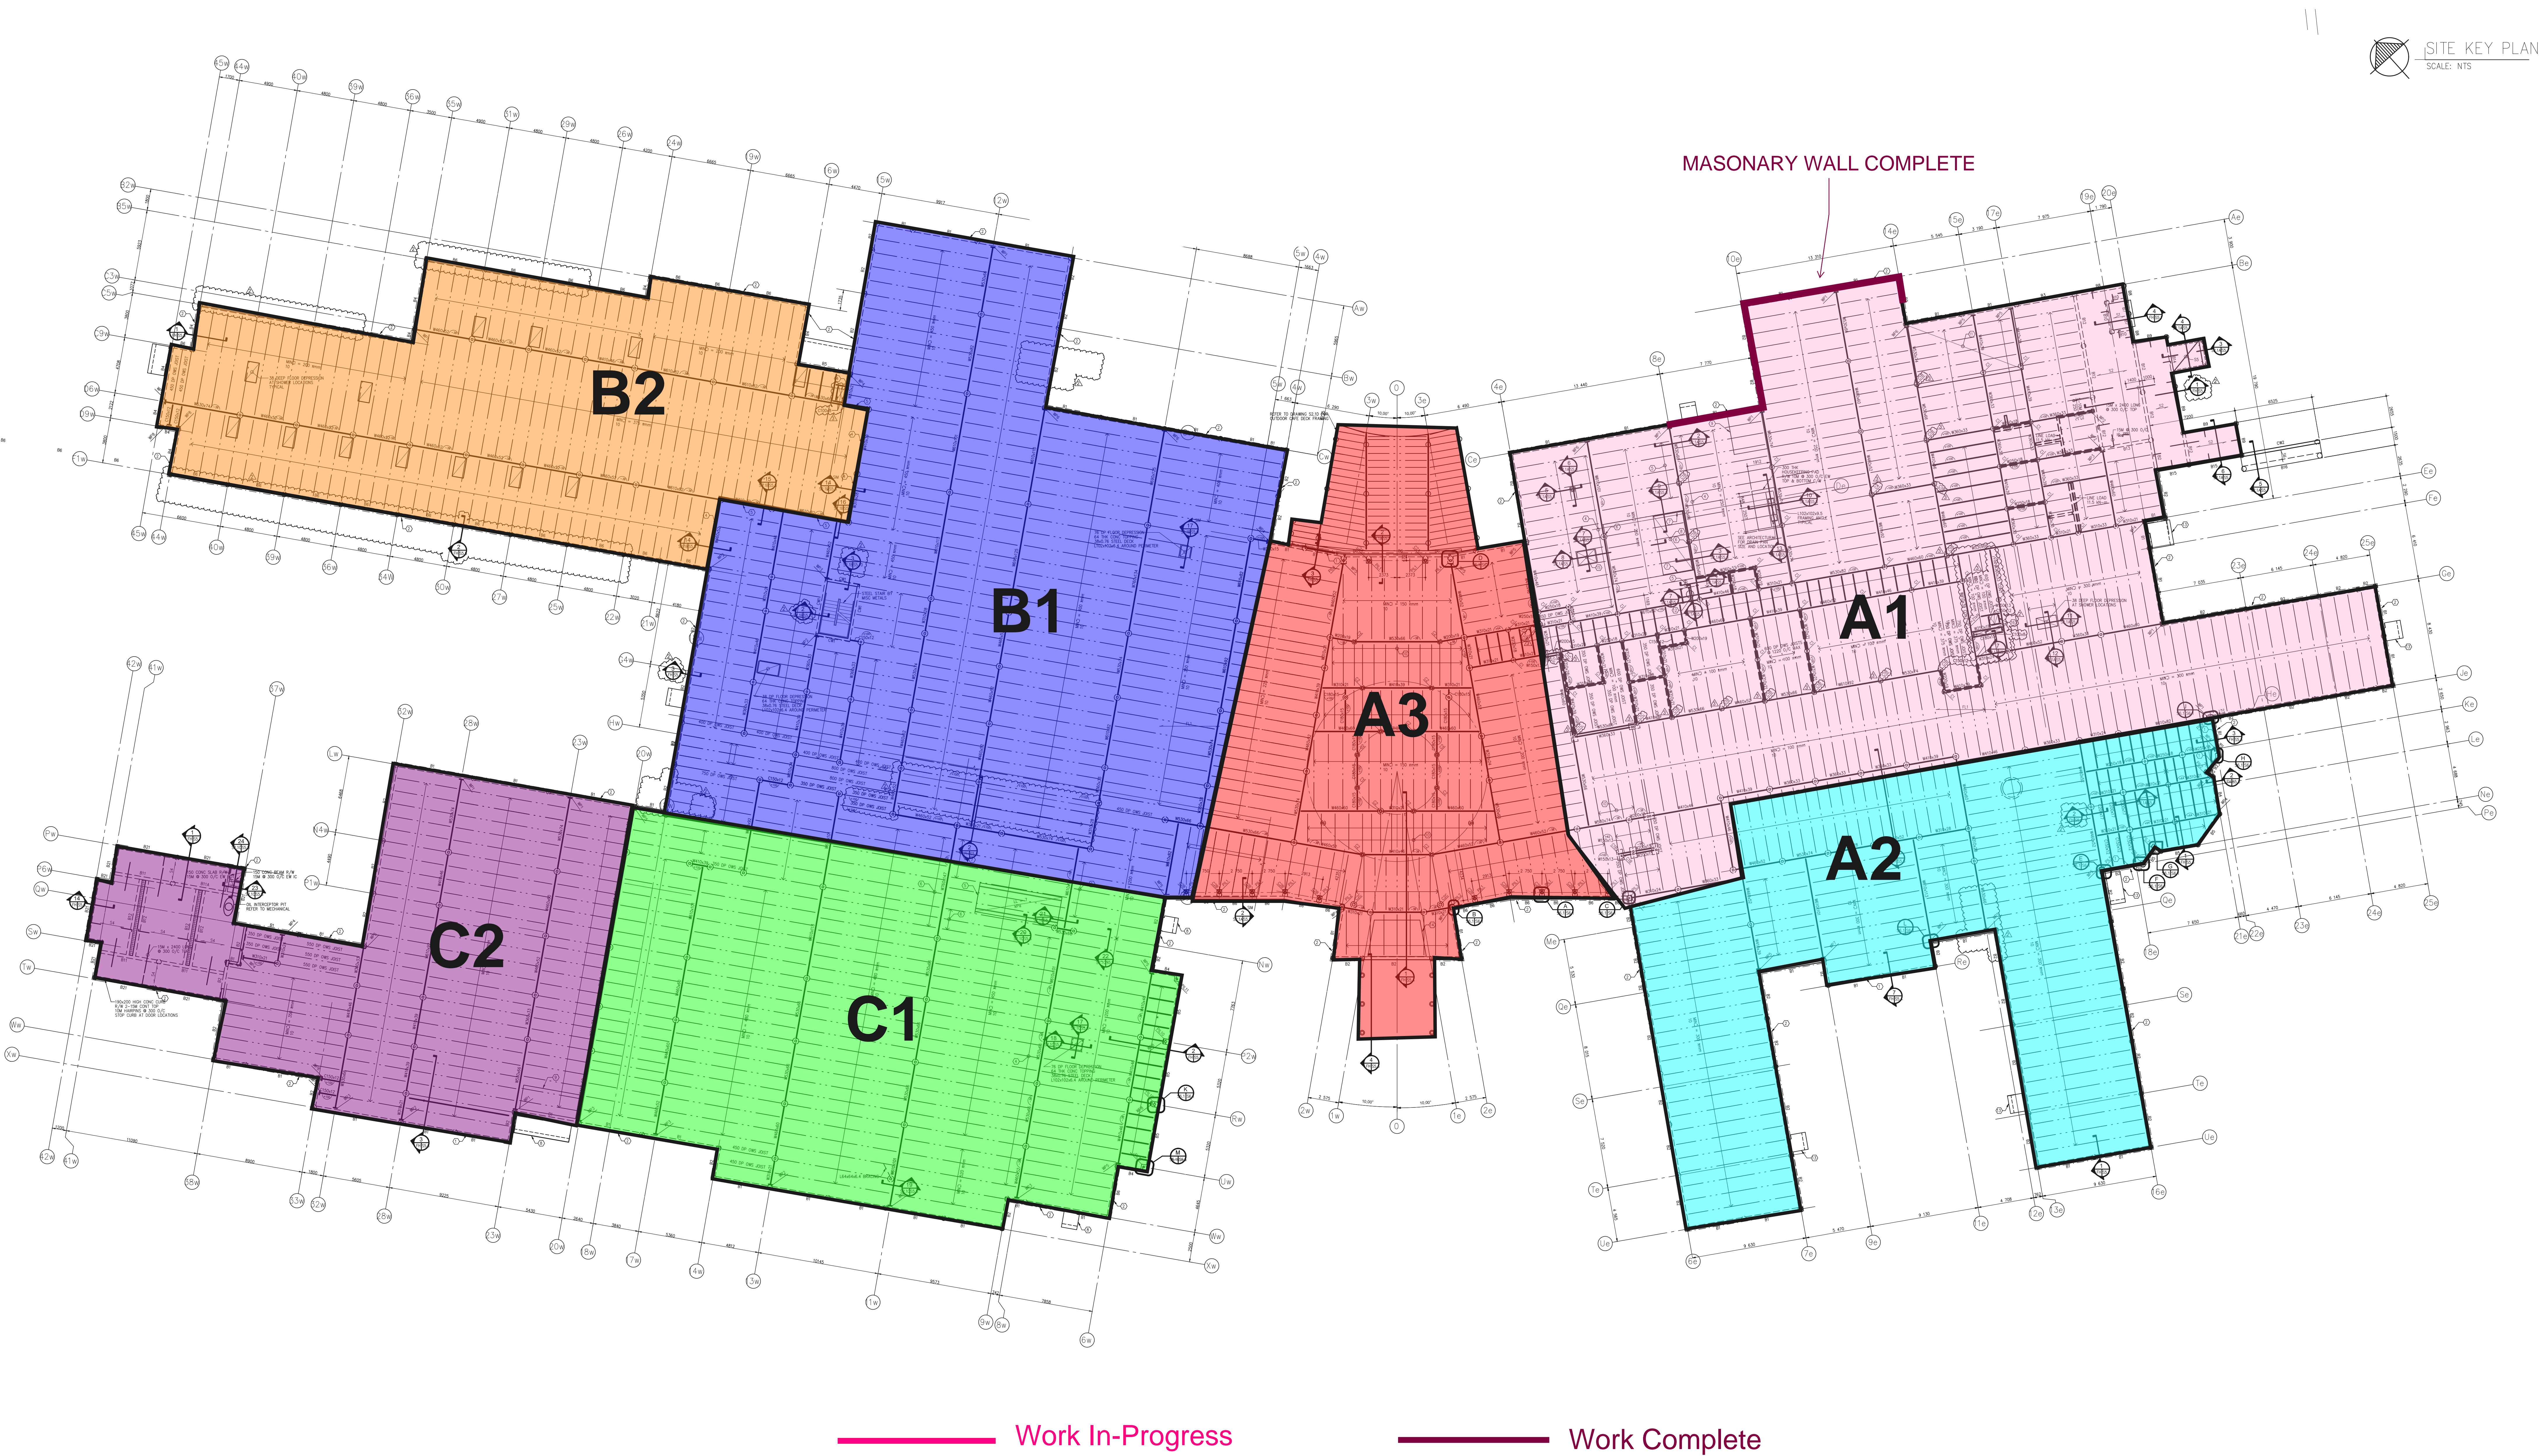

STRUCTURAL STEEL

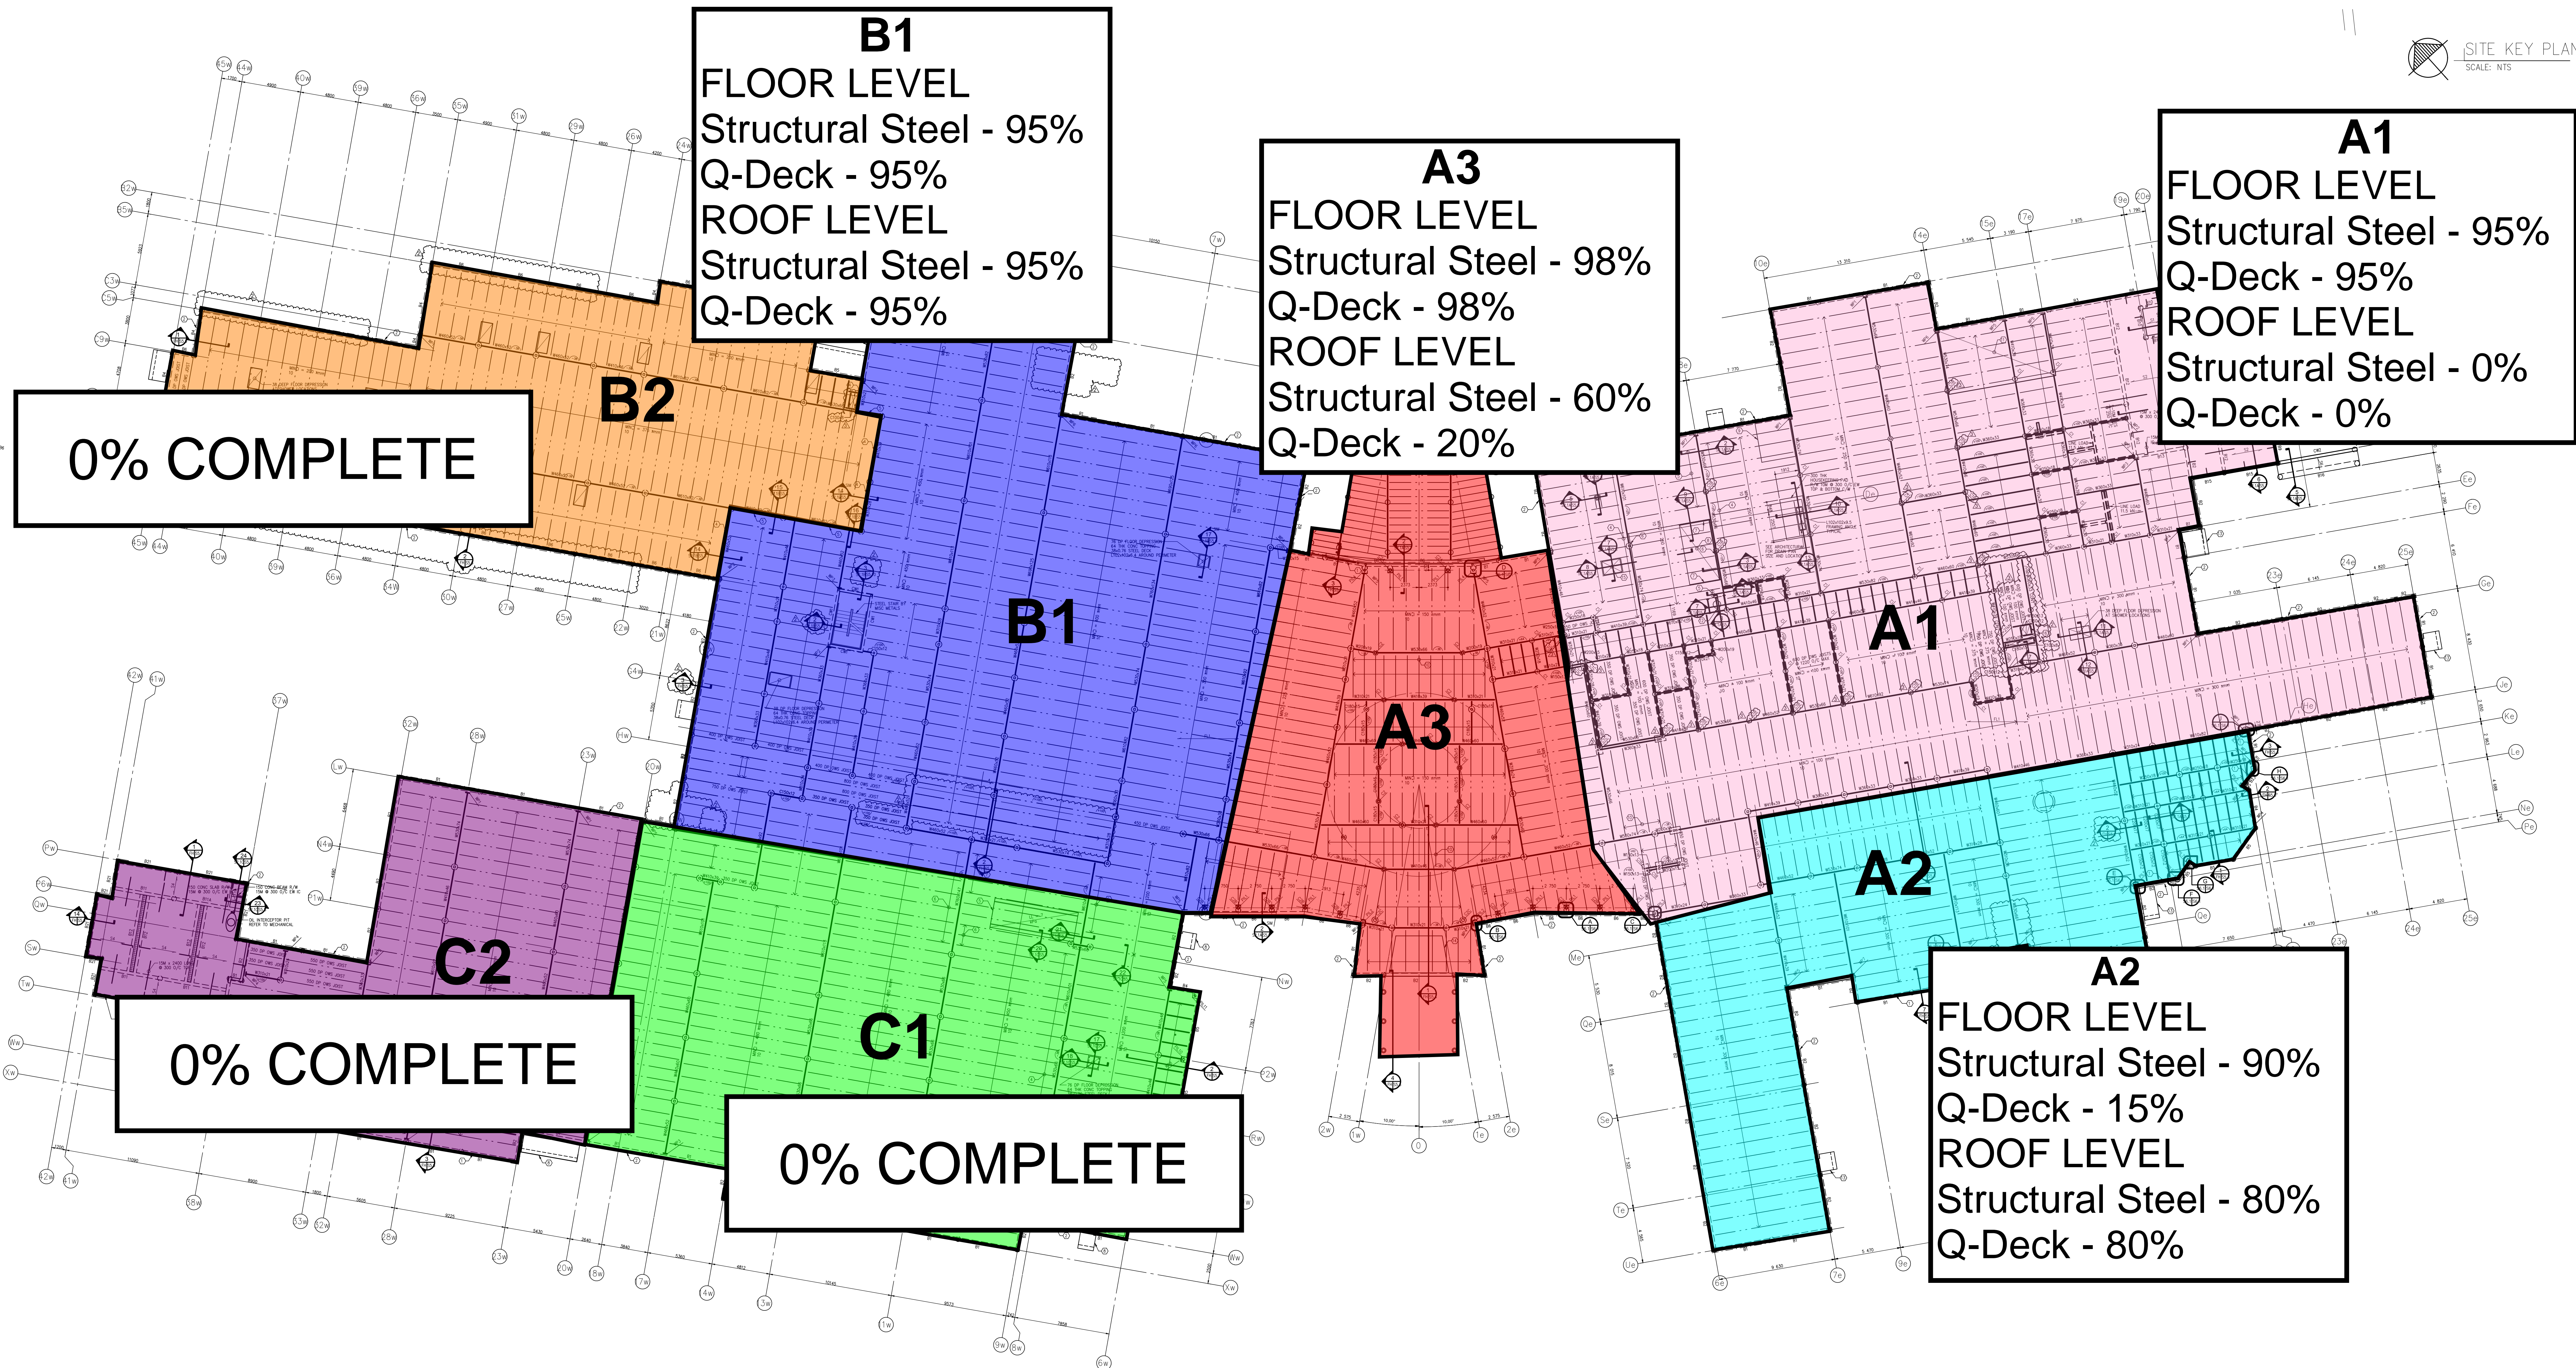

WEEPING TILE UPDATE

