

WEEKLY REPORT
REPORT NO. 56

MARCH 31, 2021

NORWAY HOUSE CREE NATION

HEALTH CENTRE OF EXCELLENCE



PROJECT: NHCN CD3 PROFESSIONAL ACCOMMODATIONS



PREPARED BY:

JNR CONSTRUCTION

PROJECT NAME: PROFESSIONAL ACCOMMODATIONS		PROJECT NUMBER: CD3 – 19015B	
SAFETY STATISTICS			
DESCRIPTION	PREVIOUSLY REPORTED	THIS PERIOD	PROJECT TO DATE
FIRST AIDES	14	0	14
INCIDENTS	18	0	18
DAILY COVID SCREENINGS	5062	144	5206
QUALITY/ENGINEERING			
ITEMS	SUBMITTED	RESOLVED	OUTSTANDING
RFIS	89	88	1
SHOP DRAWINGS	89	89	0
SAMPLES	7	7	0
GREEN GLOBES	28	17	11

OUTSTANDING ITEMS OR CONCERNS:

- NCR002 – Floor Level. Ongoing
- RFI087 – Range/Cooktop Millwork Clearances. Submitted February 22, 2021
- GG019 – GG028. Submitted March 09, 2021

COMPLETED THIS PERIOD	COMMENTS OR CONCERNS
Fiber Cement Siding	
Millwork Mock-Up Review	
LVL 2 Millwork Install	
LVL 2 Electrical Device Install	
Board Ceilings LVL 1	
Board Walls LVL 1 3 BR	
HM Door Install LVL 2	
LVL 2 Wall/Ceiling Finishing	
Refrigeration Piping to Fan Coils	
Bell MTS/Fibre Line Install	

TO COMPLETE NEXT PERIOD	TO COMPLETE THE FOLLOWING PERIOD
Fiber Cement Siding	LVL 2/LVL 1 Millwork Install
LVL 2 Millwork Install	LVL 2 Flooring Install
Board Ceilings LVL 1	Wood Door/Frame Install
Board Walls LVL 1 3 BR	LVL 2 Paint
Electrical Finishing	Fiber Cement Siding
Taping Ceiling/Walls LVL 1	Mechanical Rough Ins/Sump Pumps
LVL 2 Flooring Install	Electrical Finishing
Mechanical Rough Ins/Sump Pumps	Electrical Corridor Lighting
	Equipment Terminations

PROGRESS PHOTOS



PROGRESS PHOTOS

Exterior View – South



Exterior View – South



LVL 2 Millwork Mock-Up Suite Progress



LVL 2 Millwork Mock-Up Suite Progress

PROGRESS PHOTOS



LVL 2 Millwork Mock-Up Suite Install



LVL 2 Short Stay Millwork Install Progress



LVL 2 1 BR Millwork Install Progress



LVL 2 2 BR Millwork Install Progress

PROGRESS PHOTOS

LVL 2 Accessible Suite Vanity Install



LVL 2 Vanity Mock-Up Suite Install



LVL 2 Mock-Up Suite Millwork Shelving Install



LVL 2 Mock-Up Suite Windowsill Install

PROGRESS PHOTOS



LVL 2 Corridor Bulkhead Progress



LVL 1 Wall/Ceiling Board



LVL 2 Corridor Bulkhead Progress



LVL 2 Corridor Progress

PROGRESS PHOTOS




LVL 2 Corridor Progress



LVL 2 Corridor Progress



LVL 2 Elevator Lobby Ceiling Framing

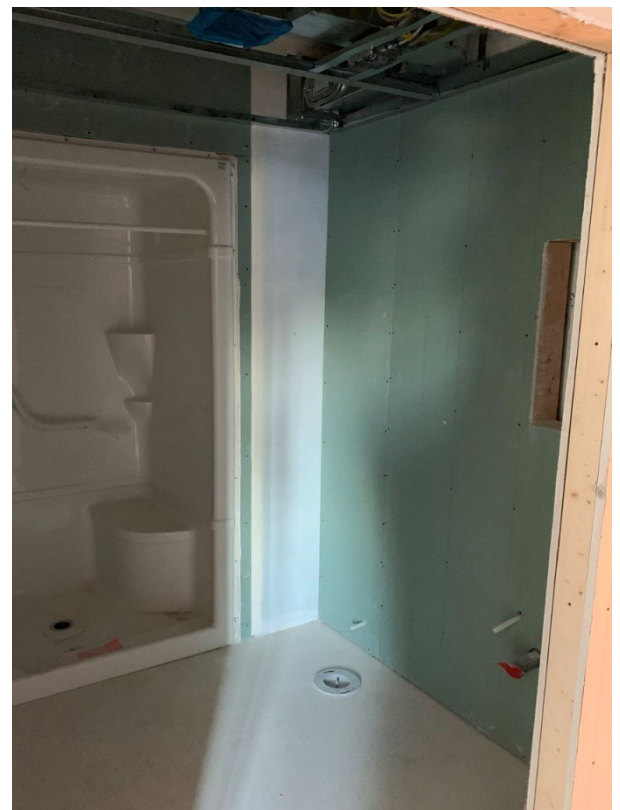

LVL 1 Tub Install/Mould Resistant Board

PROGRESS PHOTOS



LVL 1 Refrigerant Piping Install



Mechanical Room HVAC Ductwork



Curtain Wall Protection



MTS Device Installation in Comm. Room
