

WEEKLY REPORT
REPORT NO. 58

April 14, 2021

NORWAY HOUSE CREE NATION

HEALTH CENTRE OF EXCELLENCE



PROJECT: NHCN CD3 PROFESSIONAL ACCOMMODATIONS



PREPARED BY:

JNR CONSTRUCTION

PROJECT NAME: PROFESSIONAL ACCOMMODATIONS		PROJECT NUMBER: CD3 – 19015B	
SAFETY STATISTICS			
DESCRIPTION	PREVIOUSLY REPORTED	THIS PERIOD	PROJECT TO DATE
FIRST AIDES	14	0	14
INCIDENTS	18	0	18
DAILY COVID SCREENINGS	5206	106	5312
QUALITY/ENGINEERING			
ITEMS	SUBMITTED	RESOLVED	OUTSTANDING
RFIS	90	90	0
SHOP DRAWINGS	89	89	0
SAMPLES	9	8	1
GREEN GLOBES	28	17	11

OUTSTANDING ITEMS OR CONCERNS:

- NCR002 Floor Level. Ongoing.
- SD089 Signage. Revise/resubmit.
- SAMPLES009 Signage Etched/Vinyl Film. Outstanding.

COMPLETED THIS PERIOD	COMMENTS OR CONCERNS
Fiber Cement Siding	
LVL 2 Flooring Install	
LVL 2 Wood Door/Frame Install	
LVL 2 Paint	
Mechanical Rough Ins	
LVL 2 Millwork Install	
Electrical Corridor Lighting	
LVL 1 Ceiling Board	
LVL 1 Tape/Finishing	
LVL 2 Ceiling Grid	

TO COMPLETE NEXT PERIOD	TO COMPLETE THE FOLLOWING PERIOD
Fiber Cement Siding	Fiber Cement Siding
LVL 2 Flooring Install	LVL 1 Tape/Finishing
LVL 2 Wood Door/Frame Install	LVL 1 EW Paint
LVL 2 Paint	Mechanical Rough Ins/Sump Pumps
Mechanical Rough Ins	LVL 2 Wood Door/Frame Install
LVL 2 Millwork Install	Electrical Finishing
Mechanical Insulation	LVL 2 Ceiling Grid
LVL 1 EW Paint	Data Comm Installation
LVL 1 Tape/Finishing	Mechanical Insulation
LVL 2 Ceiling Grid	
Data Comm Installation	
LVL 1 EW Millwork	

PROGRESS PHOTOS



Exterior Progress - South



Exterior Progress - South East



LVL 2 EW Flooring Install



LVL 2 EW Flooring Install

PROGRESS PHOTOS




LVL 2 EW Flooring Install



LVL 2 EW Flooring Install



LVL 2 EW Flooring Install

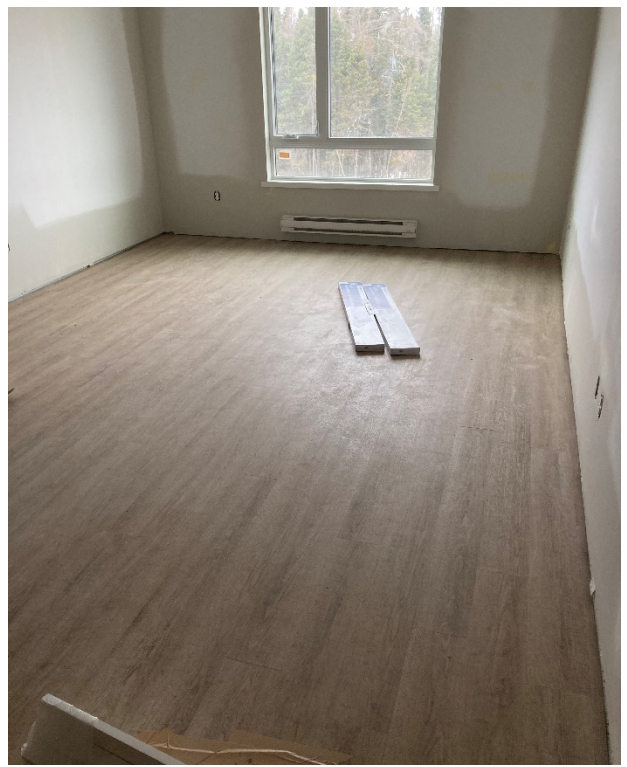

LVL 2 EW Flooring Install

PROGRESS PHOTOS



LVL 2 EW Flooring Protection



LVL 2 EW Flooring Protection



LVL 2 EW Flooring Protection



Electrical Light Fixtures

PROGRESS PHOTOS



LVL 1 Corridor Progress



LVL 1 Corridor Progress



LVL 2 Corridor Progress



LVL 2 Stair 1 Ceiling Framing Progress

PROGRESS PHOTOS



LVL 2 Corridor Acoustic Ceiling Progress



LVL 2 Suspended Ceiling Framing Progress



LVL 1 EW Taping/Finishing Progress



LVL 1 EW Taping/Finishing Progress

PROGRESS PHOTOS



Mechanical Room Plumbing Hanger Installation



Mechanical Room HVAC Ductwork
