

WEEKLY REPORT
REPORT NO. 63

May 19, 2021

NORWAY HOUSE CREE NATION

HEALTH CENTRE OF EXCELLENCE



PROJECT: NHCN CD3 PROFESSIONAL ACCOMMODATIONS



PREPARED BY:

JNR CONSTRUCTION

PROJECT NAME: PROFESSIONAL ACCOMMODATIONS		PROJECT NUMBER: CD3 – 19015B	
SAFETY STATISTICS			
DESCRIPTION	PREVIOUSLY REPORTED	THIS PERIOD	PROJECT TO DATE
FIRST AIDES	14	0	14
INCIDENTS	19	0	19
DAILY COVID SCREENINGS	5856	104	5960
QUALITY/ENGINEERING			
ITEMS	SUBMITTED	RESOLVED	OUTSTANDING
RFIS	92	91	1
SHOP DRAWINGS	90	88	2
SAMPLES	11	11	0
GREEN GLOBES	28	17	11

OUTSTANDING ITEMS OR CONCERNS:

- NCR002 Floor Level. Ongoing.
- SD089 Signage. Revise/resubmit.
- RFI092 Fire Safety Plan. Submitted 18-May-21
- SD083Rev01 Wire Mesh Lockers. Submitted 19-May-21
- Bell MTS Coordination by Owner – Fire Alarm Monitoring/Phone System
- Manitoba Hydro – Incoming High Voltage

COMPLETED THIS PERIOD	COMMENTS OR CONCERNS
Fiber Cement Siding	
LVL 1 EW Flooring Install	
LVL 1 Wood Doors/Frame Install	
LVL 1 WW Ceiling Grid	
LVL 1 Ceiling Tile	
LVL 1/LVL 2 M/E Finishes	
LVL 1 WW Millwork	
LVL 1/LVL 2 Paint	

TO COMPLETE NEXT PERIOD	TO COMPLETE THE FOLLOWING PERIOD
Fiber Cement Siding	Fiber Cement Siding
LVL 1 EW Flooring Install	LVL 1 WW Flooring Install
LVL 1 WW Flooring Install	LVL 1/LVL 2 M/E Finishes
M/E Equipment Start Ups - Tentative	LVL 1/LVL 2 Final Paint
LVL 1 Wood Doors/Frame Install	M/E Commissioning - Tentative
Sprinkler System Testing/Finishing	Air Balancing - Tentative
LVL 1/LVL 2 M/E Finishes	Fire Alarm VI - Tentative

PROGRESS PHOTOS

LVL 2 EW Progress



LVL 2 Corridor Progress



LVL 2 Storage Progress



LVL 2 Housekeeping Progress

PROGRESS PHOTOS



LVL 1 Fitness Centre Flooring Progress



LVL 1 Fitness Centre Flooring Progress



LVL 1 Fitness Centre Flooring Progress



LVL 1 Fitness Centre Flooring Progress

PROGRESS PHOTOS


LVL 1 EW Progress



LVL 1 EW Flooring Progress



LVL 2 EW Lighting Install

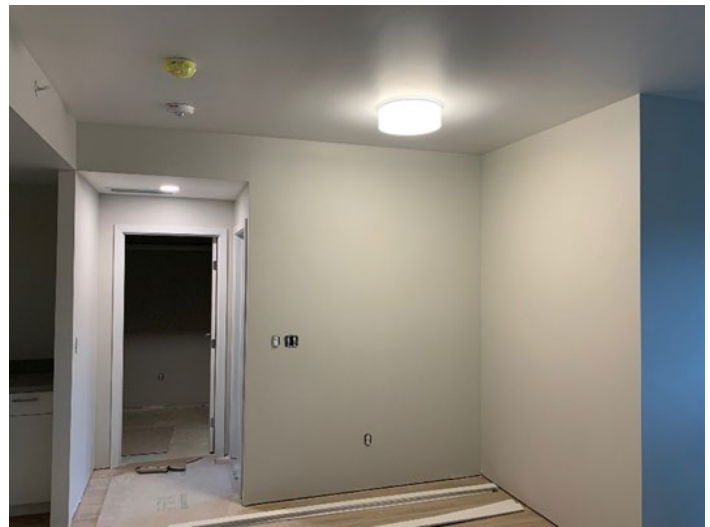

LVL 2 EW Lighting Install

PROGRESS PHOTOS



LVL 2 EW Lighting Install



LVL 2 Corridor Progress



Sprinkler Piping Firestop System Labelling



Mechanical Room Water Service Installation

PROGRESS PHOTOS

Mechanical Room Sprinkler System Installation



LVL 2 Accessible Suite Sunken Floor Install
