Weekly Report #61

Nov 24th-30th 2021

Norway House Cree Nation

Health Centre of Excellence

Project:

CD4 – Health Centre of Excellence

Aman Chana

JNR Construction

Weekly Progress Report
Nov 30, 2021, ID #579

REPORT DETAILS

Description

Created by Aman Chana

Status Draft

Last update Dec 9, 2021 2:33 PM

Last updated by Aman Chana

1. WORK LOG

Crew	# Workers	# Total hours	Work performed
JNR and Subtrades	107	6420	See below
Totals	107	6420	

2. CREW ONSITE

2.1 The following crews were active in this report period

- [x] JNR
- [x] Mechanical
- [x] Electrical
- [x] Masonry
- [ ] Structural Steel
- [x] Carlson
- [x] Oakwood

3. ARCHITECTURAL

3.1 Ongoing Work

JNR Local Labour
-Working on backing in B1
-Working on RTU curbs C2 roof
-Working heating and hoarding
-Working heating and hoarding A1/A2
-Working on heating for masonry A3
-Working on insulating GB C2 North
-Working on warming up shack between C-Cans

General site clean up / Hauling water for washroom / Fueling / Checking pumps, fans & de-humidifiers / Removing garbage / Moving material on site / Operating zoom boom, fuel truck/ Snow removal

3.2 Completed Work

N/A

4. STRUCTURAL

4.1 Ongoing Work

JNR Concrete Crew
-Pouring and finishing housekeeping pads

4.2 Completed Work

5. MECHANICAL

5.1 Ongoing Work

-Coil connections B1
-B1 medical gas install
-B1 West corridor water main and branch install
-A2 horizontal water mains and branches
-Coil connections A3
-C1 RWL install
-Move boiler components and burners into mech room
-B2 South hallway install prep
-B2 South hallway hanger install
-B1 medical gas install
-B2 In-wall rough in south
-B2 South hallway install prep
-Install ductwork (B1)

-Insulation work in B1
-Insulate water mains B1 corridor
-Insulate HYD piping in B1
-Install hangers and pipe for pre-action in B1
-Install sprinkler in Penthouse
-Install piping in A2 where ready

-Install controls conduit in area B1
-Install conduits from main floor to crawlspace
-Terminate VAV and RHC in B1

5.2 Completed Work

6. ELECTRICAL

6.1 Ongoing Work

-Install conduit work packages in area A2
-Cable pulling roof
-Arranged materials on site
-Outside grounding
-B1 conduit install
-Door security B2
-B1 room review
-Rack install building roof
-Cable management A1
-BI conduit packages
-A2 pipe packages installed

6.2 Completed Work

7. CIVIL

7.1 Ongoing Work

Civil
-Cleared snow A3 South
-Started covering insulation with clay
-Hauled and placed clay on A3 South

JNR Surveyor
-Backing layout & monitoring B1/A2
-Drafting & data management

7.2 Completed Work

8. MASONRY

8.1 Ongoing Work

-Installing stone veneer B2 North
-Installing stone veneer A3 North
-Thru wall flashing over angle in C1 and C2 South

8.2 Completed Work

9. OAKWOOD ROOFING/SIDING

9.1 Ongoing Work

SIDING
-Working on insulating A2 around Hot tub
-Insulating the portions that blew out on B2 West
-Pin wheel around pipes A1 North and insulating.
-General house keeping
-Insulating the temporary foam to cover the areas between Oakwood and Roma insulation in A2
-Installing panels A1 North
-Install plywood and secure rock on C2 projection
-Priming and installing AVB A3 South
-Insulating A2 parapet wall
-Working on insulating A2 between fingers
-Insulating and priming around electrical pipes in A2
-Insulating A3 South over curtain wall

ROOFING
-General housekeeping and snow clearing
-Working in RTU curb B1 so that Wescan can weld
-Installed cap sheet on curbs A1 roof
-Sealed parapet wall C1 East
-Installed flashing on C1 South
-Install plywood and secure rock on C1 projection
-Insulated and installed cap sheet on RTU C1
-Insulate RTU on C2 roof
-Install plywood and secure rock on C2 projection
-Insulate inside RTU on C2 roof
-Working on elevation inside B2 RTU

9.2 Completed Work

10. CARLSON

10.1 Ongoing Work

-Framing interior steel stud (B2)
-Installing drywall tops (B2)
-Installing door frames in A2 (Hot tub)
-Framing interior steel stud (A1)
-Framing interior steel stud (A1) over block wall

10.2 Completed Work

11. SAFETY AND COVID-19 SCREENING

11.1 Number of Covid Screening reports completed

JNR is continuing screening all visitors and staff daily who report to site. 636 Covid screening reports completed on site from this time period.

12. SITE VISIT SCHEDULE

12.1 Next scheduled site visit

PHOTOS (39)

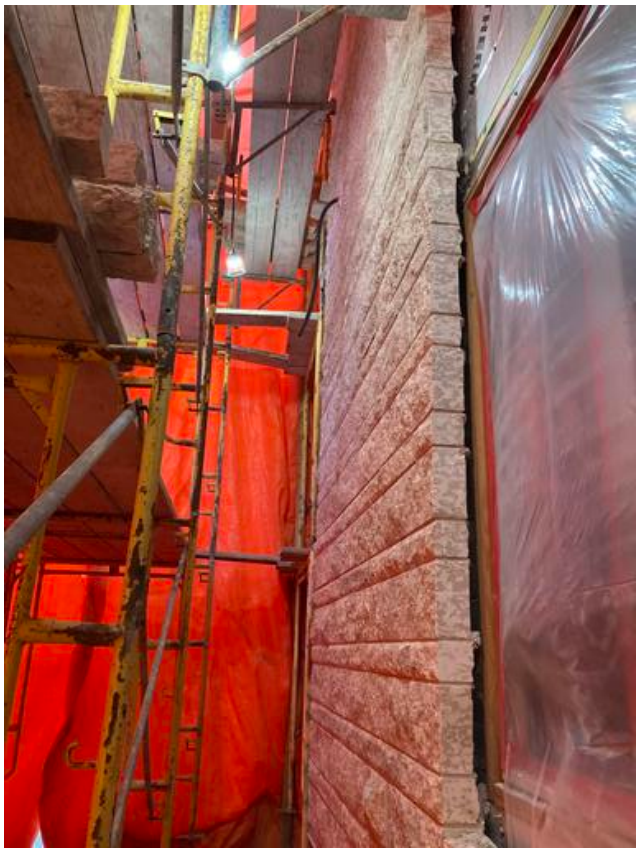

Veneer installation on going B2 North
Anmol Kang
Nov 29, 2021 4:29 PM

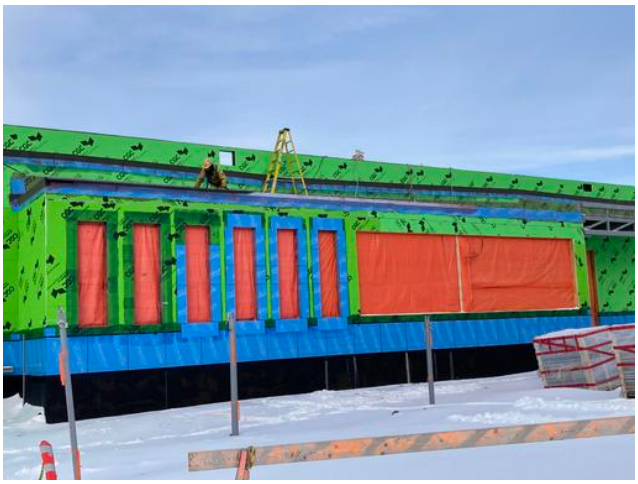

Installing flashing C2 projection
Anmol Kang
Nov 29, 2021 4:28 PM

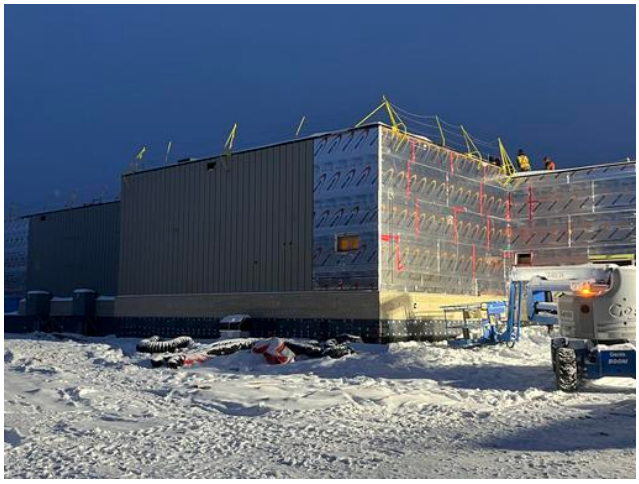

Panels installed A1 North
Anmol Kang
Nov 29, 2021 4:28 PM

A1 hoarded
Anmol Kang
Nov 29, 2021 4:25 PM

AVB installation on going C1 East
Anmol Kang
Nov 28, 2021 1:37 PM

Installing AVB A3 South
Anmol Kang
Nov 28, 2021 1:37 PM

Scaffolding setup North of A3
Anmol Kang
Nov 27, 2021 7:02 PM

Insulation work around hot tub
Anmol Kang
Nov 27, 2021 6:13 PM

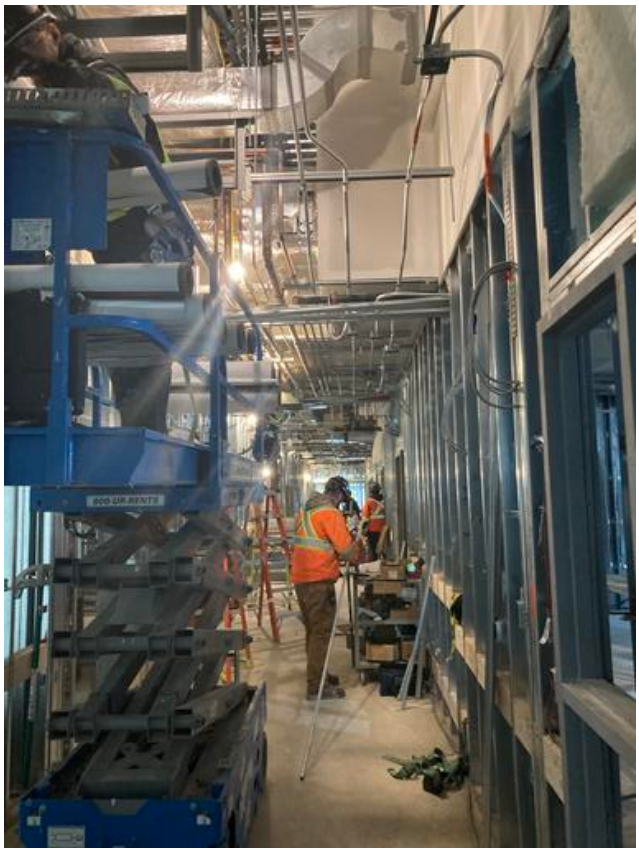

conduit installation on going B1
Anmol Kang
Nov 27, 2021 5:36 PM

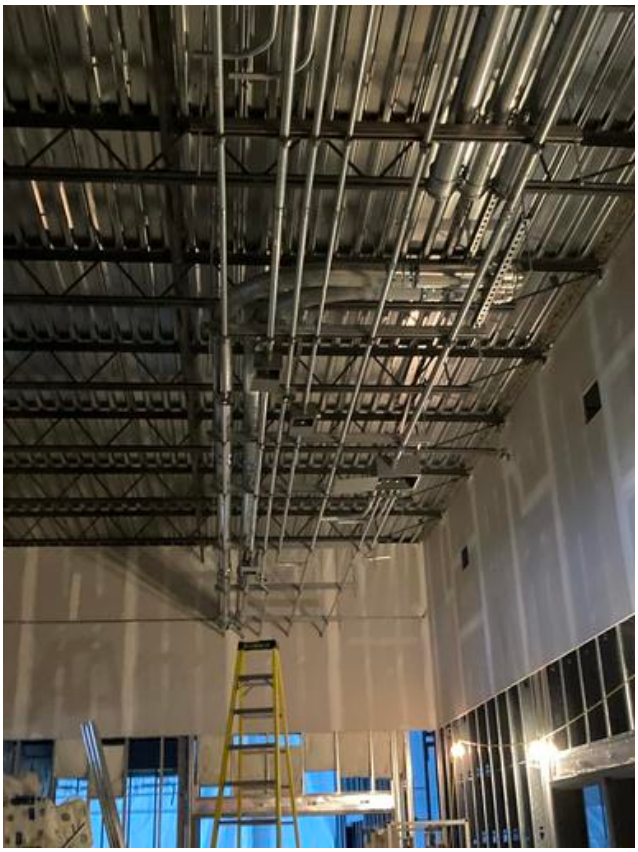

Conduit installation in A2
Anmol Kang
Nov 27, 2021 5:33 PM

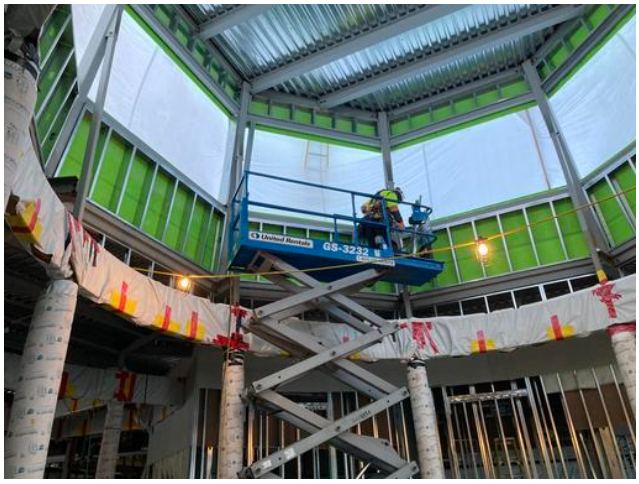

Cultural hall framing on going
Anmol Kang
Nov 27, 2021 5:33 PM

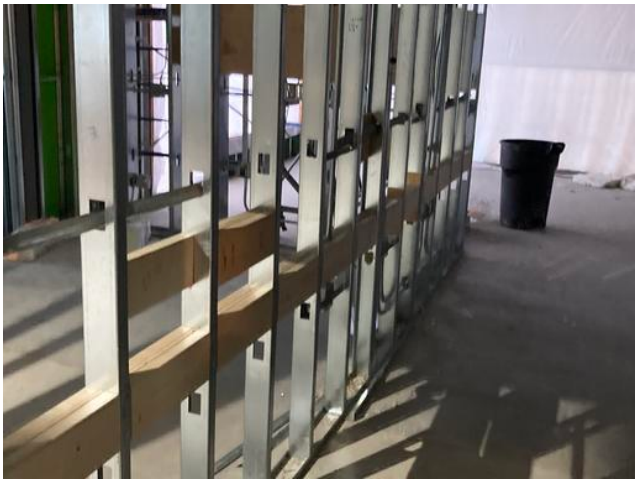

Backing work on going in B1
Anmol Kang
Nov 27, 2021 5:23 PM

Placing clay over insulation A3 South
Anmol Kang
Nov 26, 2021 12:55 PM

Stone veneer installation on going B2 North
Anmol Kang
Nov 26, 2021 12:54 PM

Installing base sheet A3 roof
Anmol Kang
Nov 26, 2021 12:52 PM

Installing panels A1 North
Anmol Kang
Nov 26, 2021 12:45 PM

Work on going in B1 corridor
Anmol Kang
Nov 25, 2021 5:57 PM

Installing top tracks A1
Anmol Kang
Nov 25, 2021 5:57 PM

Installing drywall tops B2
Anmol Kang
Nov 25, 2021 5:56 PM

Installing door frame
Anmol Kang
Nov 25, 2021 5:55 PM

Rough in work on going B1
Anmol Kang
Nov 25, 2021 5:54 PM

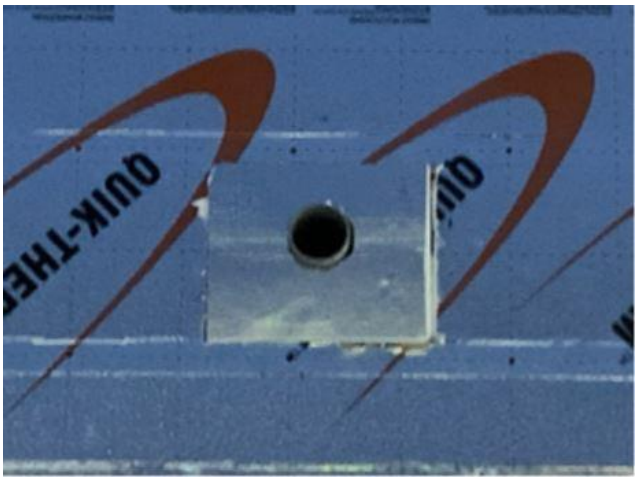

Insulation work around pipes
Anmol Kang
Nov 25, 2021 5:53 PM

Insulating around hot tub
Anmol Kang
Nov 25, 2021 5:53 PM

Removing snow for backfill
Anmol Kang
Nov 25, 2021 5:53 PM

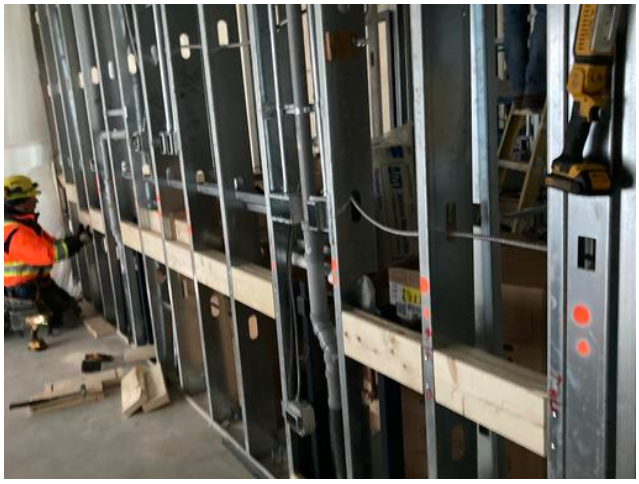

Backing on going in B1
Anmol Kang
Nov 25, 2021 5:51 PM

Installing flashing C1
Anmol Kang
Nov 25, 2021 5:49 PM

Insulating remaining open areas A1
Anmol Kang
Nov 25, 2021 5:49 PM

Working on parapet wall C1 East
Anmol Kang
Nov 25, 2021 5:44 PM

Installing cap sheet
Anmol Kang
Nov 25, 2021 5:44 PM

Working on RTU curb C2
Anmol Kang
Nov 25, 2021 5:43 PM

Taping work on going B2
Anmol Kang
Nov 25, 2021 5:43 PM

Installing conduits A2
Anmol Kang
Nov 25, 2021 5:42 PM

Insulation work on going
Anmol Kang
Nov 24, 2021 5:56 PM

Backing work on going B1 corridor
Anmol Kang
Nov 24, 2021 5:56 PM

Priming A3 vestibule
Anmol Kang
Nov 24, 2021 5:55 PM

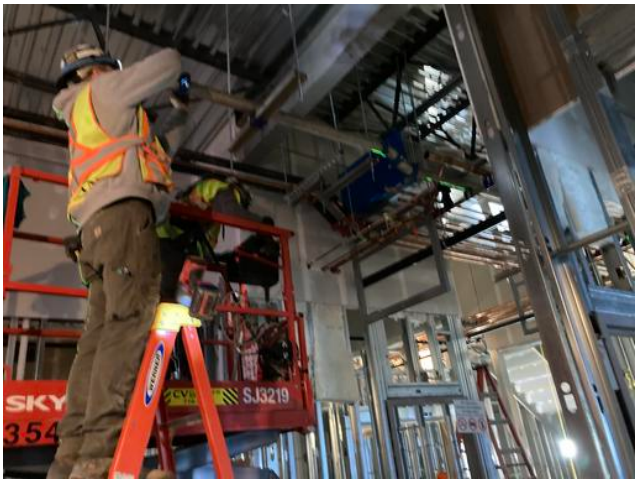

Working on domestic water lines
Anmol Kang
Nov 24, 2021 5:44 PM

Working on cable trays
Anmol Kang
Nov 24, 2021 5:43 PM

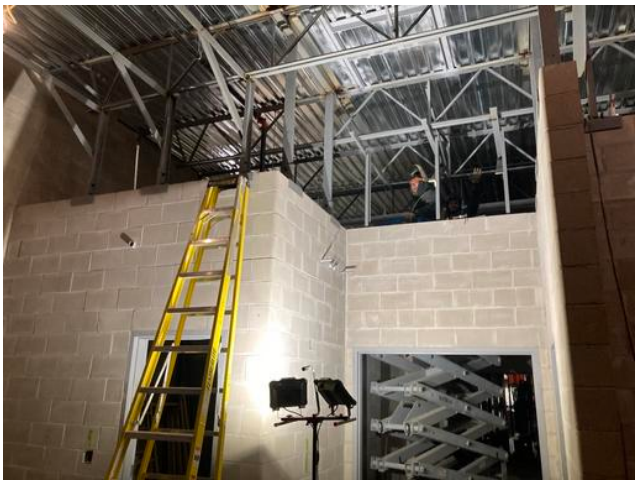

Misc metal work on going
Anmol Kang
Nov 24, 2021 5:43 PM

Hoarding for masonry
Anmol Kang
Nov 24, 2021 5:43 PM

NORWAY HOUSE HEALTH CENTRE OF EXCELLENCE WEEKLY UPDATE NOVEMBER 28TH 2021

DRYWALL TOP PROGRESS

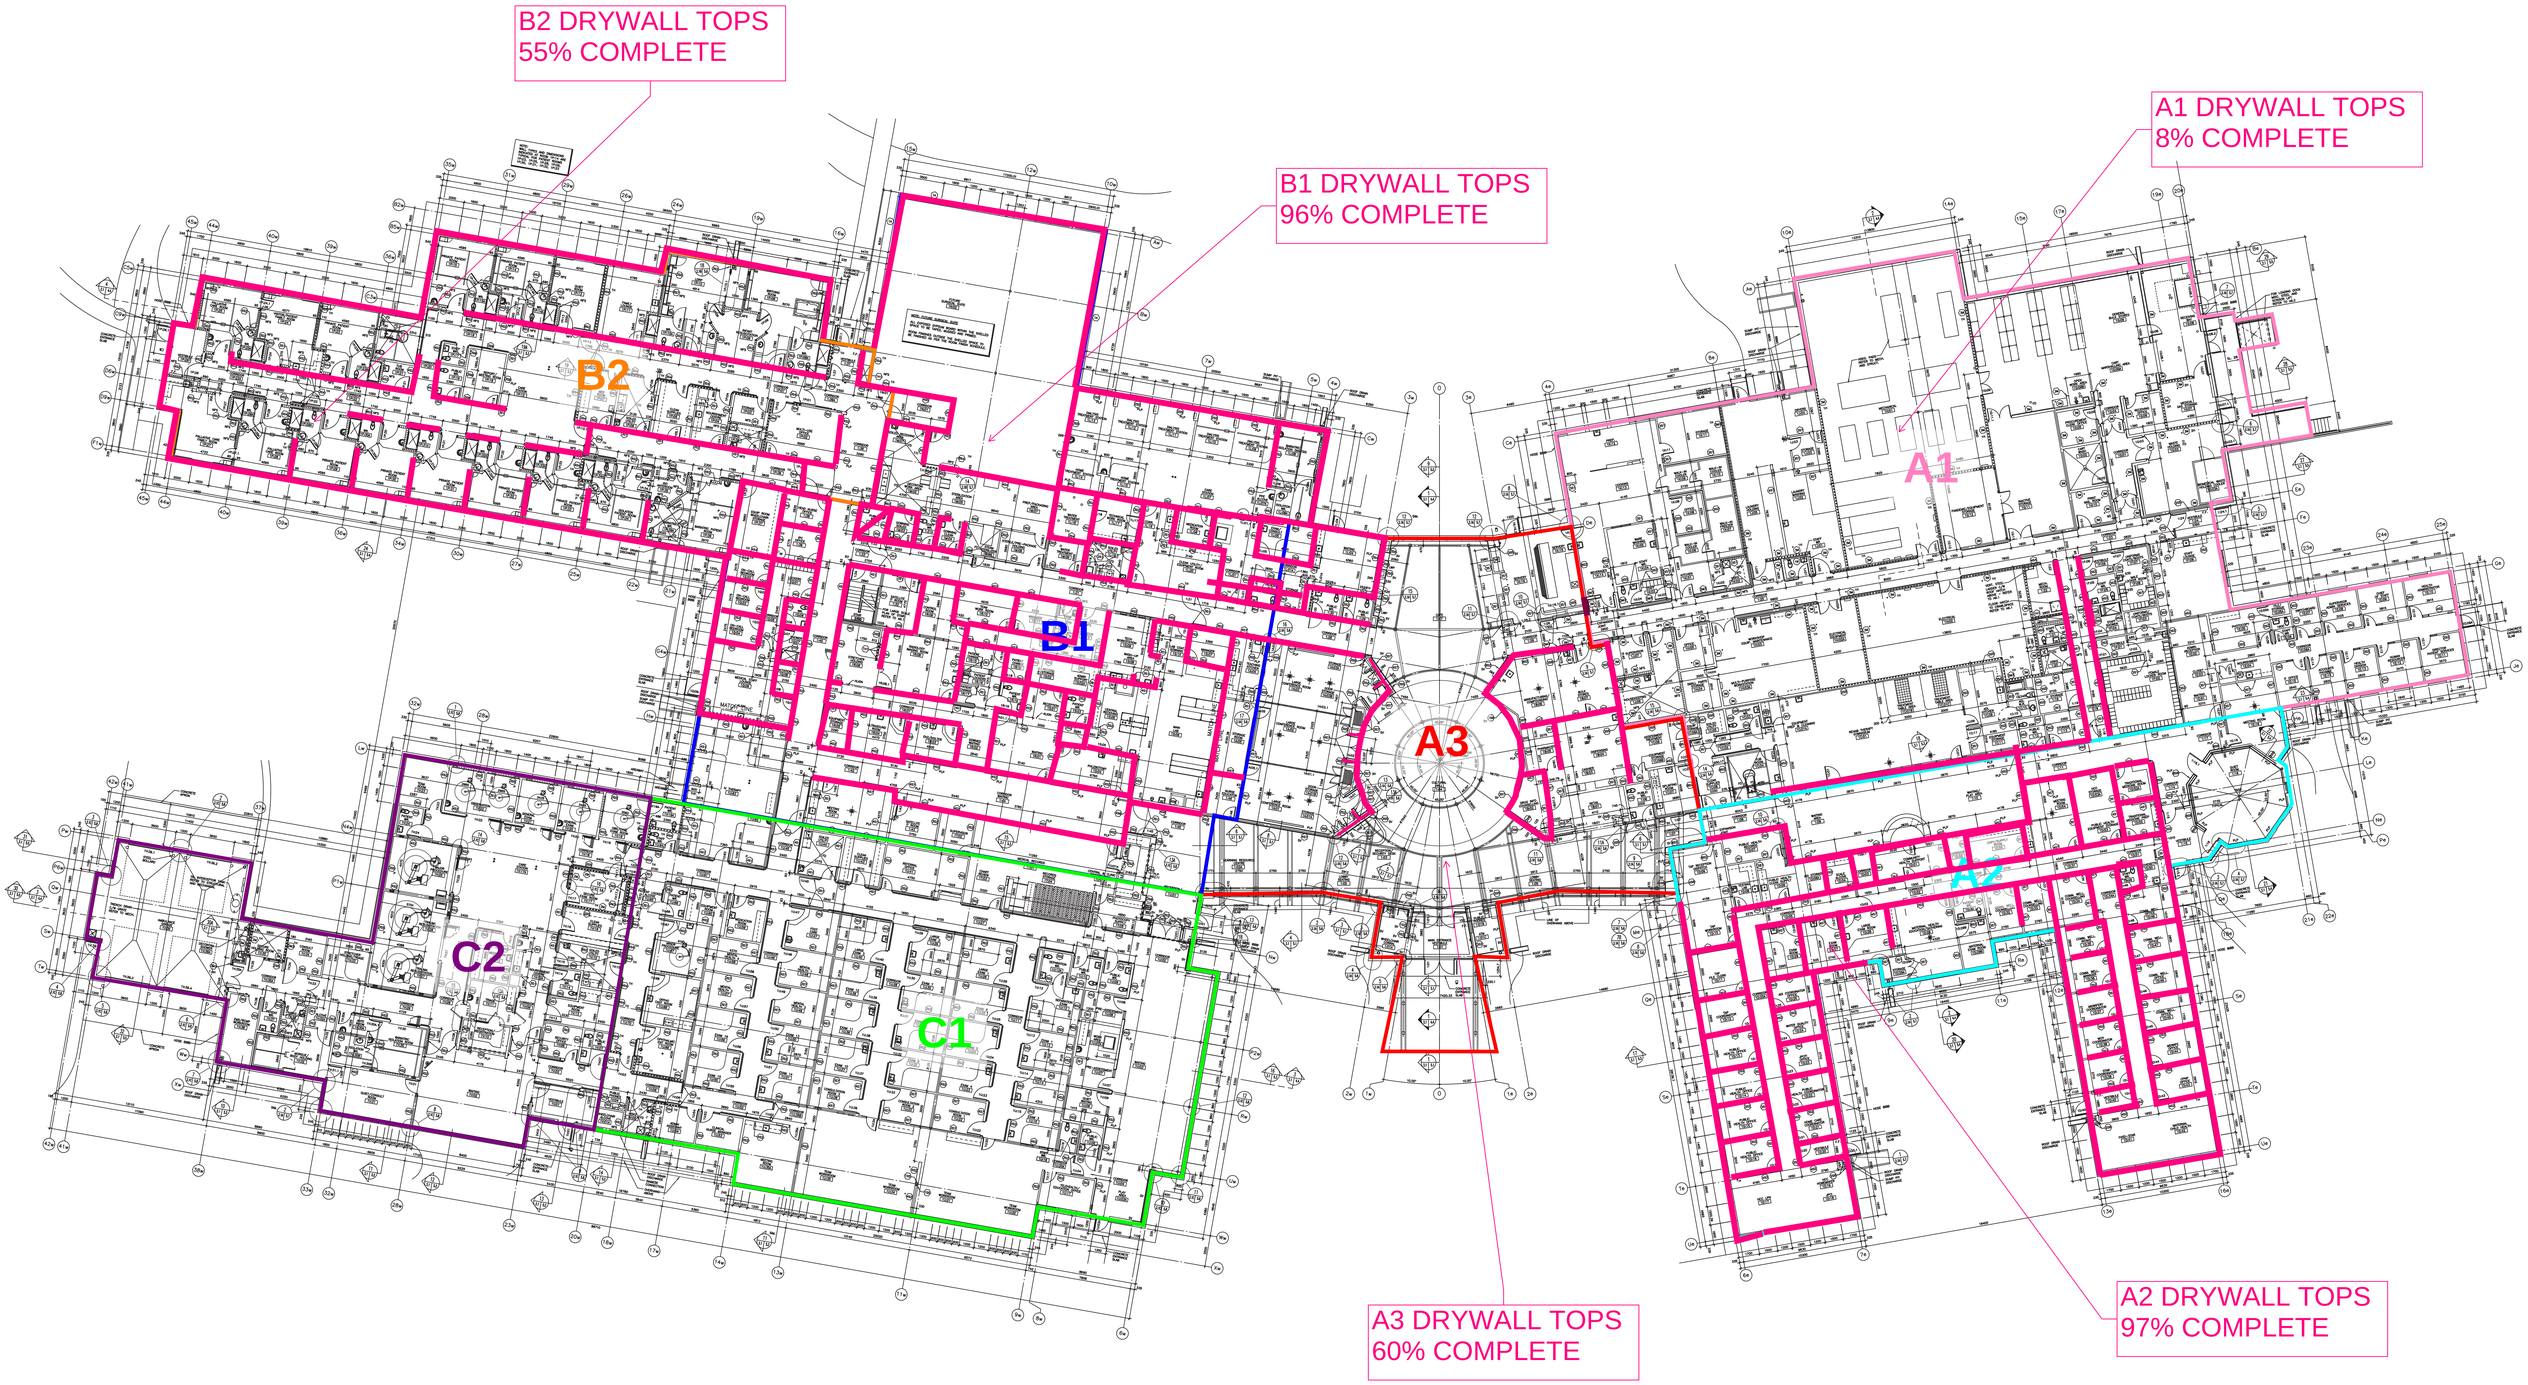

NORWAY HOUSE HEALTH CENTRE OF EXCELLENCE WEEKLY UPDATE NOVEMBER 28TH 2021

EXTERIOR STEEL STUD FRAMING

AREA	EXTERIOR WALL % COMPLETION
A1	100
A2	100
A3	100
B1	100
B2	100
C1	97 (+2)
C2	95

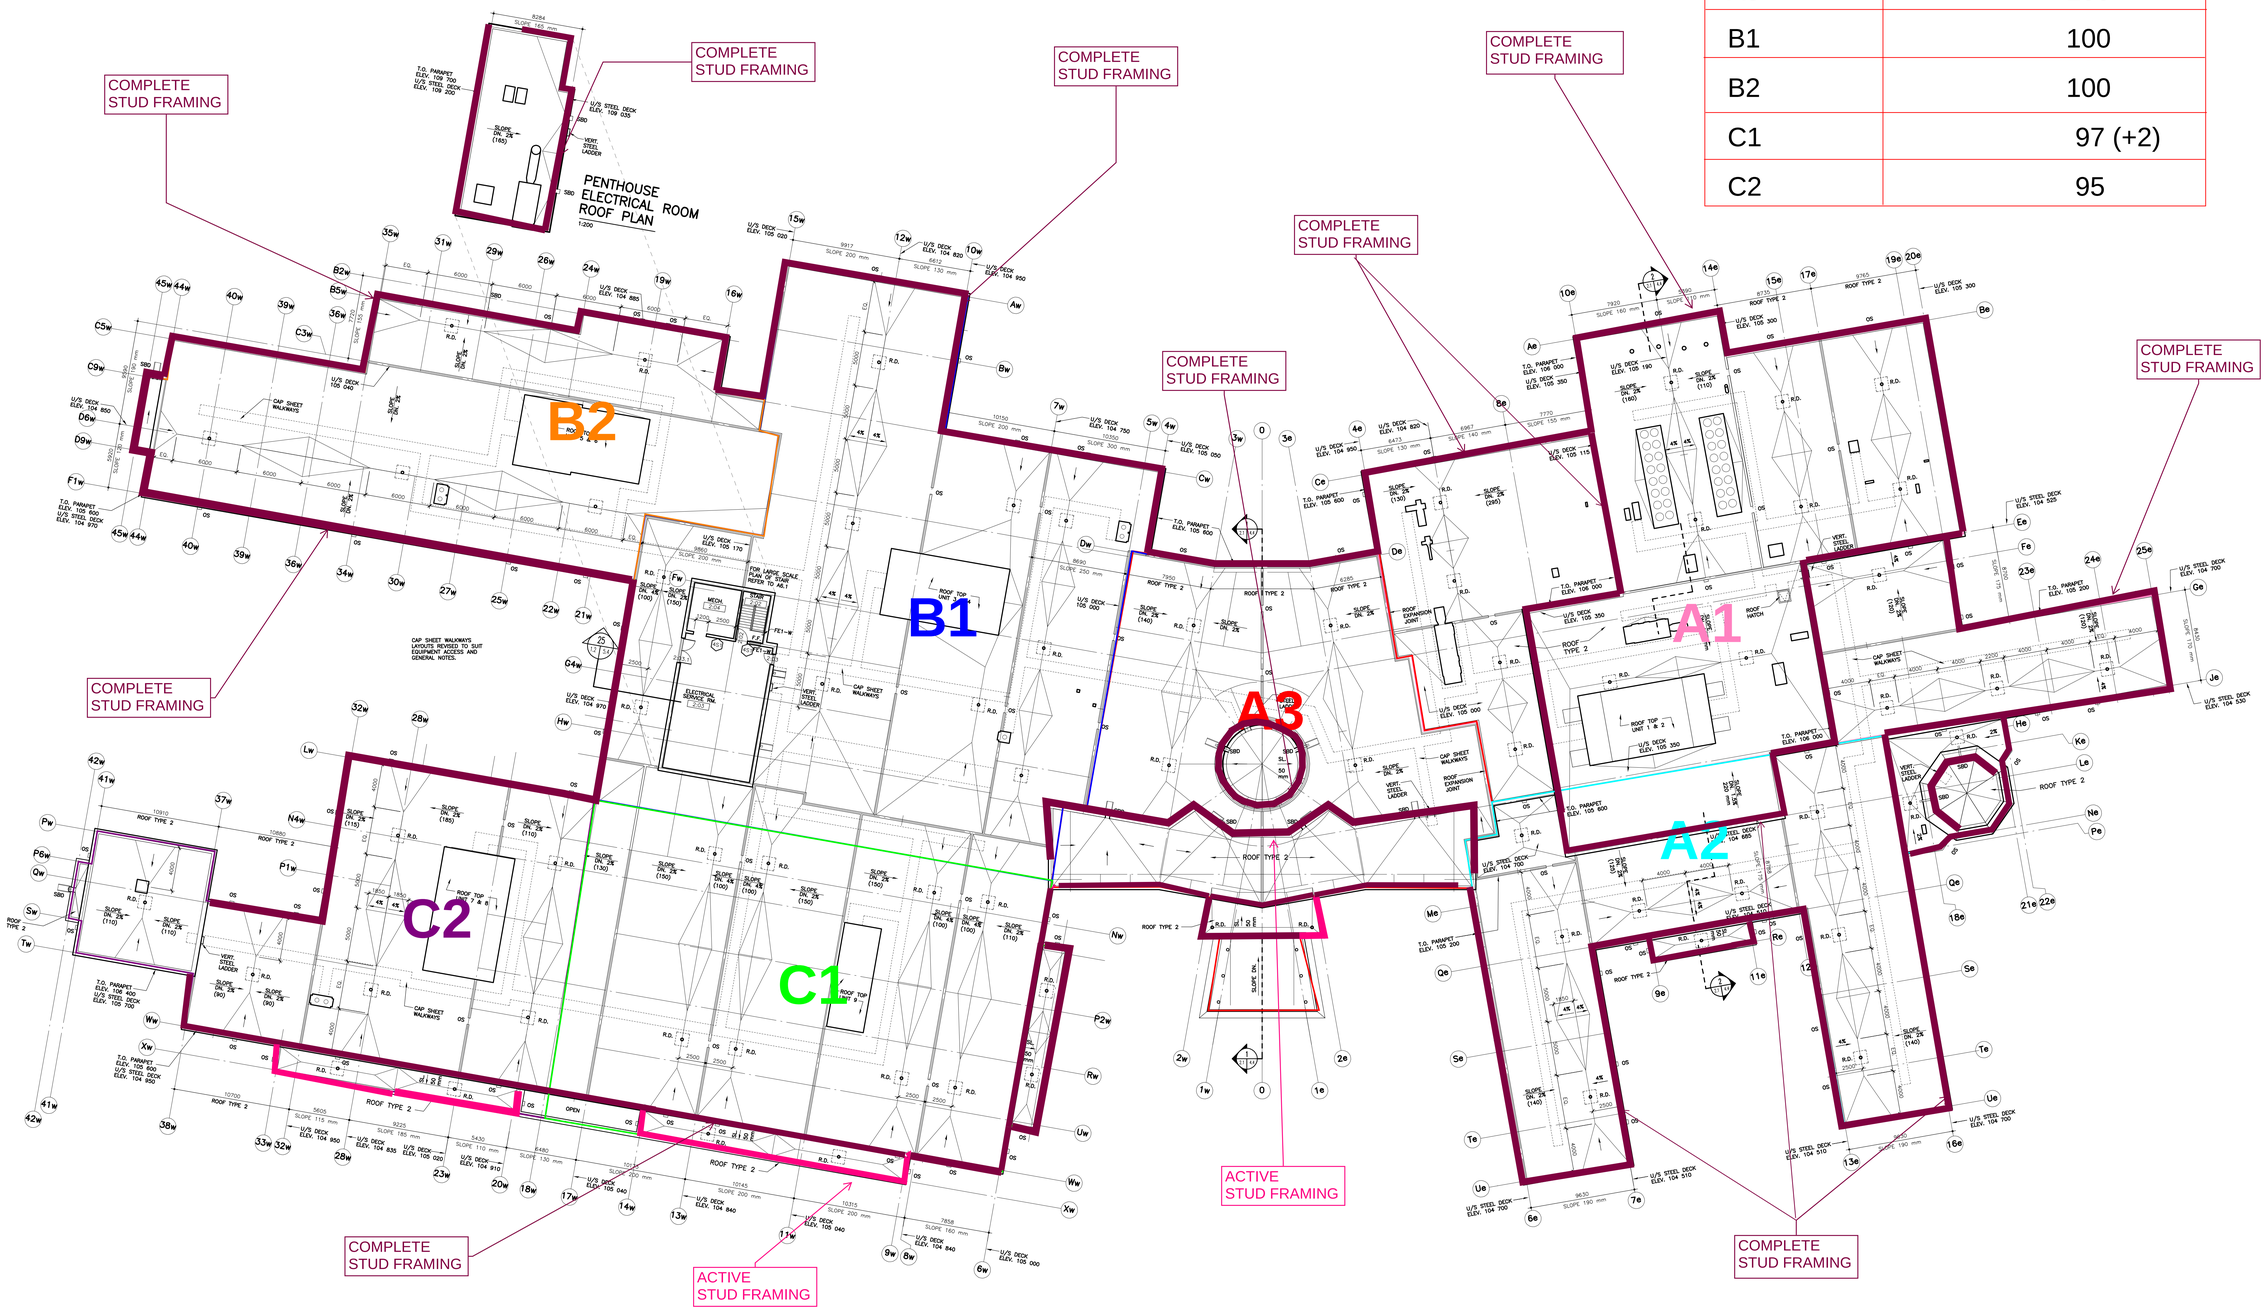

Work In-Progress

Work Complete

NOTE: STUD FRAMING COMPLETE INDICATES COMPLETION OF STEEL STUD FRAMING SCOPE OF WORK AT A PARTICULAR AREA INCLUDING SHEATHING & PARAPET WHERE APPLICABLE.

NORWAY HOUSE HEALTH CENTRE OF EXCELLENCE WEEKLY UPDATE NOVEMBER 28TH 2021

EXTERIOR TRENCHING & FOUNDATION

Ongoing trenching & backfilling activities
-Base & sub-base layers are placed for Propane & Diesel pad.
-JNR forming & tying rebar for propane & diesel pads

Pouring Schedule for pads:
-Mech. Pad - Generator 1 - Poured October 30, 2021
-Mech. Pad - Generator 2 - Poured October 30, 2021
-Mech. Pad - Med Gas - Poured November 01, 2021
-Mech. Pad - Diesel - Poured November 12, 2021
-Mech. Pad - Propane / Splitter - TBD

POURED
LIGHT STANDARD FOUNDATION

POURED
LIGHT STANDARD FOUNDATION

POURED
Code Blue Foundation

POURED
LIGHT STANDARD FOUNDATION

POURED
LIGHT STANDARD FOUNDATION

POURED
LIGHT STANDARD FOUNDATION

Poured
Sweat Lodge Slab
-November 10

Expected Trenching

Work In-Progress

Trenching Complete

NORWAY HOUSE HEALTH CENTRE OF EXCELLENCE WEEKLY UPDATE NOVEMBER 28TH 2021

AREA	INTERIOR WALL % COMPLETION
A1	80 (+5)
A2	97
A3	87
B1	99
B2	85 (+5)
C1	0
C2	0

INTERIOR STEEL STUD FRAMING

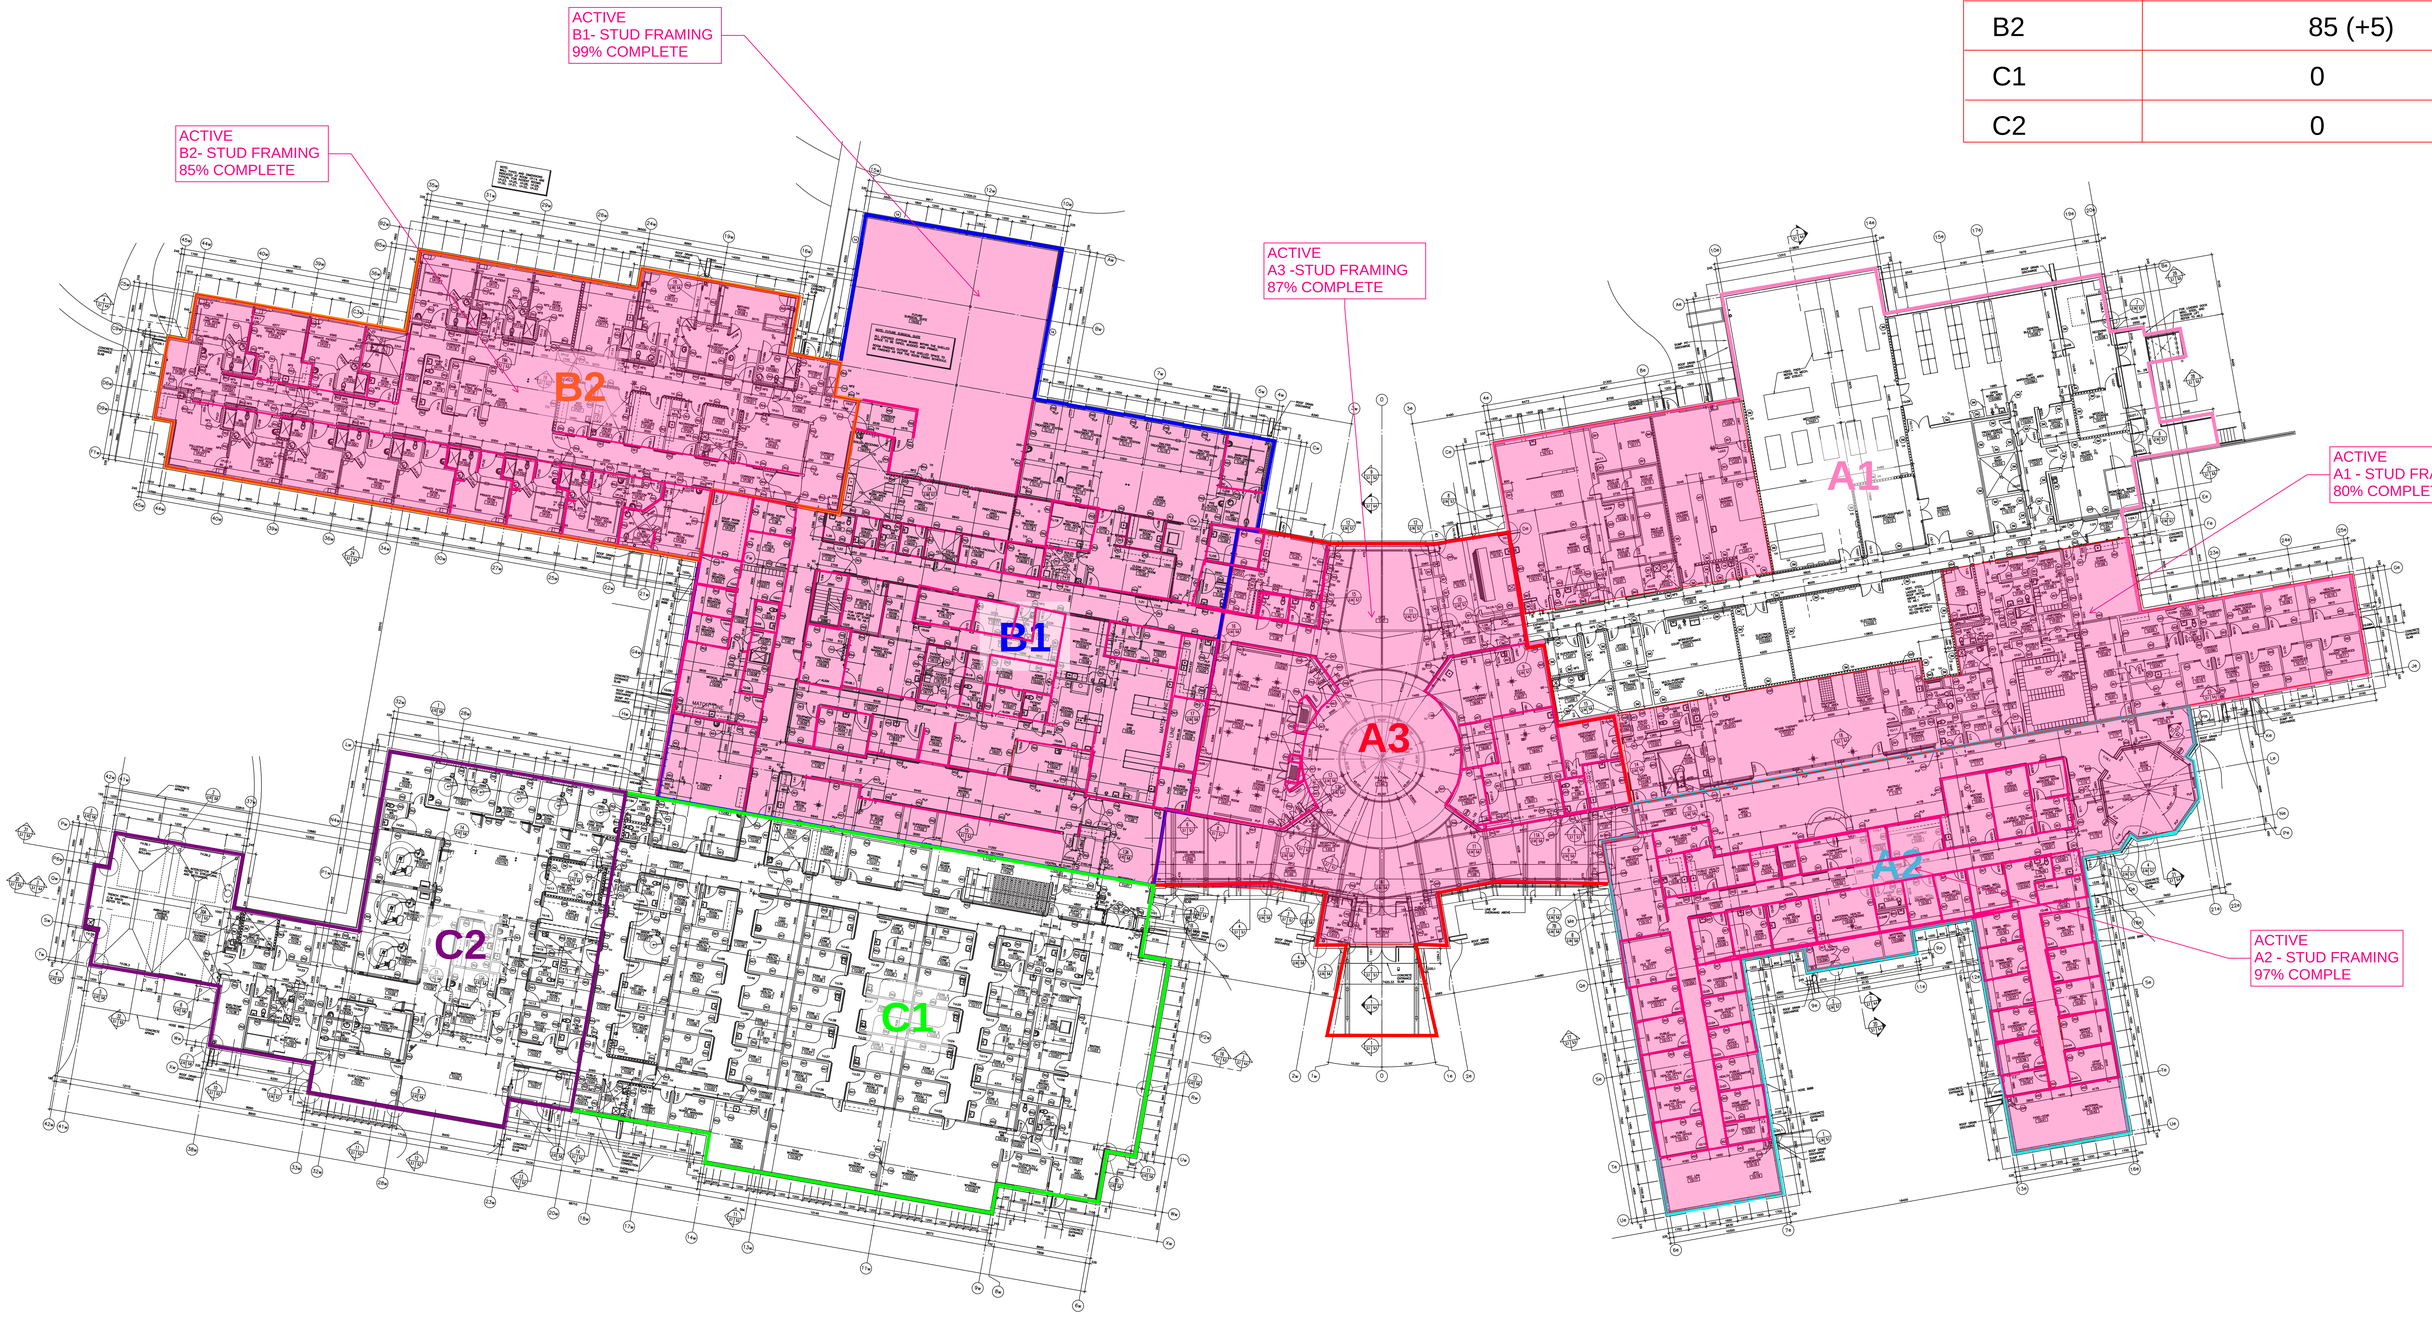

NORWAY HOUSE HEALTH CENTRE OF EXCELLENCE WEEKLY UPDATE NOVEMBER 28TH 2021

MASONRY ACTIVITY

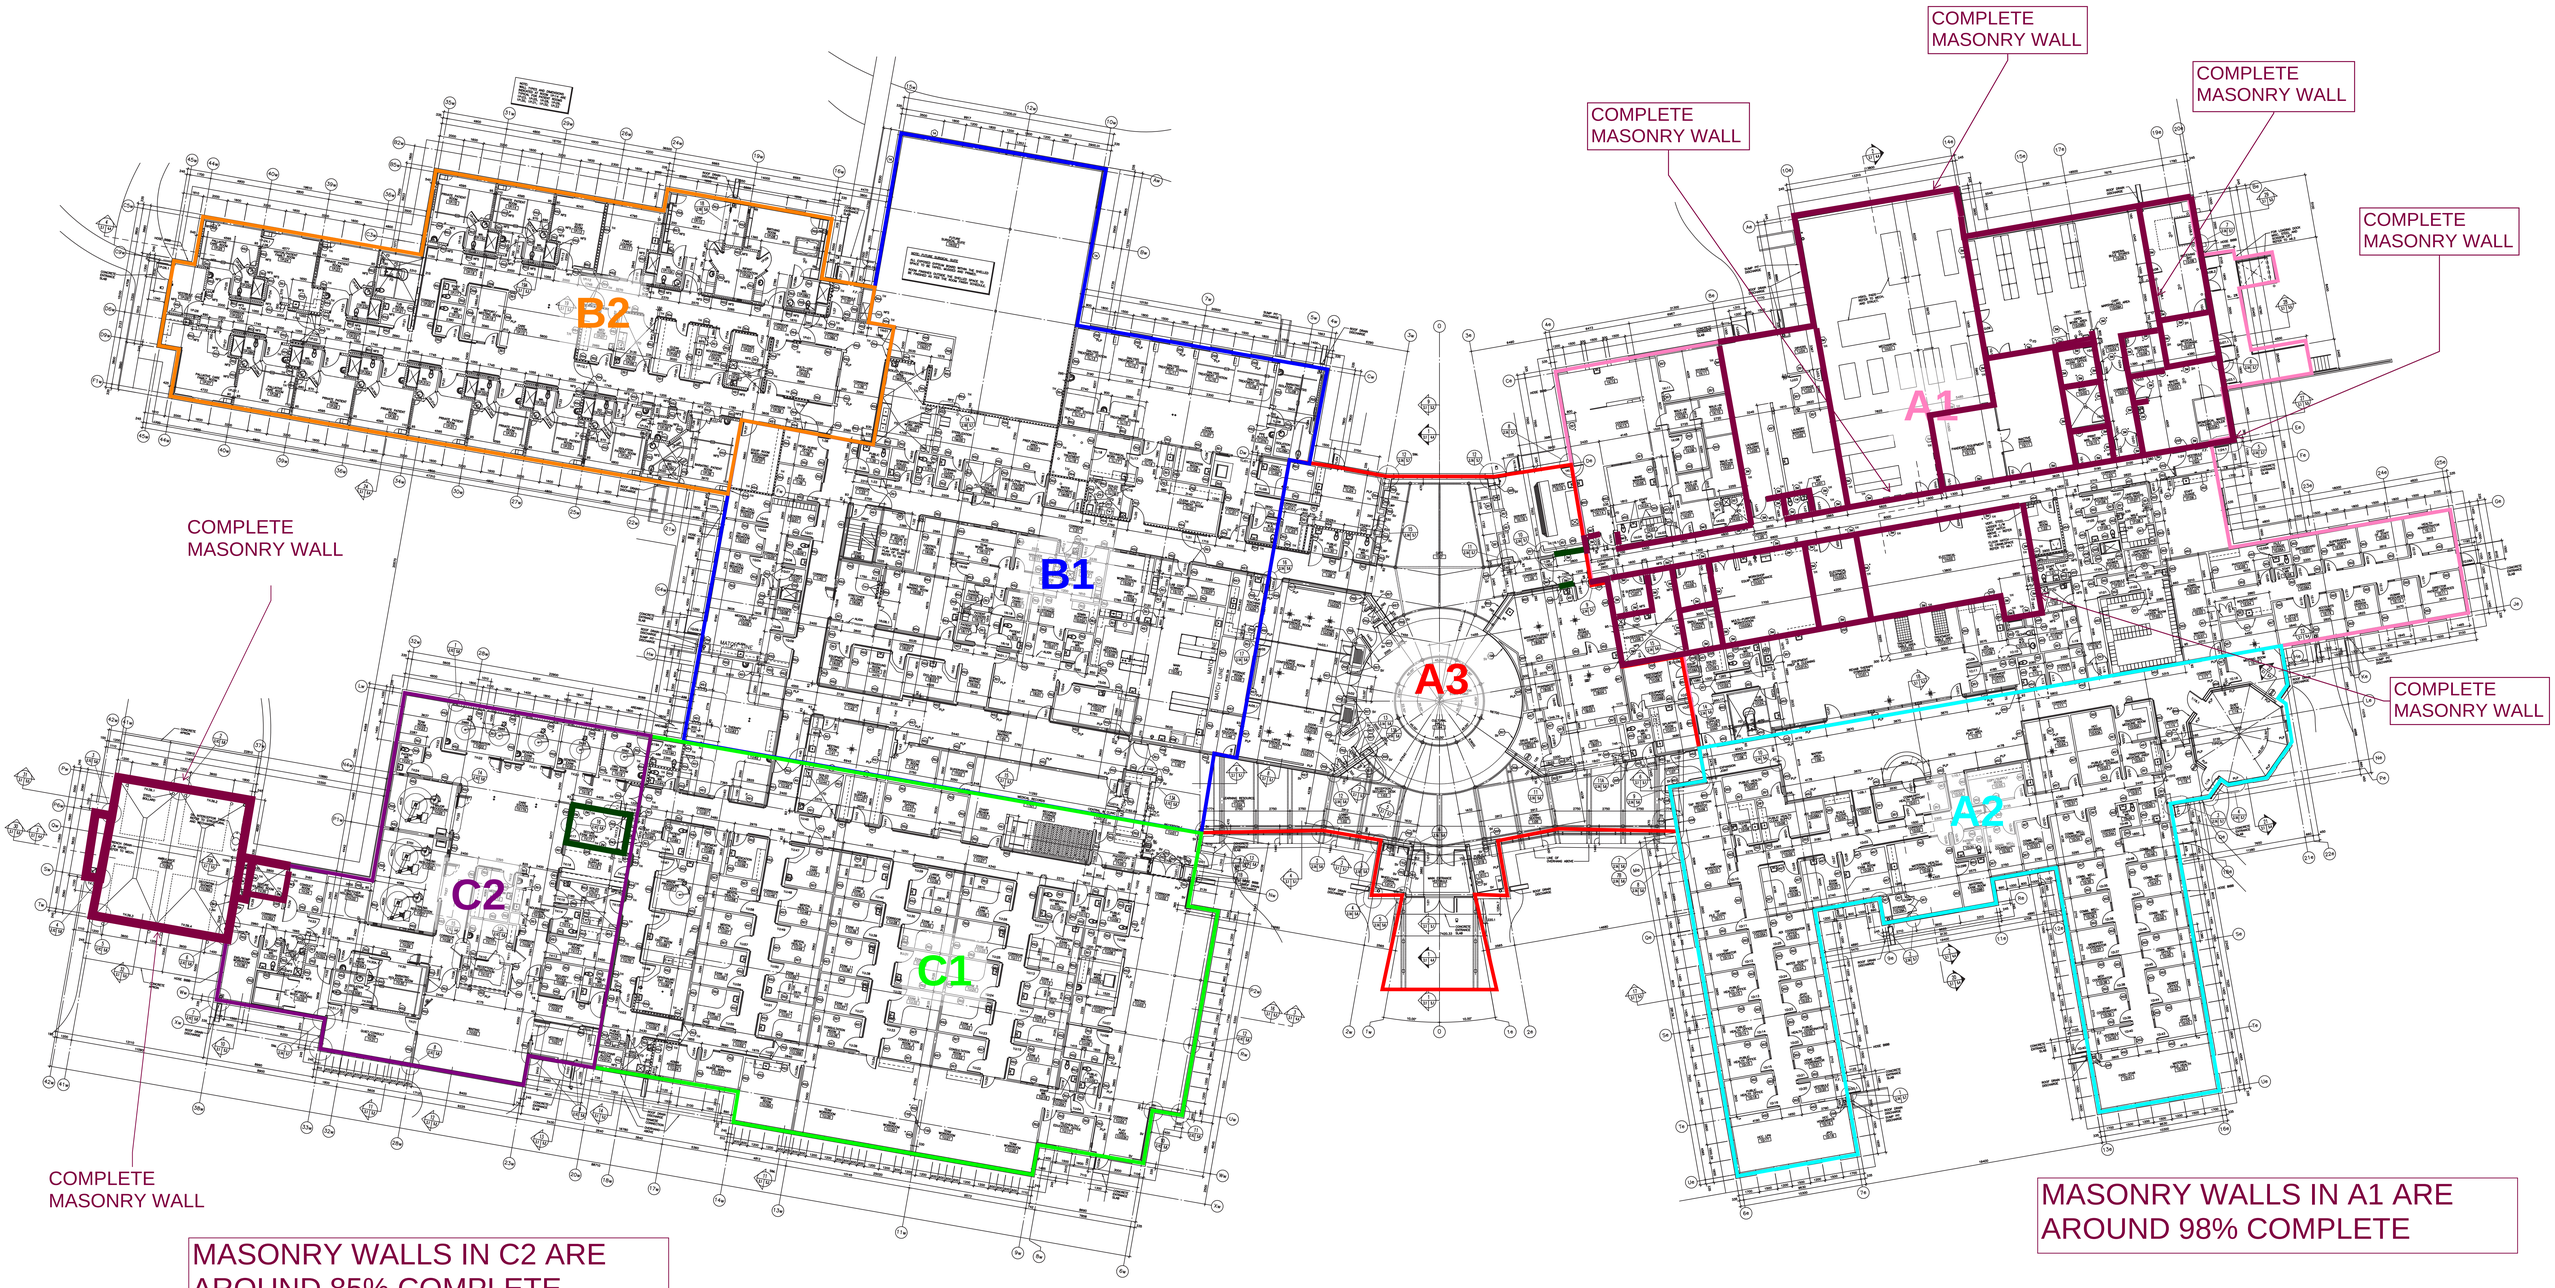

NORWAY HOUSE HEALTH CENTRE OF EXCELLENCE WEEKLY UPDATE NOVEMBER 28TH 2021

ROOFING ACTIVITY

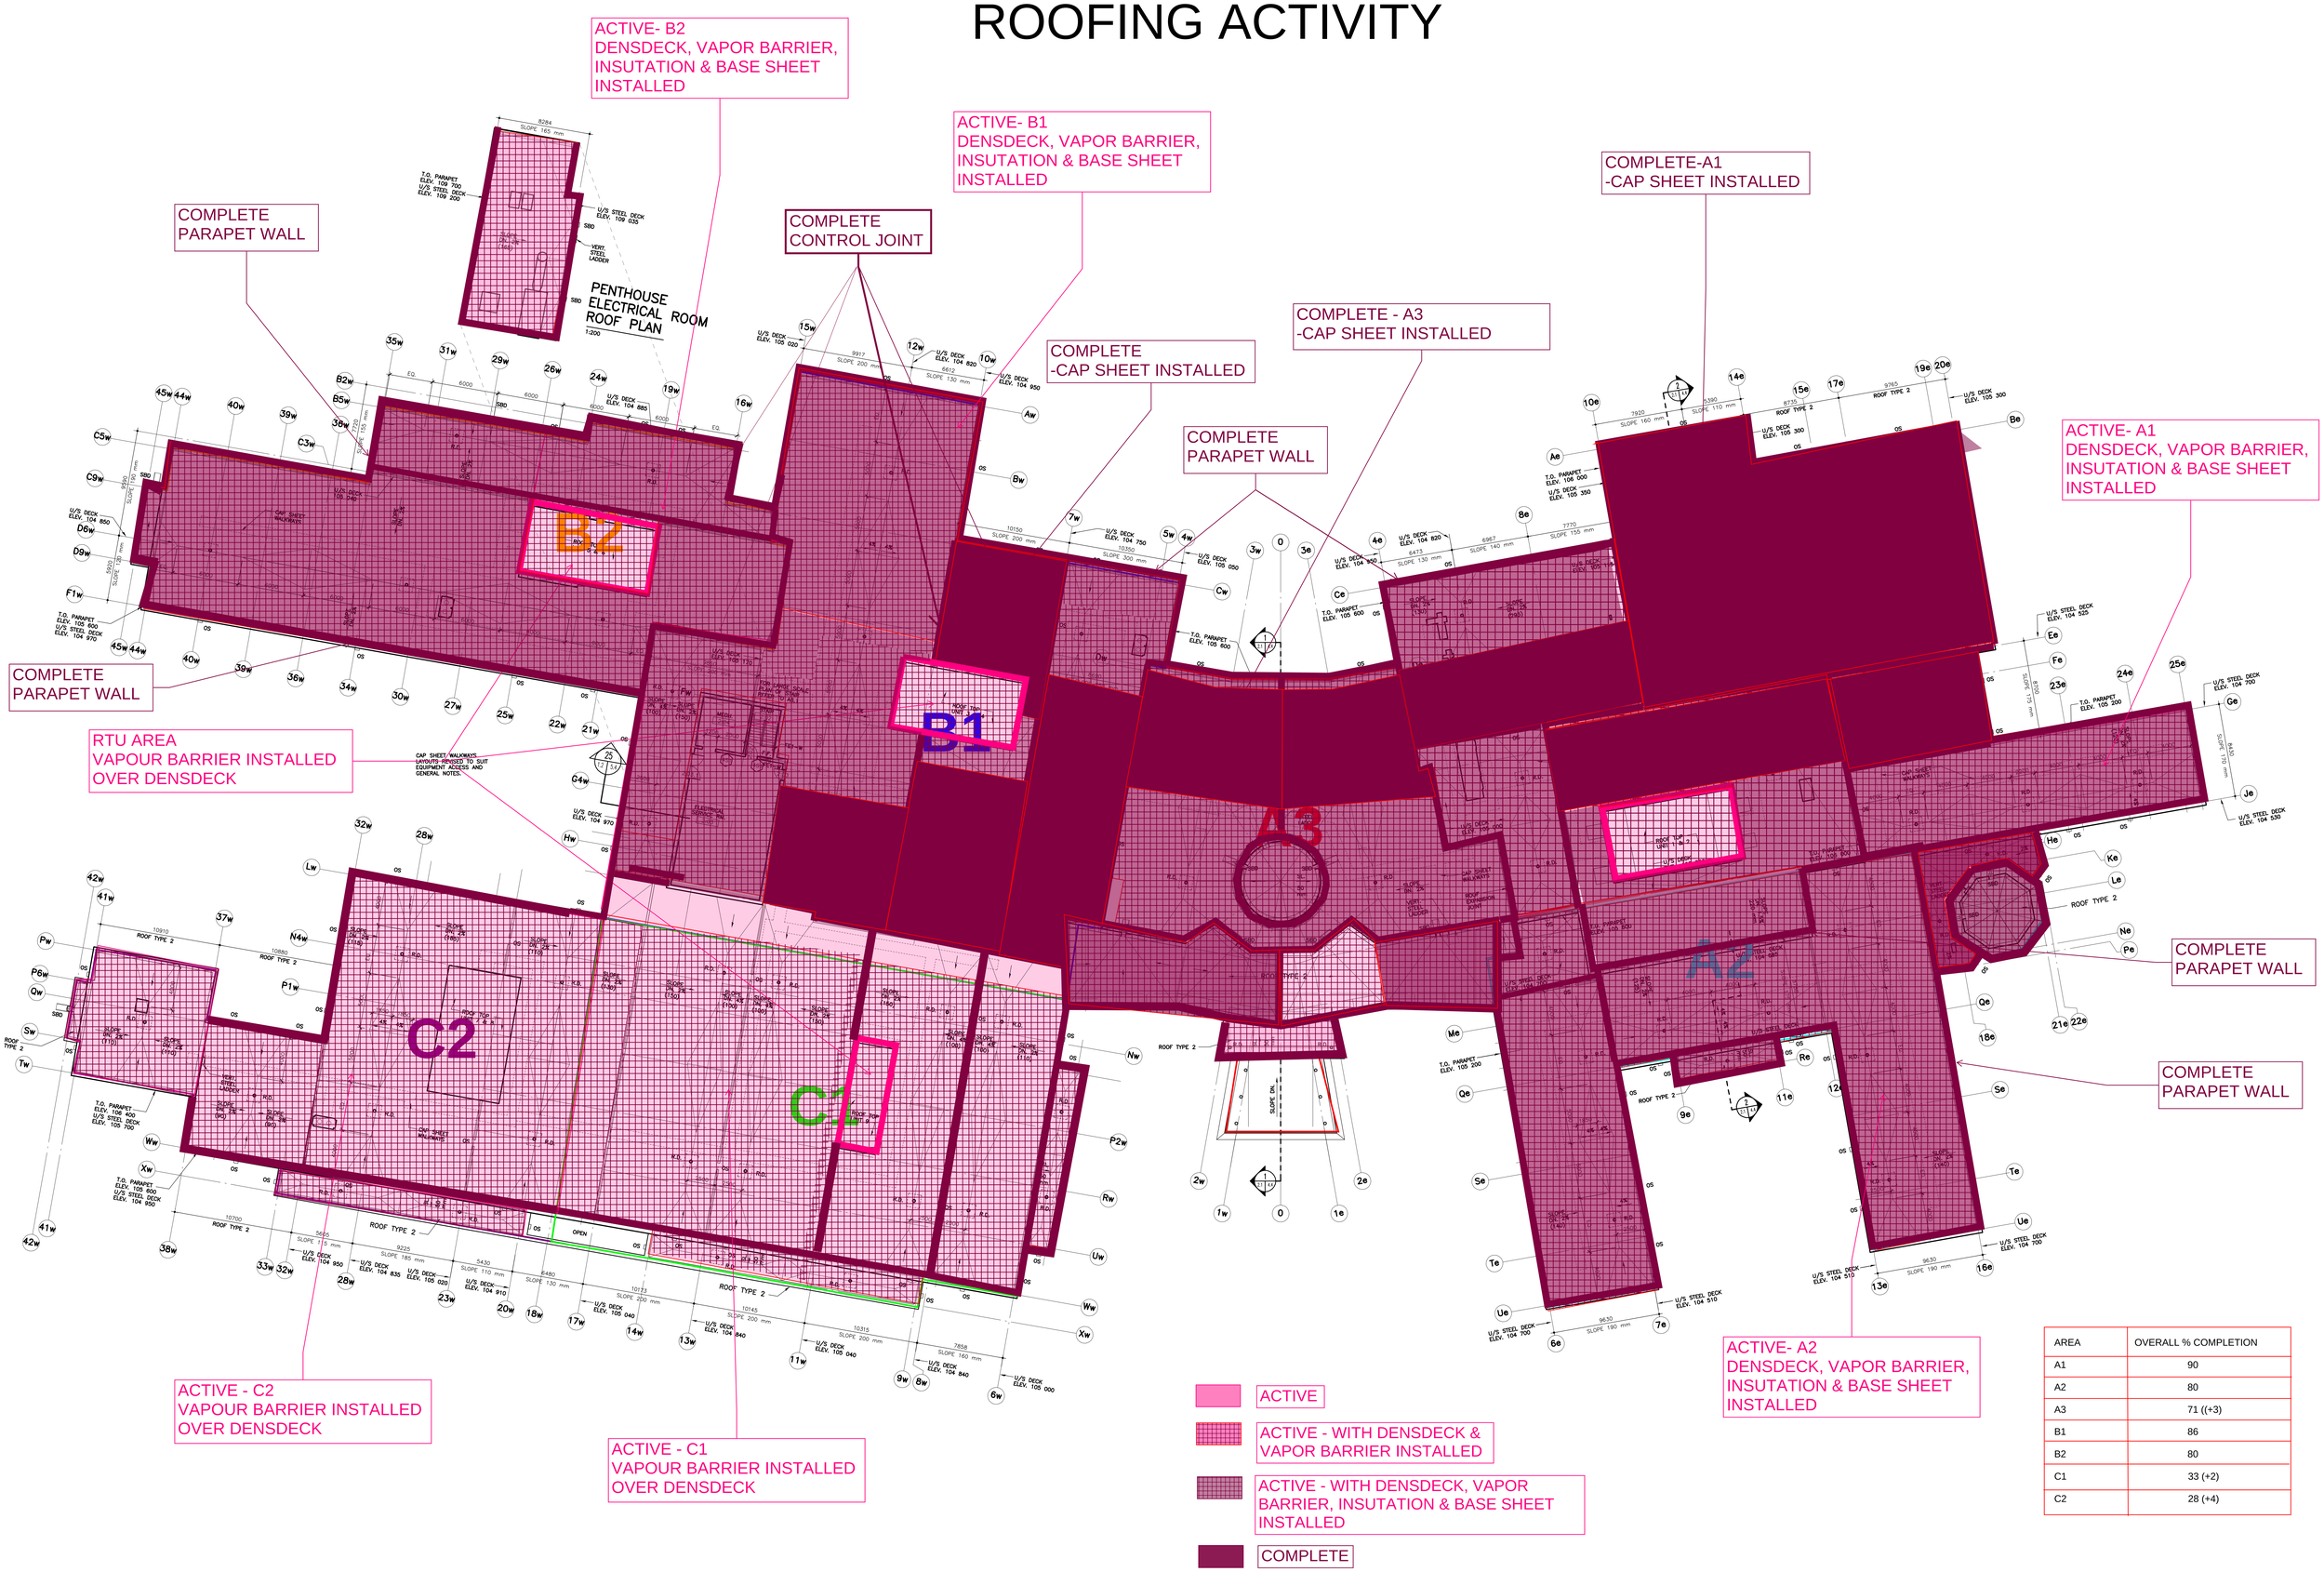

AREA	OVERALL % COMPLETION
A1	90
A2	80
A3	71 ((+3)
B1	86
B2	80
C1	33 (+2)
C2	28 (+4)

NORWAY HOUSE HEALTH CENTRE OF EXCELLENCE WEEKLY UPDATE NOVEMBER 28TH 2021

EXTERIOR WALL & GRADE BEAM LAYERS

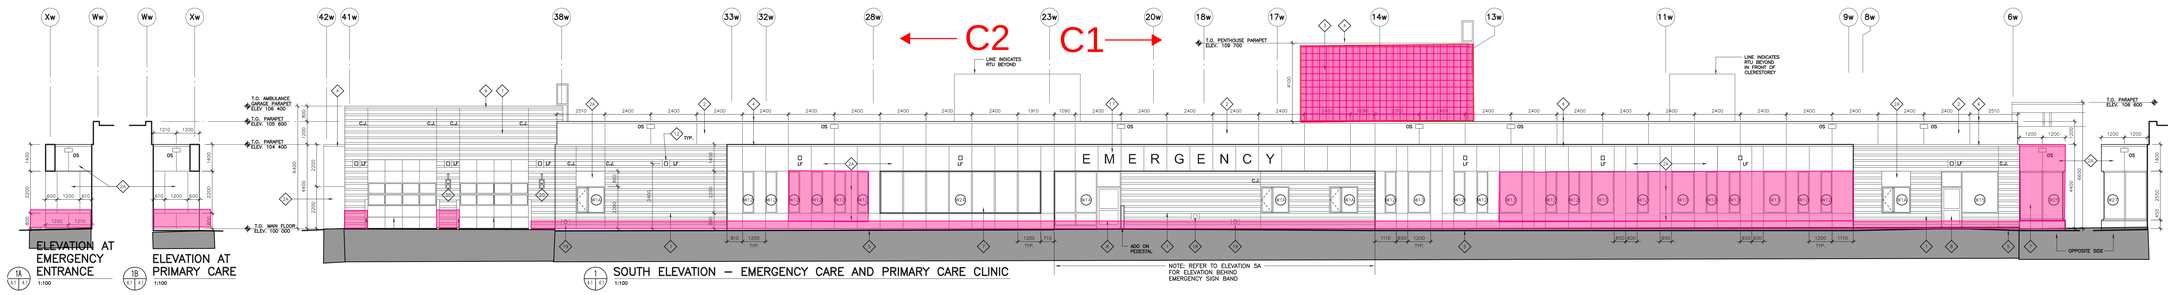

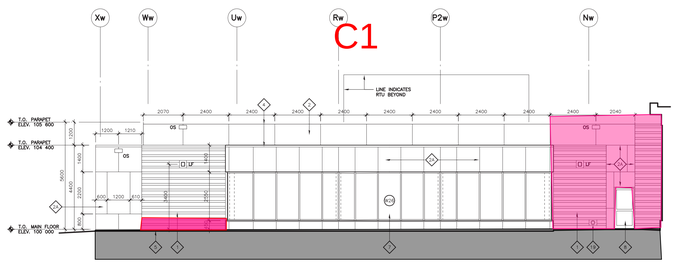

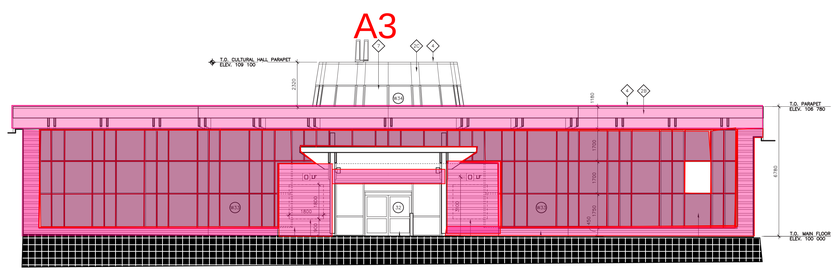



GRADE BEAM

COMPLETE DAMP PROOFING

ACTIVE GRADE BEAM INSULATION

COMPLETE INSTALLED GRADE BEAM INSULATION & DRAINAGE BOARD

EXTERIOR WALL

ACTIVE INSTALLING AVB

ACTIVE INSTALLING WALL INSULATION

COMPLETE VENEER/PANELS INSTALLED

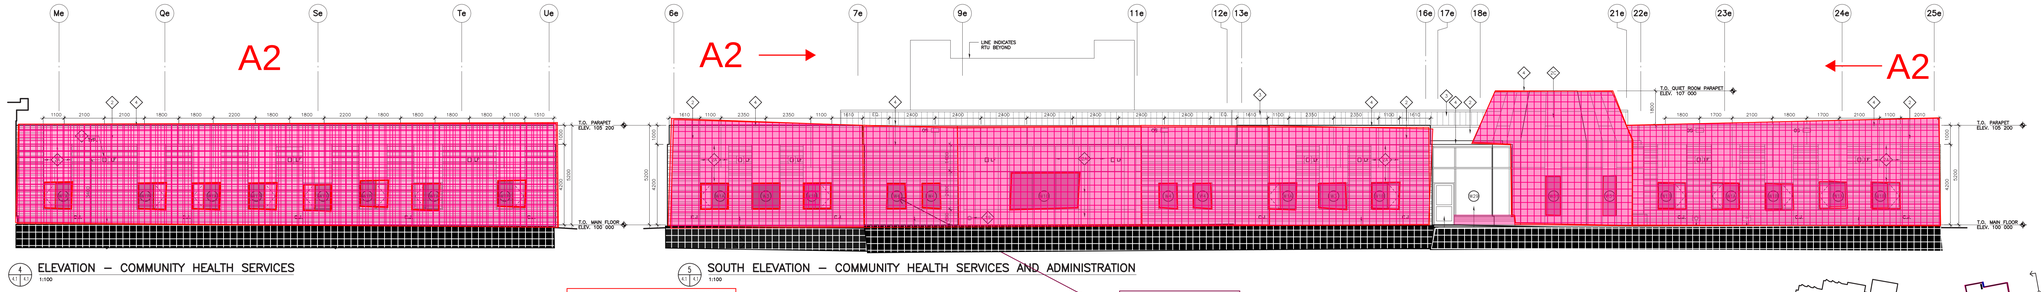

Window Frame Installed

Glazing Installed

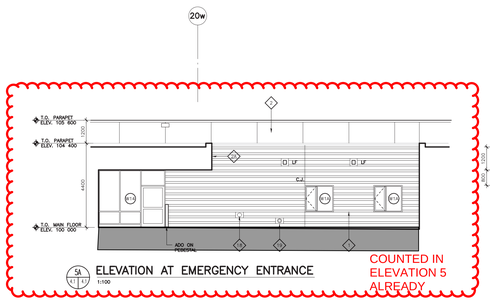

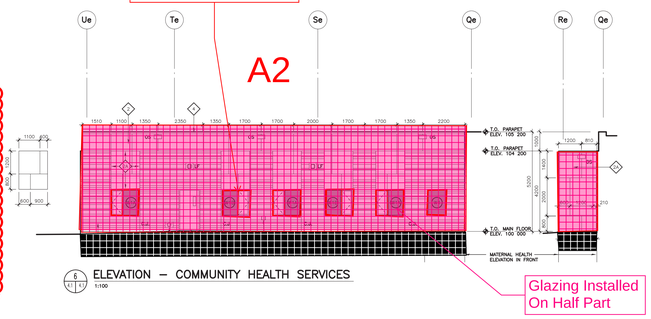

Glazing Installed On Half Part

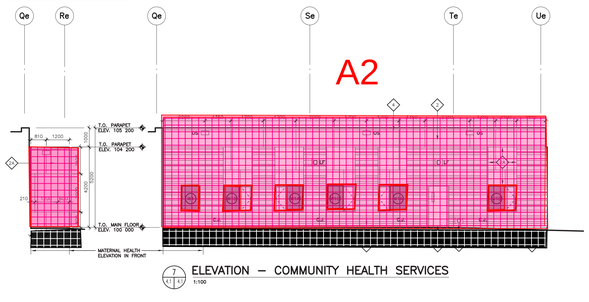



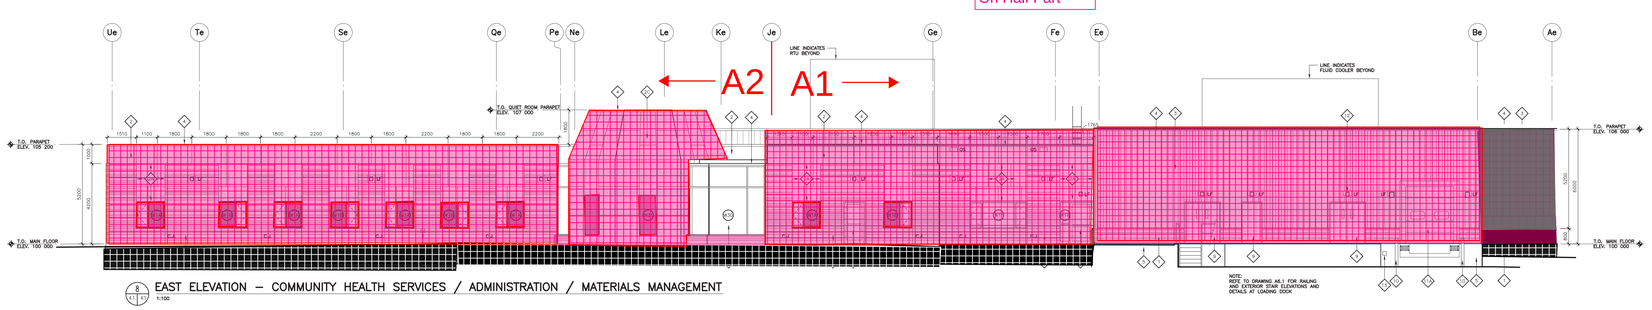

AREA	AVB % COMPLETION	INSULATION % COMPLETION
A1	100	96 (+6)
A2	98	90 (+8)
A3	98 (+8)	65
B1	100	100
B2	100	100
C1	25 (+23)	0
C2	56 (+6)	7

EXTERIOR WALL & GRADE BEAM LAYERS

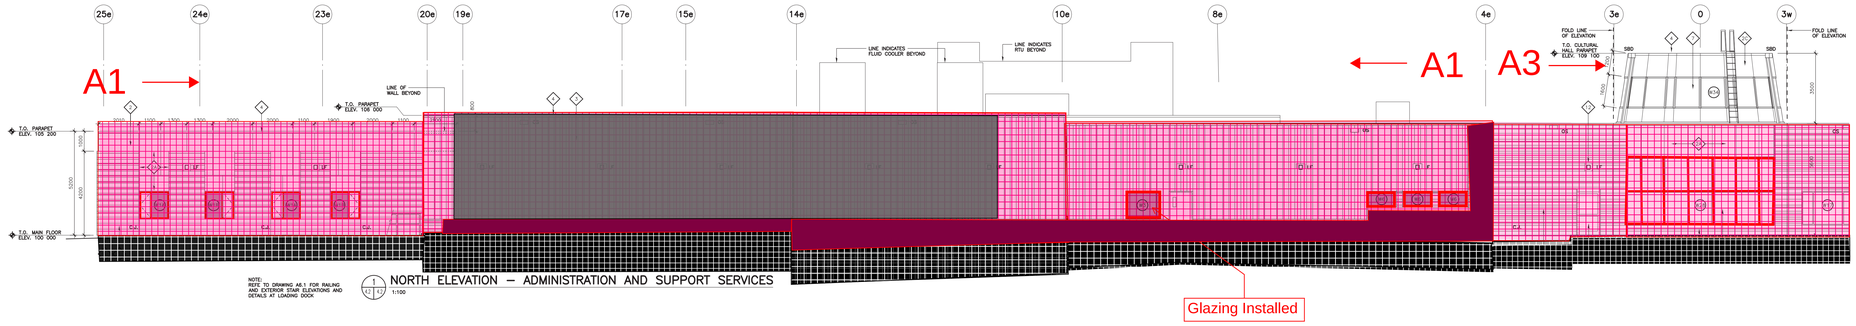

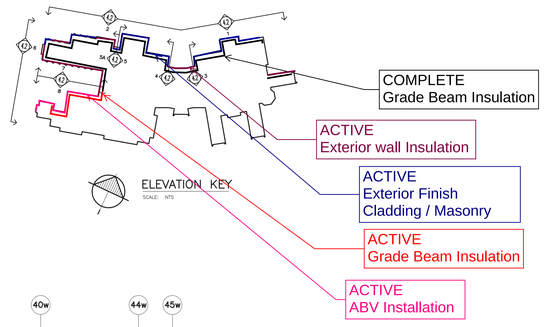

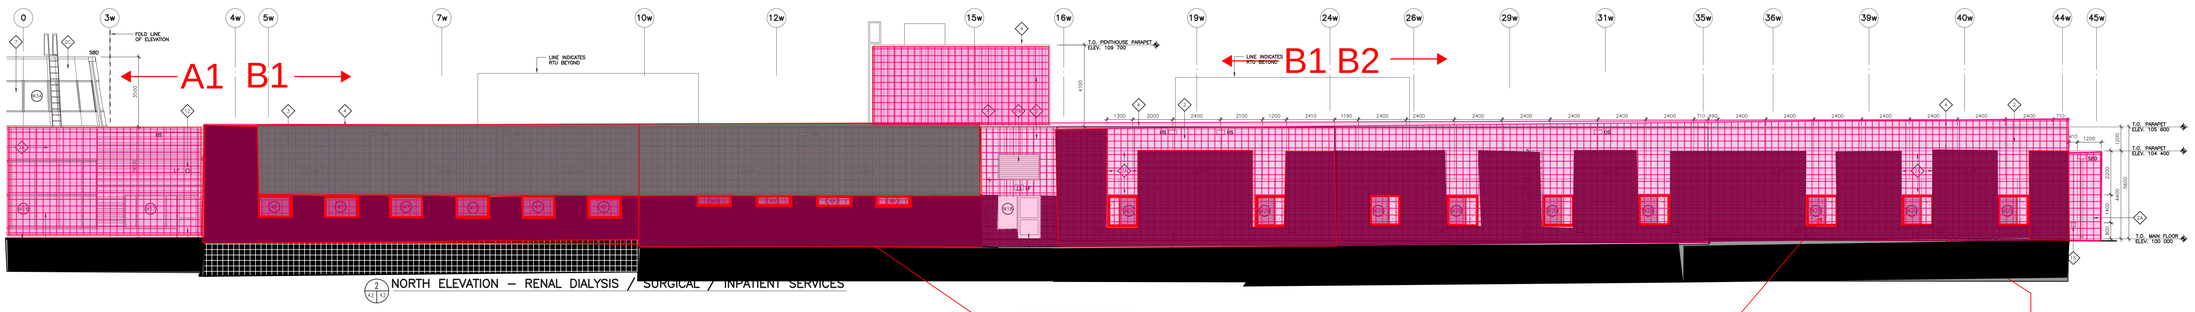

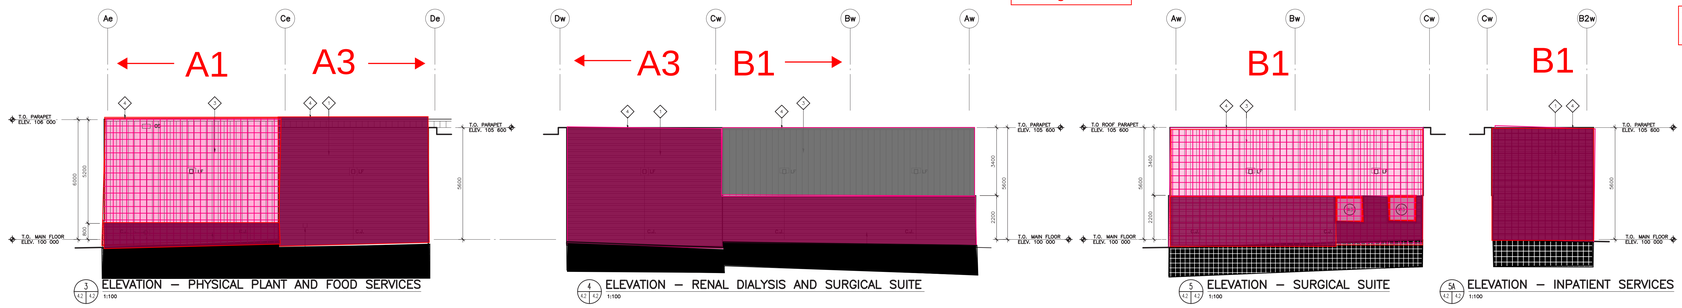

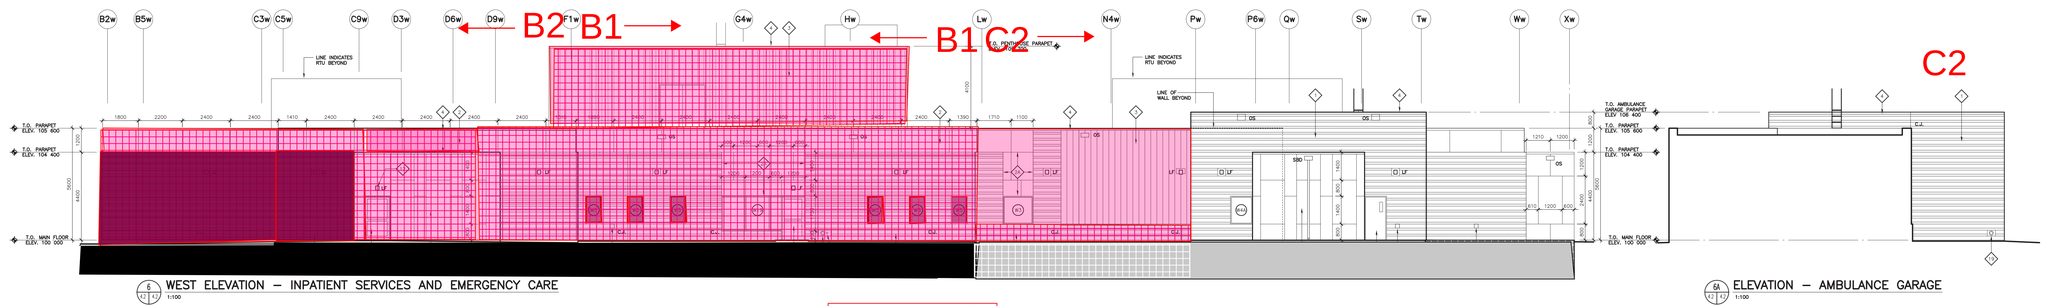

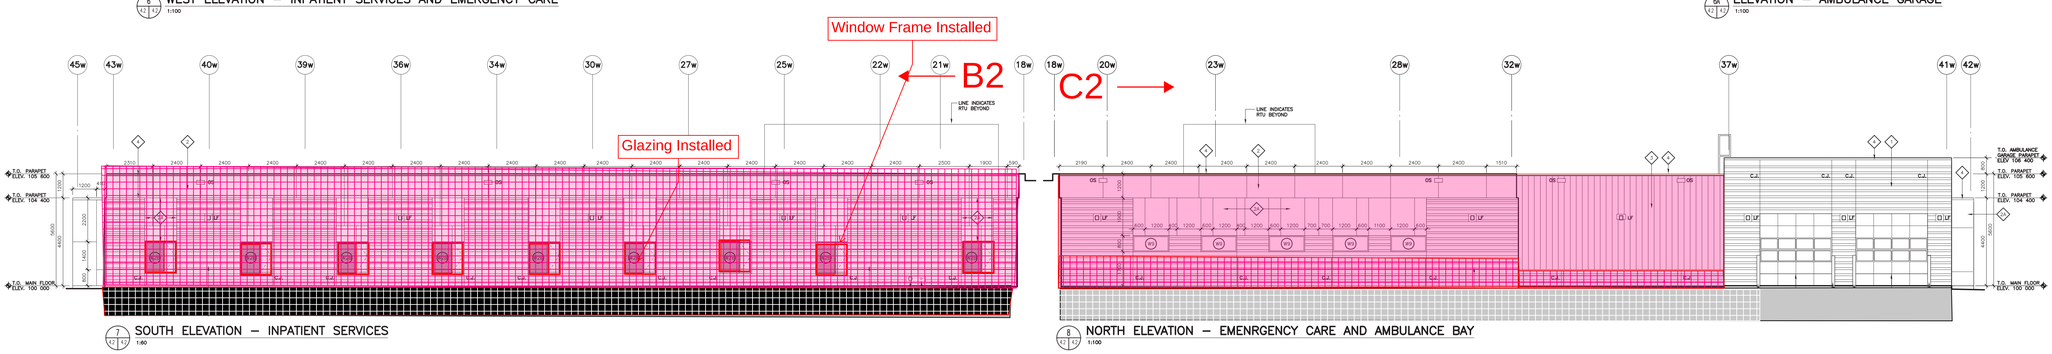

GRADE BEAM

- COMPLETE DAMP PROOFING
- ACTIVE GRADE BEAM INSULATION
- COMPLETE INSTALLED GRADE BEAM INSULATION & DRAINAGE BOARD

EXTERIOR WALL

- ACTIVE INSTALLING AVB
- ACTIVE INSTALLING WALL INSULATION
- COMPLETE VENEER
- COMPLETE PANELS
